



Verified Carbon Standard

WIND BASED POWER GENERATION BY MYTRAH ENERGY (INDIA) LIMITED (EKIESL- VCS-JANUARY-16-01)



INFINITE SOLUTIONS

Document Prepared by Infinite Solutions

Project Title	Wind Based Power Generation by Mytrah Energy (India) Limited (EKIESL-VCS-January-16-01)
Version	03
Report ID	VVER72
Date of Issue	20-July-2022
Project ID	1521
Monitoring Period	01-March-2022 to 31-March-2022 (Inclusive of both days)
Prepared By	Infinite Solutions
Contact	Infinite Solutions Registered Address: 214-215 Milinda Manor, Opp. Next Treasure Island, 2 RNT Marg, Indore- 452001

CONTENTS

1	PROJECT DETAILS	4
1.1	Summary Description of the Implementation Status of the Project	4
1.2	Sectoral Scope and Project Type	5
1.3	Project Proponent	5
1.4	Other Entities Involved in the Project	5
1.5	Project Start Date	6
1.6	Project Crediting Period	6
1.7	Project Location	6
1.8	Title and Reference of Methodology	12
1.9	Participation under other GHG Programs.....	12
1.10	Other Forms of Credit.	12
1.11	Sustainable Development Contributions	12
2	SAFEGUARDS	13
2.1	No Net Harm	13
2.2	Local Stakeholder Consultation	13
2.3	AFOLU-Specific Safeguards	14
3	IMPLEMENTATION STATUS	14
3.1	Implementation Status of the Project Activity.....	14
3.2	Deviations.....	14
3.3	Grouped Projects	15
4	DATA AND PARAMETERS	15
4.1	Data and Parameters Available at Validation	16
4.2	Data and Parameters Monitored.....	17
4.3	Monitoring Plan.....	18
5	QUANTIFICATION OF GHG EMISSION REDUCTIONS AND REMOVALS	24
5.1	Baseline Emissions	24
5.2	Project Emissions	25
5.3	Leakage.....	25
5.4	Net GHG Emission Reductions and Removals.....	25
	APPENDIX I: DATE OF COMMISSIONING	26

APPENDIX II: CALIBRATION DETAILS 33

1 PROJECT DETAILS

1.1 Summary Description of the Implementation Status of the Project

The purpose of the project activity is to generate electrical energy using renewable energy source (wind) for the purpose of captive utility. The project activity generates electricity using wind potential and converts it into kinetic energy using Wind turbines, which drives the alternators to generate energy. The generated electricity is exported to the regional grid system which is under the purview of the Southern grid of India (Now INDIAN Grid).

This project activity involves the installation of Wind Power Projects. The total installed capacity of the project is 233.1 MW; which involves operation of 156 Wind Turbine Generators (WTGs) with capacity of 0.85 MW each located at Karnataka (112 WTGs) and Andhra Pradesh (44 WTGs) implemented by Mytrah Vayu Krishna Private Limited and 67 Wind Turbine Generator (WTGs) of 1.5 MW implemented by Mytrah Vayu (Manjira) Private Limited Tamil Nadu state in India. These are the subsidiary companies of Mytrah Energy (India) Limited. However, the project is promoted by Mytrah Energy (India) Limited, which is also the project proponent in the project activity. The commissioning dates of the project activity is mentioned in APPENDIX 1: Date of Commissioning. The first WTG was commissioned on 21 February 2014 and last WTG was commissioned on 26 February 2015

The power produced displaces an equivalent amount of power from the grid, which is fed mainly by fossil fuel fired power plants. Hence, as per VCS PD, it results in total electricity generation of 488,388.4 MWh/year and of GHG emission reductions of 479,448 tonnes of CO₂/year.

The Project activity is a new facility (Greenfield) and the purpose of the project activity is to generate electricity by the utilization of wind velocity, and selling the generated electrical energy from 132.6 MW project implemented by Mytrah Vayu Krishna Private Limited to respective state utilizes under the Southern Grid. Further energy generation from 100.5 MW wind mill project implemented by Mytrah Vayu (Manjira) Private Limited is for captive utilization, under Tamil Nadu state. In this process there is no consumption of any fossil fuel and hence the project does not lead to any greenhouse gas emissions. Thus, electricity would be generated through sustainable means without causing any negative impact on the environment.

In the Pre- project scenario, the equivalent amount of electricity delivered to the grid by the project activity, would have otherwise been generated by the operation of grid-connected fossil fuel-based power plants and by the addition of new generation sources. The Pre-project scenario for the facility where the electricity is wheeled (in case of TN WTGs), the electricity was sourced from southern grid.

The total emission reductions achieved during current monitoring period is 12,889 t CO₂e.,

1.2 Sectoral Scope and Project Type

The project activity falls under the following Sectoral scope and Project Type:

Sectoral Scope: 01 - Energy industries (renewable / nonrenewable sources)

Project Type: I - Renewable Energy Projects

Methodology: ACM0002: Grid-connected electricity generation from renewable sources - Version 16.0

The project is not a grouped project activity

1.3 Project Proponent

Organization name	Mytrah Energy (India) Limited
Contact person	Mr. Ramesh Kure
Title	Assisstant Manager
Address	1st Floor, Prestige Meridian-II, No. 30 M.G Road, Bangalore - 560 001.
Telephone	+91 72888 75975
Email	cleancredits@mytrah.com

1.4 Other Entities Involved in the Project

Organization name	Infinite Solutions
Role in the Project	Carbon Consultant
Contact person	Richa Sah
Title	Project Manger
Address	214-215 Milinda Manor, Opp. Next Treasure Island, 2 RNT Marg, Indore-452001
Telephone	+91-731-4050174
Email	richa@infisolutions.org

1.5 Project Start Date

Project Start Date: 21-February-2014

The project start date is the date on which first WTG was commissioned under the Project activity.

1.6 Project Crediting Period

Crediting Period Start date: 21-February -2014¹

Crediting Period End date: 20-February-2024

The project activity adopts renewable crediting period of 10 years' period which can be renewed for maximum 2 times.

1.7 Project Location

For Tamil Nadu

S.No.	Machine ID	Feeder Nos.	HTSC No.	Latitude	Longitude
1	KOO - 518	Feeder 9	DRA 001	10.695026 N	77.570779 E
2	KOO - 1359		DRA 003	10.688039 N	77.592838 E
3	APY - 241	Feeder 5	DRA 004	10.696430 N	77.655525 E
4	APY - 416		DRA 005	10.693031 N	77.653586 E
5	PAR - 9		DRA 006	10.678811 N	77.553641 E
6	PON - 534		DRA 008	10.676050 N	77.571935 E
7	PON - 1043		DRA 009	10.729955 N	77.576547 E
8	NAL-119		Feeder 2	DRA 012	10.652837 N
9	NAL - 81	Feeder 5	DRA 013	10.664993 N	77.528386 E
10	NAL - 57		DRA 015	10.763263 N	77.625708 E
11	MAN - 210	Feeder 9	DRA 017	10.727352 N	77.585324 E
12	MAN - 898		DRA 018	10.713748 N	77.629144 E
13	MAN - 802		DRA 021	10.657353 N	77.553426 E
14	KON - 556	Feeder 4	DRA 022	10.650216 N	77.649013 E
15	KON - 563		DRA 023	10.699483 N	77.688256 E
16	KON - 590		DRA 024	10.684740 N	77.608212 E
17	KON - 640		DRA 025	10.738135 N	77.688168 E
18	KON - 658		DRA 026	10.670208 N	77.629071 E
19	KON - 621		DRA 027	10.667608 N	77.611546 E
20	KON - 501		Feeder 3	DRA 031	10.694380 N
21	ALA - 1639	Feeder 8	DRA 043	10.665640 N	77.659623 E
22	ALA - 1946		DRA 044	10.663297 N	77.566886 E
23	NAL - 434	Feeder 6	DRA 049	10.648711 N	77.550586 E
24	KON - 234		DRA 054	10.658922 N	77.561651 E
25	PAR - 50	Feeder 5	DRA 007	10.737605 N	77.627596 E
26	MAN - 625	Feeder 3	DRA 032	10.662515 N	77.557552 E
27	MAN - 604	Feeder 2	DRA 033	10.644345 N	77.515043 E
28	ALA-2301/2304	Feeder 8	DRA 046	10.720840 N	77.587169 E

29	ALA - 1569		DRA 047	10.759444 N	77.604996 E
30	ALA-2352		DRA 048	10.763189 N	77.616268 E
31	KOO - 1157	Feeder 2	DRA 002	10.669956 N	77.554773 E
32	PON - 1081		DRA 010	10.660363 N	77.617842 E
33	MAN - 940	Feeder 9	DRA 019	10.668934 N	77.569253 E
34	PON - 1565	Feeder 9	DRA 037	10.673908 N	77.529976 E
35	PON - 1568	Feeder 6	DRA 038	10.646536 N	77.555893 E
36	VEL - 1936	Feeder 8	DRA 039	10.677837 N	77.535691 E
37	ALA - 1618	Feeder 9	DRA 042	10.66492 N	77.547432 E
38	PON - 908	Feeder 8	DRA 050	10.718534 N	77.615573 E
39	PON - 1203	Feeder 6	DRA 052	10.71890 N	77.581396 E
40	MAN - 963	Feeder 7	DRA 055	10.683484 N	77.617876 E
41	PON - 1021	Feeder 2	DRA 011	10.773698 N	77.61412 E
42	KUL - 652	Feeder 5	DRA 014	10.68742 N	77.616146 E
43	PON - 4		DRA 016	10.692721 N	77.615369 E
44	MAN-828	Feeder 9	DRA 020	10.692721 N	77.615369 E
45	KON - 618	Feeder 3	DRA 028	10.710023 N	77.646516 E
46	KON-395		DRA 029	10.77361 N	77.639413 E
47	KON-451	Feeder 2	DRA 030	10.754682 N	77.62652 E
48	APA-84	Feeder 3	DRA 034	10.689743 N	77.610703 E
49	PUN-270		DRA 035	10.66565 N	77.517593 E
50	PUN - 34		DRA 036	10.673745 N	77.54778 E
51	VEL-1702	Feeder 9	DRA 040	10.681788 N	77.689854 E
52	KAL-93	Feeder 8	DRA 041	10.649539 N	77.51747 E
53	ALA-2290		DRA 045	10.654515 N	77.559157 E
54	PON - 775	Feeder 6	DRA 051	10.65057 N	77.580673 E
55	ALA - 2260		DRA 053	10.620784 N	77.564648 E
56	MET 1664	Feeder 7	DRA 065	10.630660 N	77.569115 E
57	NAL - 445		DRA 061	10.684400 N	77.563052 E
58	KOO-1036	Feeder 6	DRA 056	10.667224 N	77.539641 E
59	VEL-1540		DRA 060	10.683467 N	77.536761 E
60	KOO-1174	Feeder 7	DRA 058	10.677765 N	77.616831 E
61	KOO-1000		DRA 057	10.714956 N	77.67510 E
62	PON-1304		DRA 059	10.659904 N	77.651955 E
63	APY-247		DRA 064	10.656300 N	77.62939 E
64	KON-411		DRA 67	10.765864 N	77.633324 E
65	KOO - 581		DRA 062	10.709670 N	77.627337 E
66	VEL - 2119		DRA 063	10.753168 N	77.683129 E
67	ALA 1385		DRA 066	10.762752 N	77.680226 E

For Andhra Pradesh

S. No.	Feeder Nos.	Location No.	Latitude	Longitude
1	Feeder 1	508	15.154461 N	77.922135 E
2		510	15.157268 N	77.921522 E

3		511	15.158979 N	77.923322 E
4		513	15.161872 N	77.923761 E
5		514	15.163549 N	77.923292 E
6		515	15.165388 N	77.922815 E
7		516	15.166574 N	77.921892 E
8		517	15.167997 N	77.920787 E
9		518	15.16929 N	77.919977 E
10		519	15.170968 N	77.918066 E
11		520	15.172449 N	77.918783 E
12	Feeder 2	528	15.185218 N	77.923655 E
13		529	15.186921 N	77.923976 E
14		530	15.189489 N	77.925118 E
15		531	15.190881 N	77.925026 E
16	Feeder 3	532	15.206692 N	77.937622 E
17		533	15.208101 N	77.938972 E
18		534	15.209818 N	77.940958 E
19		535	15.211871 N	77.942781 E
20		536	15.215178 N	77.947515 E
21		537	15.216917 N	77.949166 E
22		538	15.218416 N	77.950564 E
23		539	15.221591 N	77.953603 E
24		540	15.225099 N	77.957372 E
25		541	15.226569 N	77.958248 E
26		542	15.228387 N	77.959399 E
27		543	15.229998 N	77.960501 E
28		545	15.223820 N	77.956471 E
29	Feeder 3	546	15.213598 N	77.946804 E
30		547	15.204944 N	77.93730 E
31	Feeder 2	551	15.188055 N	77.924987 E
32	Feeder 1	509	15.155886 N	77.920862 E
33		512	15.160386 N	77.923416 E
34	Feeder 2	521	15.174326 N	77.91959 E
35		522	15.175897 N	77.92030 E
36		523	15.177475 N	77.921177 E
37		524	15.179081 N	77.921943 E
38		525	15.180875 N	77.922916 E
39		526	15.182457 N	77.923515 E
40		527	15.183845 N	77.923022 E
41	Feeder 3	544	15.231485 N	77.961368 E
42		548	15.202938 N	77.936743 E
43		549	15.201556 N	77.936035 E

44	Feeder 2	550	15.192441 N	77.927995 E
----	----------	-----	-------------	-------------

For Karnataka

S.No.	Feeder Nos.	Machine ID	Latitude (N)	Longitude (E)
1.	Feeder 01	MVKPL_01-03	17° 09' 49.3"	75° 43' 2.6"
2.		MVKPL_01-04	17° 09' 37.1"	75° 43' 1.5"
3.		MVKPL_01-05	17° 09' 31.4"	75° 43' 1.1"
4.		MVKPL_01-06	17° 9' 29.4"	75° 43' 18.8"
5.		MVKPL_01-07	17° 9' 24.3"	75° 43' 21.4"
6.		MVKPL_01-08	17° 9' 16.6"	75° 43' 26.9"
7.		MVKPL_01-09	17° 09' 11.2"	75° 43' 28.3"
8.		MVKPL_01-10	17° 9' 3.6"	75° 44' 26.9"
9.		MVKPL_01-11	17° 8' 59.1"	75° 44' 31"
10.		MVKPL_01-12	17° 8' 51.9"	75° 44' 34.5"
11.		MVKPL_01-13	17° 8' 38.9"	75° 44' 20.9"
12.		MVKPL_01-14	17° 8' 34.3"	75° 44' 26.1"
13.		MVKPL_01-15	17° 8' 26.2"	75° 44' 26.7"
14.	Feeder 2	MVKPL_02-01	17° 09' 02.4"	75° 42' 49.2"
15.		MVKPL_02-02	17° 08' 57.4"	75° 42' 44.3"
16.		MVKPL_02-03	17° 08' 51.0"	75° 42' 39.8"
17.		MVKPL_02-04	17° 08' 52.5"	75° 42' 31.9"
18.		MVKPL_02-05	17° 08' 45.7"	75° 42' 41.7"
19.		MVKPL_02-06	17° 08' 36.2"	75° 42' 37.6"
20.		MVKPL_02-07	17° 08' 31.4"	75° 42' 31.1"
21.		MVKPL_02-08	17° 08' 22.3"	75° 42' 23.2"
22.		MVKPL_02-09	17° 08' 20.5"	75° 42' 46.8"
23.		MVKPL_02-10	17° 08' 40.9"	75° 42' 53.7"
24.		MVKPL_02-11	17° 08' 35.6"	75° 42' 59"
25.		MVKPL_02-12	17° 08' 29.4"	75° 42' 59.9"
26.		MVKPL_02-13	17° 08' 22.0"	75° 43' 00.1"
27.		MVKPL_02-14	17° 08' 12.4"	75° 43' 03.0"
28.		MVKPL_02-15	17° 08' 06.8"	75° 43' 04.7"
29.		MVKPL_02-16	17° 08' 17.9"	75° 44' 29.8"
30.		MVKPL_02-17	17° 07' 59.4"	75° 43' 53.5"
31.		MVKPL_02-18	17° 07' 53.6"	75° 43' 50.9"
32.		MVKPL_02-19	17° 07' 49.5"	75° 43' 36.0"
33.		MVKPL_02-20	17° 07' 24.0"	75° 44' 02.4"

34.	Feeder 3	MVKPL_03-01	17° 07' 03.4"	75° 41' 51.5"
35.		MVKPL_03-02	17° 07' 10.6"	75° 42' 08.1"
36.		MVKPL_03-03	17° 07' 52.0"	75° 42' 09.8"
37.		MVKPL_03-04	17° 07' 03.2"	75° 42' 21.6"
38.		MVKPL_03-05	17° 07' 29.2"	75° 42' 37.1"
39.		MVKPL_03-06	17° 07' 44.7"	75° 43' 03.3"
40.		MVKPL_03-07	17° 07' 48.5"	75° 42' 58.7"
41.		MVKPL_03-08	17° 07' 18.6"	75° 43' 03.0"
42.		MVKPL_03-09	17° 07' 11.3"	75° 43' 01.4"
43.		MVKPL_03-10	17° 07' 04.4"	75° 42' 57.3"
44.		MVKPL_03-11	17° 06' 58.5"	75° 42' 58.1"
45.		MVKPL_03-12	17° 07' 34.2"	75° 43' 37.7"
46.		MVKPL_03-13	17° 07' 18.1"	75° 43' 24.2"
47.		MVKPL_03-14	17° 07' 12.3"	75° 43' 25.2"
48.		MVKPL_03-15	17° 07' 06.2"	75° 43' 36.3"
49.		MVKPL_03-16	17° 06' 51.9"	75° 42' 0.1"
50.		MVKPL_03-17	17° 6' 46.2"	75° 43' 59.9"
51.		MVKPL_03-18	17° 06' 37.9"	75° 43' 55.5"
52.		MVKPL_03-19	17° 06' 31.1"	75° 43' 49.7"
53.	Feeder 4	MVKPL_04-01	17° 06' 35.1"	75° 42' 52.8"
54.		MVKPL_04-02	17° 06' 01.9"	75° 42' 29.4"
55.		MVKPL_04-03	17° 05' 54.7"	75° 42' 21.6"
56.		MVKPL_04-04	17° 05' 51.3"	75° 42' 46.6"
57.		MVKPL_04-05	17° 05' 46.4"	75° 42' 41.3"
58.		MVKPL_04-06	17° 05' 39.9"	75° 42' 41.6"
59.		MVKPL_04-07	17° 06' 35.9"	75° 43' 23.6"
60.		MVKPL_04-08	17° 06' 28.8"	75° 43' 24.4"
61.		MVKPL_04-09	17° 06' 23.9"	75° 43' 47.1"
62.		MVKPL_04-10	17° 06' 15.6"	75° 43' 39.4"
63.		MVKPL_04-11	17° 05' 59.5"	75° 43' 31.8"
64.		MVKPL_04-12	17° 05' 27.3"	75° 43' 30.0"
65.		MVKPL_04-13	17° 06' 04.5"	75° 43' 55.5"
66.		MVKPL_04-14	17° 05' 59.0"	75° 43' 54.1"
67.		MVKPL_04-15	17° 05' 51.0"	75° 43' 53.2"
68.		MVKPL_04-16	17° 05' 38.9"	75° 43' 45.7"
69.		MVKPL_04-17	17° 05' 30.6"	75° 43' 49.0"
70.		MVKPL_04-18	17° 06' 02.7"	75° 44' 32.2"

71.		MVKPL_04-19	17° 05' 53.1"	75° 44' 20.5"
72.		MVKPL_04-20	17° 05' 48.0"	75° 44' 11.2"
73.		MVKPL_04-21	17° 05' 42.7"	75° 44' 20.2"
74.	Feeder 5	MVKPL_05-01	17° 05' 54.8"	75° 40' 38.6"E
75.		MVKPL_05-02	17° 05' 49.1"	75° 40' 40.6"
76.		MVKPL_05-03	17° 05' 43.2"	75° 40' 40"
77.		MVKPL_05-04	17° 05' 37.5"	75° 40' 39.2"
78.		MVKPL_05-05	17° 05' 31.7"	75° 40' 38.1"
79.		MVKPL_05-06	17° 5' 26.1"	75° 40' 34"
80.		MVKPL_05-07	17° 05' 20.1"	75° 40' 30.9"
81.		MVKPL_05-08	17° 05' 13.9"	75° 40' 32.7"
82.		MVKPL_05-09	17° 05' 44.4"	75° 41' 52.6"
83.		MVKPL_05-10	17° 05' 29.6"	75° 41' 42.6"
84.		MVKPL_05-11	17° 05' 25.2"	75° 41' 26.4"
85.		MVKPL_05-12	17° 05' 23.1"	75° 41' 49"
86.		MVKPL_05-13	17° 05' 16.5"	75° 41' 48"
87.		MVKPL_05-14	17° 05' 12.5"	75° 41' 59.3"
88.		MVKPL_05-15	17° 05' 3.4"	75° 41' 57.6"
89.		MVKPL_05-16	17° 05' 52.3"	75° 41' 36.9"
90.		MVKPL_05-17	17° 05' 45.3"	75° 41' 33"
91.		MVKPL_05-18	17° 05' 34.7"	75° 41' 32.7"
92.	Feeder 6	MVKPL_06-01	17° 04' 51.4"	75° 42' 53.2"
93.		MVKPL_06-02	17° 04' 43.4"	75° 42' 58.2"
94.		MVKPL_06-03	17° 04' 31.8"	75° 43' 01.3"
95.		MVKPL_06-04	17° 04' 25.3"	75° 43' 0.4"
96.		MVKPL_06-05	17° 05' 9.3"	75° 43' 42.7"
97.		MVKPL_06-06	17° 05' 5.6"	75° 43' 49.8"
98.		MVKPL_06-07	17° 04' 53"	75° 43' 54.7"
99.		MVKPL_06-08	17° 04' 45.3"	75° 44' 0.8"
100.		MVKPL_06-09	17° 04' 28"	75° 44' 9.1"
101.		MVKPL_06-10	17° 04' 20.3"	75° 44' 12.4"
102.		MVKPL_06-11	17° 04' 12.7"	75° 44' 13.8"
103.		MVKPL_06-12	17° 03' 48.9"	75° 44' 23.9"
104.		MVKPL_06-13	17° 03' 55.5"	75° 44' 22.7"
105.		MVKPL_06-14	17° 04' 57.8"	75° 42' 49.1"
106.		MVKPL_06-15	17° 04' 9.1"	75° 44' 22.6"
107.		MVKPL_06-16	17° 04' 5.2"	75° 43' 45.8"

108.		MVKPL_06-17	17° 04' 1.3"	75° 45' 0"
109.		MVKPL_06-18	17° 03' 41.6"	75° 44' 49.5"
110.		MVKPL_06-19	17° 03' 55"	75° 43' 44.1"
111.		MVKPL_06-20	17° 03' 44.1"	75° 44' 49"
112.		MVKPL_06-21	17° 03' 50.6"	75° 44' 48.9"

1.8 Title and Reference of Methodology

Methodology: ACM0002: Grid-connected electricity generation from renewable sources -- Version 16.0, Sectoral Scope: 01, EB 81, Annex 9

<https://cdm.unfccc.int/methodologies/DB/EY2CL7RTEHRC9V6YQHLAR6MJ6VEU83>

The project activity also takes reference from following Tools from the tools prescribed by applied methodology:

1. Tool for the demonstration and assessment of additionality -- Version 07.0.0, EB 70, Annex 8, <https://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-01-v7.0.0.pdf>
2. Tool to calculate the emission factor for an electricity system -- Version 05.0, EB 87, Annex 09, <https://cdm.unfccc.int/methodologies/PAmethodologies/tools/am-tool-07-v5.0.pdf>

1.9 Participation under other GHG Programs

The PP has not participated under any other GHG program with this project activity

1.10 Other Forms of Credit.

Emission Trading Programs and Other Binding Limits: The PP has not applied this project in any Emission Trading Programs and other Binding Limits.

Other Forms of Environmental Credit: The PP has not applied this project in any other form of environmental credits other than Tamil Nadu 45 MW WTGs. The electricity generated from 45 MW REC component of Tamil Nadu are not included for VCU calculations to avoid any double accounting. The HTSC numbers DRA 01,03,04,05,06,07,08,09,12,13,15,17,18,21,22,23,24,25,26,27,31,32,33,43,44,46,47,48,49, 54 (TOTAL 30 WTGs of 1.5 MW from Tamil Nadu site) are availing REC. Thus electricity generated from these WTGs having REC component are not considered for VCU calculations for current complete monitoring period.

1.11 Sustainable Development Contributions

As this section is not mandatory now hence no Sustainable development contribution is claimed right now. In case if required in future, separate SDC report will be submitted to VERRA.

2 SAFEGUARDS

2.1 No Net Harm

The project does not involve any potential negative environmental and socio-economic impacts and hence this criterion is not applicable to this project activity.

2.2 Local Stakeholder Consultation

The stakeholders identified for the project were: the usual occupants of the villages around and the local communities, NGOs, governmental agencies, employees, contractors. Local population is considered to be a major stakeholder with respect to the project activity. The stakeholders of the project activity were invited to attend the stakeholder meeting. Personal invitations were also sent to the prominent members (villagers, local community people) of the regions in the vicinity.

A discussion was held in which the views of the local stakeholders were addressed. The stakeholder meeting was organised at all of the three locations i.e Burgula, Salvasang and Vagarai on the dates given below at the time of validation of this project activity.

Tamil Nadu	
Date of Invitation	Meeting date
10-October-2012	23-October-2012
	24-October-2012
	25-October-2012
Andhra Pradesh	
Date of Invitation	Meeting date
12-April-2013	22-April-2013
Karnataka	
Date of Invitation	Meeting date
11-April-2013	21-April-2013

Representative of the project proponent explained the purpose of the meeting and detailed each questions in the questionnaire. He further explained about the advantages of the wind energy generation and explained how the project would help in reducing demand supply gap in environment friendly manner.

According to the feedback received from the stakeholders, due to the erection of wind farms the socioeconomic situation in the area and the village people's living standard has been improved. It has not only provided employment but also significantly contributed to the infrastructure development likes roads. Local Stakeholder consultation had been carried out

during VCS registration of this project activity. There were no comments that required follow up action from PP.

The PP also placed a grievance register onsite in where the stakeholder can put down his/her complain and the same if found genuine will be addressed immediately. During the current monitoring period, no negative comments are received from the local stakeholders. Thus, no any mitigations has been applied.

2.3 AFOLU-Specific Safeguards

Not required as this is a non-AFOLU project activity.

3 IMPLEMENTATION STATUS

3.1 Implementation Status of the Project Activity

The Project Activity envisages implementation of a 233.1 MW wind power project consisting of 156 Wind TurbineGenerators (WTGs) of individual capacity 0.85 MW in Andhra Pradesh and Karnataka state of India by Mytrah Vayu Krishna Private Limited. And another 67 Wind Electric Generators of individual capacity 1.5 MW in Tamil Nadu state of India by Mytrah Vayu (Majira) Private Limited. All the 223 Wind Turbine Generators (WTGs) which are part of the project activity are commissioned and the commissioning details are provided in Appendix-1.

The project has been under operation since commissioning without any major breakdowns. Though normal breakdowns due to O&M measures are continuously being worked upon by the dedicated O&M contractor for the projects WTGs. There has been no event that may have an impact on the GHG emissions or removals during the current monitoring period.

Further, there are no changes to the project participant for the project activity during the monitoring period.

3.2 Deviations

3.2.1 Methodology Deviations

There has not been any methodology deviation during the aforesaid monitoring period.

3.2.2 Project Description Deviations

. Deviation 1 for Mytrah Energy India Limited

This project Tamilnadu site WTGs are under group captive since commissioning. To meet

group captive consumers annual energy requirement, banking is done during high wind season ((i.e., from June to October) and then those units will get utilize in low wind season (ie. from Nov to Mar). Due to this process electricity in invoice is different than JMR and cannot be consistent and not appropriate to compare or to take lower values as conservative approach. Also TANGEDCO will deduct Transmission & Distribution loss in generating end while doing the energy allocation. This T&D loss will vary based on consumer drawal voltage (3.06%, 4.24%. Due to above reason, the comparison of JMR and invoices value for Tamilnadu Site (Vagarai) is not appropriate as there is adjustment of electricity due to banking as explained above. Thus PP is considering the JMR value for net electricity supplied to grid and for emission reduction calculations. There is no cross check possible due to difference in JMR and invoice values due to banking for Tamilnadu site, hence only JMR value is considered for ER calculations. State electricity board is doing adjustment in invoice based on JMR value. Hence month wise JMR and invoice is not matching. Since JMRs are issued by state electricity board and authentic, JMR values are considered for ER calculations. There is no material impact on ER calculations as primary source of data are correctly applied for ER calculations.

This deviation has already been approved during previous verification.

Deviation-2

For Burgula site of Andhra Pradesh, there is no individual meter which shows the generation from this site. The combined generation is shown in meter located at 132/33 KV, Racharla and JMR issued for 39.7 MW. This was requested in previous verification.

Deviation-3

For Burgula site of Andhra Pradesh, export value for 37.4 MW is given and can be used for calculation but the import values need to be apportioned to obtain import for 37.4 MW. This was requested in previous verification.

Deviation-4

The invoices for Burgula site is generated on export value. The total generation cannot be cross-checked with invoice. Hence, as conservative approach the minimum of invoice JMR and Invoice is considered for emission reduction. This was requested in previous verification.

3.3 Grouped Projects

The project is not a grouped project.

4 DATA AND PARAMETERS

4.1 Data and Parameters Available at Validation

Data / Parameter	EF _{grid,OM,y}
Data unit	tCO ₂ /MWh
Description	Operating Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 10, December 2014
Value applied	0.9887
Justification of choice of data or description of measurement methods and procedures applied	Calculated as per “Tool to calculate the emission factor for an data or description of electricity system, version 05.0” as 3-year generation weighted measurement methods average using data for the years 2011-2012, 2012-2013 & and procedures applied 2013- 2014. The data are obtained from “CO ₂ Baseline Database for Indian Power Sector” version 10.0, published by the Central Electricity Authority, Ministry of Power, Government of India
Purpose of Data	For the calculation of the Baseline Emission
Comments	This parameter is fixed ex-ante for the entire crediting period.

Data / Parameter	EF _{grid,BM,y}
Data unit	tCO ₂ /MWh
Description	Build Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 10, December 2014
Value applied	0.9609
Justification of choice of data or description of measurement methods and procedures applied	Calculated as per “Tool to calculate the emission factor for an electricity system, version 05.0” for the year 2013-2014. The data is obtained from “CO ₂ Baseline Database for Indian Power Sector” version 10.0, published by the Central Electricity Authority, Ministry of Power, Government of India.
Purpose of Data	For the calculation of the Baseline Emission
Comments	This parameter is fixed ex-ante for the entire crediting period.

Data / Parameter	EF _{grid,CM,y}
Data unit	tCO ₂ /MWh
Description	Combines Margin CO ₂ emission factor in year y
Source of data	Calculated from CEA database, Version 10, December 2014
Value applied	0.9817

Justification of choice of data or description of measurement methods and procedures applied	The combined margin emissions factor is calculated as follows: $EF_{grid,CM,y} = EF_{grid,OM,y} * W_{OM} + EF_{grid, BM,y} * W_{BM}$ $EF_{grid,CM,y} = \text{Build margin CO}_2 \text{ emission factor in year } y \text{ (tCO}_2\text{/MWh)}$ $EF_{grid,OM,y} = \text{Operating margin CO}_2 \text{ emission factor in year } y \text{ (tCO}_2\text{/MWh)}$ $W_{OM} = \text{Weighting of operating margin emissions factor (\%)} = 75\%$ $W_{BM} = \text{Weighting of build margin emissions factor (\%)} = 25\%$
Purpose of Data	For the calculation of the Baseline Emission
Comments	This parameter is fixed ex-ante for the entire crediting period.

4.2 Data and Parameters Monitored

Data / Parameter	$EG_{PJ,y}$
Data unit	MWh
Description	Quantity of net electricity generation supplied by the project (Wind) plant/unit to the grid in year y
Source of data	Credit note/ JMR/Form B reports from respective state electricity board
Description of measurement methods and procedures to be applied	Quantity of net electricity generation supplied by the project (Wind) plant/unit to the grid in year y Credit note/ JMR/Form B reports from respective state electricity board Quantity of net electricity generation supplied by the project (Wind) plant/unit to the grid in year y $EG_{PJ,y} = EG_{BLKNy} + EG_{BLTNy} + EG_{BLAPy}$ Where, $EG_{BLKNy} = EG_{Export,KN} - 115\% * EG_{Import} - \text{Transmission Loss (TE,KN)}$ $EG_{BLTNy} = EG_{Export} - EG_{Import}$ $EG_{BLAPy} = EG_{Export} - EG_{Import} * 37.4/39.7$ For Karnataka and Tamil Nadu- The value of net electricity generation supplied to the grid as per Monthly electricity form B /Credit Note or Joint Meter Reading Report forms the basis for calculation of the emission reductions; which can be cross checked from the invoice raised to DISCOM & Adjustment reports (in case of captive utility). For Andhra Pradesh- The value of export can be cross checked with the invoice raised to DISCOM, Net electricity supplied to is calculated as the difference of the measured values of “export” and “import” of electricity through the dedicated SEB energy meter installed at the delivery point.

	Monthly meter readings are taken from the main and check meter installed at metering point and certified by the representatives of SEB Officials and the representatives of the project proponent for apportioning procedure refer section 3.3
Frequency of monitoring/recording	Continuous monitoring hourly measurement and at least monthly recording.
Value monitored	13,130
Monitoring equipment	Monitoring: Tri vector meter is used Data type: Measured Type of meter: Static type meter (Main & Check). Both are Bidirectional meters. Class of meter:0.2s.
QA/QC procedures to be applied	The calibration of all the meters is undertaken at required intervals and faulty meters are duly replaced immediately. The meters are of accuracy class 0.2s. The meter accuracy class and calibration interval is under purview of state electricity board and PP does not have any control on it. It is also noted that apportioning procedure is under control of state electricity board and PP do not have any control on it. The available parameter to PP is the net electricity supplied to grid and same parameter is mentioned as monitoring parameter The Net electricity exported to the grid is cross checked against the invoice raised by the PP towards the DISCOM and Adjustment Reports in case of captive consumption. For Tamil nadu site, being group captive consumption banking of electricity is done, hence JMR value is considered for VCU calculations as per deviation request mentioned in section 2.3.2 ofVCS PD.
Purpose of the data	Calculation of Baseline emissions
Calculation method	-
Comments	The data would be archived electronically and maintained for the entire crediting period plus two years.

4.3 Monitoring Plan

Aim of monitoring:

The monitoring procedure sets guidelines for the project investor to monitor the parameters regularly and to ensure quality and accuracy in monitoring. It elaborates on the functions of the monitoring team and procedures to be followed in monitoring of the CDM parameters.

The monitoring includes all the equipment's that contribute towards reduction in GHG emissions. Since the project activity focuses mainly on the generation of renewable power

from the WTGs, it is important to monitor all the equipment's involved in the metering of all the necessary instruments.

The monitoring plan has been prepared in accordance with the applied methodology, ACM0002 Version 16.0. The project investor has a well-defined management structure for monitoring the project activity.

Monitoring Plan at Karnataka

The main parameter to be monitored for a wind project is the Quantity of net electricity supplied to the grid as a result of the implementation of the CDM project activity in year y. The parameter is measured as electricity export, import and transmission loss, which was issued by BESCO officials and recorded in the B-Form and issued monthly to the project proponent. These monthly reports for the entire monitoring period form the basis to report the emission reductions achieved due to the project activity. The project proponent in turn raises the invoices to the BESCO for the electricity supplied to the grid. The electricity is measured by two-way energy meters of an accuracy class of 0.2 which are calibrated periodically by officials from the BESCO/KPTCL

The procedure for calculation of transmission loss as given in the PPA is set-out below:

$$Z = ((X1+X2+X3...+Xn)-Y)/((X1+X2+X3...+Xn)) \times 100$$

Z = Percentage transmission loss for export incurred in transmission line between the meter located at 33 kV metering point and the meters located at bulk 220 metering point (bulk meter: main and check) high voltage side of receiving sub-station.

X_i = Energy Export Reading of energy meter installed at 33 kV metering point

Y = Energy Export Reading at bulk meter installed at high voltage side of transformer of the receiving station 220kV.

X1, X2, X3, Xn are the meters that are installed at 33kV metering point and are connected to the receiving substation by internally connected lines to the receiving station.

The Export Reading X_i is adjusted for transmission loss that is determined by the state utility and is applied directly to the JMR (Form B) taken at 33 kV metering point. This can be checked from the JMR signed jointly by the representatives of PP and the state utility.

Transmission Loss in Export (TE) = Percentage Transmission Loss (Z) * Energy Export at 33kV metering point ($EG_{Export,KN}$)

Empirical Formula for Energy Export after adjustment of transmission loss (Equation 1)

Net Energy Export after adjustment of transmission loss = $EG_{Export,} - TE$

The transmission loss in export is generally less than 5%. However, in case of Energy Import, the state utility conservatively applies adjustment of 15% to the import values noted at 33 kV metering point

Transmission Loss in Import (TI) = 15% * Energy Import at 33kV metering point ($EG_{Import, KN}$)

Empirical Formula for Energy Import after adjustment of transmission loss (Equation 2)

$$\begin{aligned} \text{Net Energy Import after adjustment of transmission loss} &= EG_{Import} + 15\% * EG_{Import} \\ &= 115\% * EG_{Import} \end{aligned}$$

Therefore, Energy Supplied to Grid after adjustment of transmission loss is difference of equation 1 and 2 as given in the Form B signed jointly by representatives of PP and the state utility.

$$EG_{BL,KN,y} = EG - 115\% * EG - \text{Transmission Loss } (T_{E,KN})$$

The Joint meter reading noted at 33 KV metering location contains the following data:-

1. Electricity Export ($EG_{Export,KN}$)
2. Electricity Import ($EG_{Import,KN}$)
3. Transmission Loss ($TE_{,KN}$) between 33 kV metering point and 220 Kv metering point
4. Net Electricity supplied to the Grid [$EG_{BL,KN,y} = EG_{Export,KN} - 115\% * EG_{Import,KN} - TE_{,KN}$]

Form B is signed by the representatives of PP and the state utility. The net electricity supplied to the grid can be cross checked from the invoices raised on the state utility for supply of net electricity supplied to the grid.

Monitoring Plan at Tamil Nadu Reading of net electricity imports & export is taken at the metering point of TNEB, located at yard approximately 5 to 7 meters from the WTG. Each WTG has its individual EB meter, installed by the SEB. Hence, T & D losses are considered between WTG and TNEB meter.

The import & export figure at WTG controller is recorded in the logbooks (manual / electronic) of the O&M contractor / Investors representative on a daily basis. This data is preserved both in paper & electronic form. The summary of the generation is submitted by the O&M contractor / Investors representative to the investor on the monthly basis.

The TNEB meter is the main source for monitoring net export to the grid. On mutually decided / SEB official availability date of each month, the reading from the TNEB meter is recorded by the engineers of the SEB in presence of the O & M contractor/ Investors representative. Subsequently the Tamil Nadu Electricity Board statements is prepared.

A monthly statement is issued by the State Utility every month to the Project investor against sale of power. Based on the monthly sale of power, invoice is raised to TNEB.

QA/QC procedures:

Energy meters are calibrated once in a five year and faulty meters are duly replaced immediately. The entire responsibility of this task lies with the state utility. The meters have an accuracy class of at least 0.5s. TNEB has an on-site testing & calibration arrangement; hence there is no need to dismantle the meter for calibration. In case the meters are found faulty and hard to calibrate against the prescribed accuracy class the meter is replaced by the state utility.

If during any of monthly measurement, main meter is found to be beyond permissible limit of error, then meter is calibrated immediately & the correction factor applicable for the main meter is used for energy computation at time of such test checks. For the period thereafter the measurement is continued in accordance with the calibrated main meter.

Data Management and Data Archiving:

Copies of the break-up sheet, invoices raised on Discom and sales receipts are retained and archived for the entire crediting period plus two years by the project investor.

Procedures for Data Adjustments / Uncertainties:

Data uncertainties are likely under following conditions:

- In case of error in TNEB meter
- When records are lost

If during any of monthly measurement, main meter is found to be beyond permissible limit of error, then meter shall be calibrated immediately & the correction factor applicable for the main meter shall be used for energy computation at time of such test checks. For the period thereafter the measurement shall be continued in accordance with the calibrated main meter. When records are lost, the Tamil Nadu Electricity Board Statements are used as reference.

Meter calibration: The meters are tested for accuracy and calibration of the meters is taken care of, following the applicable guidance. As per the national guidelines given by CEA, electricity meters have to be calibrated once in every 5 years,

Hence the meters are scheduled to be calibrated at least once in every five years^{1,2}

Calculation method

The generated electricity is exported to TNEB grid and the exported electricity is measured by the TNEB energy meter. Representative Officer from Tamil Nadu Electricity Board (TNEB) prepares and provides the TNEB Statement. Once in a month, the designated person takes the TNEB energy meter readings and records the initial and final readings for Export and Import. The difference between the initial and final readings gives net export and net import. The difference between the net export and net import is recorded as Net Generation.

² As per VCS approved PD

Net exports for Tamil Nadu $EG_{BL, TN,y} = EG_{Export} - EG_{Import}$

Monitoring Plan at Andhra Pradesh

Metering system and monitoring plan:

- The reading is taken at the individual WTG end by the technology operator on site.
- A Joint Meter Reading combined for 39.4 MW is taken by the representatives of PP and APTRANSCO at the high voltage side of the step up transformer installed at the substation at a particular date.
- In case the main metering system is not in service, then the check metering system is to be used until the main system is back to service.
- Meter reading is jointly signed by both the representatives.
- The main and the check metering systems are sealed in presence of representatives of Power producers, and APTRANSCO.
- When any of these metering systems is found to be outside acceptable limits of accuracy or otherwise not functioning properly, it is repaired, recalibrated or replaced.
- PP raises a monthly energy bill/statement based on the JMR at the end of each calendar month and the payment by State Electricity Board is done on this basis. The billing and payment records are maintained by the PP.
- Calibration and Testing of Meters are done once in 5 years.

Calculation of data:

Net exports for Andhra Pradesh $EG_{BL, AP,y} = EG_{Export} - EG_{Import} * (37.4/39.7)$

QA and QC Procedures

The electricity meter with accuracy class 0.2s at substation end (i.e. one main and one check meter) are installed.



Data Storage and Archiving All the data items monitored under the monitoring plan will be kept for 2 years after the end of crediting period or till the last issuance of VCUs for this project activity, whichever occurs later. The data will be archived both electronically and manually, and kept in safe storage by PP.


In the event when the individual verification period dates and billing cycle dates of the various WTGs in the project activity do not coincide, then the monitoring procedure is-

- X : Sum of generation during partial days of the month recorded at controller meter (kwh) source – Electronic / Manual Log Book
- Y : Total generation during the month recorded at controller meter (kwh/month)

- $Z = X/Y$: Ratio
 B : Net Energy export by the WTG as per Monthly Report on Generation and Consumption
 $Z*B$: Generation of partial days for calculating emission reduction (kwh)

Metering Arrangements at respective project sites:

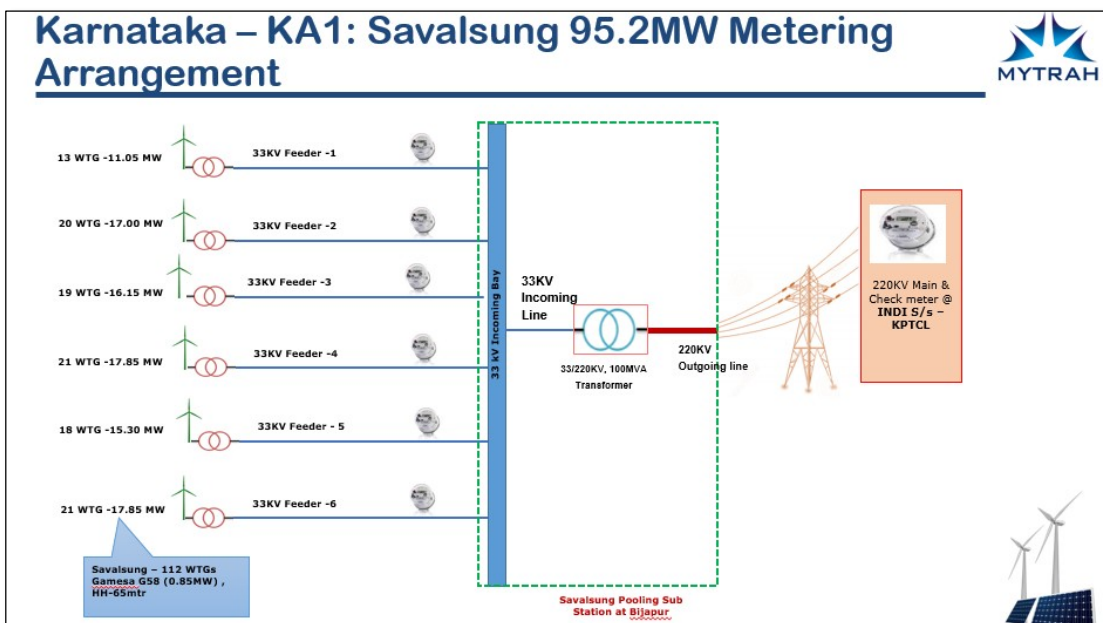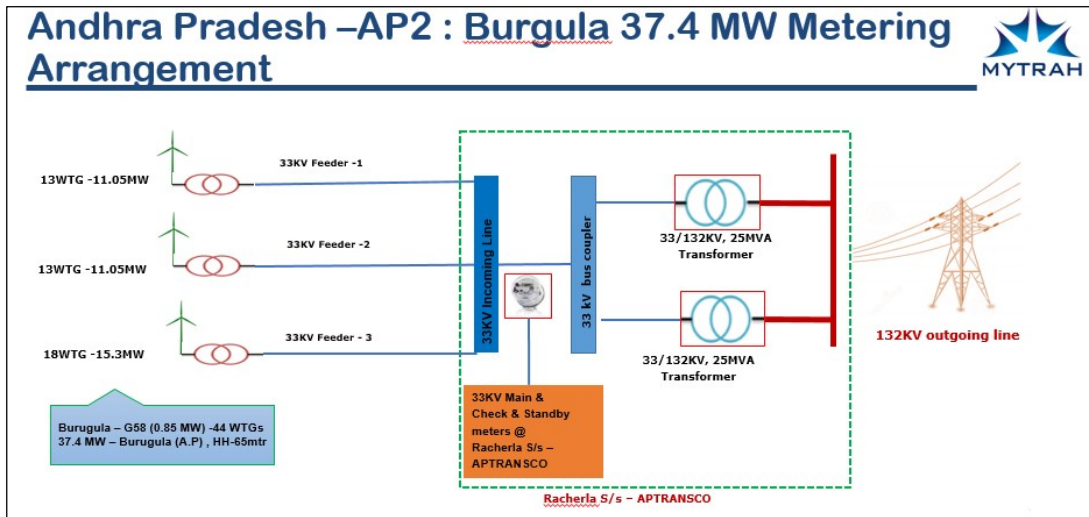

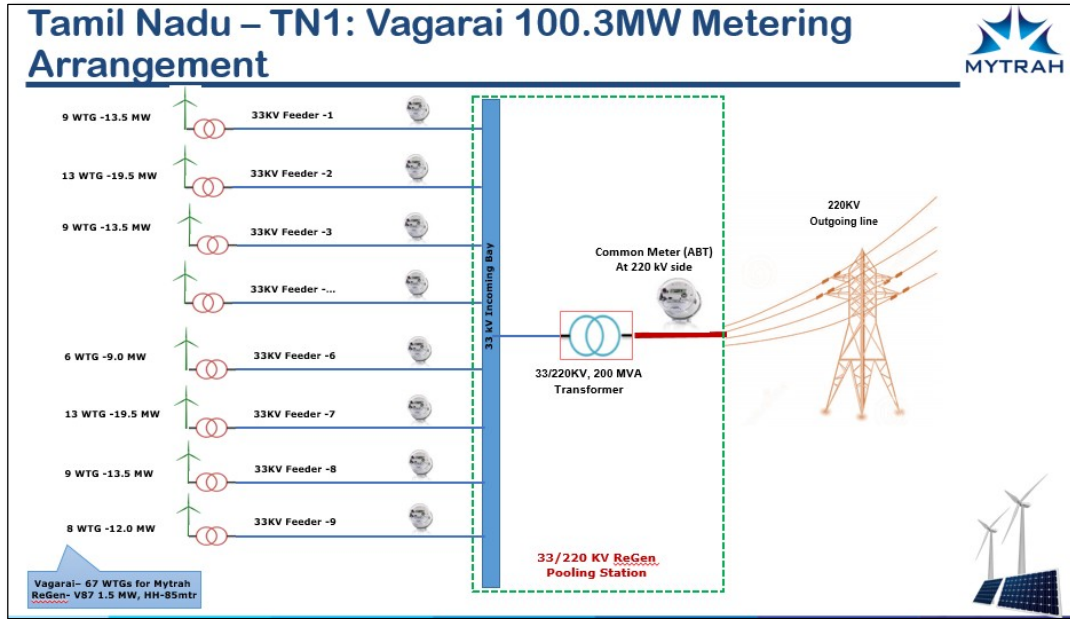

5 QUANTIFICATION OF GHG EMISSION REDUCTIONS AND REMOVALS

5.1 Baseline Emissions

As per para 46 of ACM0002 version 16.0, Baseline emissions include only CO₂ emissions from electricity generation in fossil fuel fired power plants that are displaced due to the project activity. The methodology assumes that all project electricity generation above baseline levels would have been generated by existing grid-connected power plants and the addition of new grid-connected power plants. The baseline emissions are to be calculated as follows:

$$BE_y = EG_{PJ,y} * EF_{grid,CM,y}$$

Where:

BE_y= Baseline emissions in year y (tCO₂)

EG_{PJ,y} = Quantity of net electricity generation that is produced and fed into the grid as a result of the implementation of the VCS project activity in year y (MWh/yr)

$EF_{grid,CM,y}$ = Combined margin CO₂ emission factor for grid connected power generation in year y calculated using the latest version of the “Tool to calculate the emission factor for an electricity system” (tCO₂/MWh)

Baseline Emissions

As per the equation 7 of the methodology ACM 0002 (Version 16.0),

$$BE_y = EG_{PJ, y} * EF_{grid, CM, y} \quad (1)$$

Where:

- BE_y : Baseline emissions in year y (tCO₂e/yr)
- $EG_{PJ, y}$: Quantity of net electricity generation that is produced and fed into the grid as a result of the implementation of the CDM project activity in year y (MWh/yr)
- $EF_{grid, CM, y}$: Combined margin CO₂ emission factor for grid connected power generation in year y calculated using the latest version of the “Tool to calculate the emission factor for an electricity system” (tCO₂e/MWh)

Thus, $BE_y = EG_{PJ, y} * EF_{grid, CM, y}$

$EG_{PJ, y}$	=	13,130 MWh
$EF_{grid, CM, y}$	=	0.9817 tCO ₂ e
BE_y	=	13,130 * 0.9817
	=	12,889 tCO ₂ e (Round down value)

5.2 Project Emissions

The project activity involves in harnessing wind power. So the emissions from the project are zero.

5.3 Leakage

No leakage emissions have been considered and hence the leakage emission is zero.

5.4 Net GHG Emission Reductions and Removals

As per equation number (13) of the applied methodology, emission reductions are calculated as follows:

$$ER_y = BE_y - PE_y \quad (7)$$

Where:

ER_y : Emission reductions in year y (tCO₂e/yr)

BE_y : Baseline emissions in year y (tCO₂e/yr)

PE_y : Project emissions in year y (tCO₂e/yr)

Year	Baseline emissions or removals (tCO ₂ e)	Project emissions or removals (tCO ₂ e)	Leakage emissions (tCO ₂ e)	Net GHG emission reductions or removals (tCO ₂ e)
1-March-2022 to 31-March-2022	12,889	0	0	12,889
Total	12,889	0	0	12,889

Considering the annual average emission reductions as per registered PD which is 479,448 tonnes of CO₂ per year, the number of days covered during this monitoring period comes out to be 31 days and also 45 MW capacity of Tamilnadu site availing REC component. The total number GHG emission reductions achieved during this monitoring period is 12,889tCO₂ which is 68.35 % lower than the estimated value which is conservative. The reason for the same is exclusion of 45 MW REC component.

APPENDIX I: DATE OF COMMISSIONING

Date of Commissioning of WTGs for Tamil Nadu

Vagarai@ Tamil Nadu - 100.5 MW(1.5 * 67)			
ReGen make Vensys - 87 1.5 MW WTG of model			
S. No.	Machine ID	HTSC No.	DOC ³
1.	KOO - 518	DRA 001	1-June-2014
2.	KOO - 1359	DRA 003	1-June-2014
3.	APY - 241	DRA 004	1-June-2014
4.	APY - 416	DRA 005	1-June-2014
5.	PAR - 9	DRA 006	1-June-2014
6.	PON - 534	DRA 008	1-June-2014
7.	PON - 1043	DRA 009	1-June-2014
8.	NAL-119	DRA 012	1-June-2014
9.	NAL - 81	DRA 013	1-June-2014

10.	NAL - 57	DRA 015	1-June-2014
11.	MAN - 210	DRA 017	1-June-2014
12.	MAN - 898	DRA 018	1-June-2014
13.	MAN - 802	DRA 021	1-June-2014
14.	KON - 556	DRA 022	1-June-2014
15.	KON - 563	DRA 023	1-June-2014
16.	KON - 590	DRA 024	1-June-2014
17.	KON - 640	DRA 025	1-June-2014
18.	KON - 658	DRA 026	1-June-2014
19.	KON - 621	DRA 027	1-June-2014
20.	KON - 501	DRA 031	1-June-2014
21.	ALA - 1639	DRA 043	23-June-2014
22.	ALA - 1946	DRA 044	23-June-2014
23.	NAL - 434	DRA 049	23-June-2014
24.	KON - 234	DRA 054	14-July-2014
25.	PAR - 50	DRA 007	1-June-2014
26.	MAN - 625	DRA 032	1-June-2014
27.	MAN - 604	DRA 033	1-June-2014
28.	ALA-2301/2304	DRA 046	23-June-2014
29.	ALA - 1569	DRA 047	23-June-2014
30.	ALA-2352	DRA 048	23-June-2014
31.	KOO - 1157	DRA 002	1-June-2014
32.	PON - 1081	DRA 010	1-June-2014
33.	MAN - 940	DRA 019	1-June-2014
34.	PON - 1565	DRA 037	23-June-2014
35.	PON - 1568	DRA 038	23-June-2014
36.	VEL - 1936	DRA 039	23-June-2014
37.	ALA - 1618	DRA 042	23-June-2014
38.	PON - 908	DRA 050	23-June-2014
39.	PON - 1203	DRA 052	23-June-2014
40.	MAN - 963	DRA 055	16-July-2014
41.	PON - 1021	DRA 011	1-June-2014
42.	KUL - 652	DRA 014	1-June-2014
43.	PON - 4	DRA 016	1-June-2014
44.	MAN-828	DRA 020	1-June-2014
45.	KON - 618	DRA 028	1-June-2014
46.	KON-395	DRA 029	1-June-2014
47.	KON-451	DRA 030	1-June-2014
48.	APA-84	DRA 034	1-June-2014
49.	PUN-270	DRA 035	1-June-2014

50.	PUN - 34	DRA 036	4-June-2014
51.	VEL-1702	DRA 040	23-June-2014
52.	KAL-93	DRA 041	23-June-2014
53.	ALA-2290	DRA 045	23-June-2014
54.	PON - 775	DRA 051	23-June-2014
55.	ALA - 2260	DRA 053	23-June-2014
56.	MET 1664	DRA 065	09-January-2015
57.	NAL - 445	DRA 061	03-December-2014
58.	KOO-1036	DRA 056	31-October-2014
59.	VEL-1540	DRA 060	03-December-2014
60.	KOO-1174	DRA 058	31-October-2014
61.	KOO-1000	DRA 057	31-October-2014
62.	PON-1304	DRA 059	31-October-2014
63.	APY-247	DRA 064	06-January-2015
64.	KON-411	DRA 67	26-February-2015
65.	KOO - 581	DRA 062	18-December-2014
66.	VEL - 2119	DRA 063	24-December-2014
67.	ALA 1385	DRA 066	04-February-2015

Date of commissioning of WTG at Karnataka

Savalsang@ Karnataka - 95.20 MW (0.85*112)		
Gamesa Make WTG model G53/850 kW		
S. No.	Machine ID	DOC
1	MVKPL-1-03	29-April-2014
2	MVKPL-1-04	2-June-2014
3	MVKPL-1-05	2-June-2014
4	MVKPL-1-06	29-April-2014
5	MVKPL-1-07	29-April-2014
6	MVKPL-1-08	29-April-2014
7	MVKPL-1-09	29-April-2014
8	MVKPL-1-10	29-April-2014
9	MVKPL-1-11	29-April-2014
10	MVKPL-1-12	29-April-2014
11	MVKPL-1-13	29-April-2014
12	MVKPL-1-14	29-April-2014
13	MVKPL-1-15	29-April-2014

14	MVKPL-2-01	29-April-2014
15	MVKPL-2-02	29-April-2014
16	MVKPL-2-03	29-April-2014
17	MVKPL-2-04	29-April-2014
18	MVKPL-2-05	29-April-2014
19	MVKPL-2-06	29-April-2014
20	MVKPL-2-07	29-April-2014
21	MVKPL-2-08	29-April-2014
22	MVKPL-2-09	29-April-2014
23	MVKPL-2-10	29-April-2014
24	MVKPL-2-11	29-April-2014
25	MVKPL-2-12	29-April-2014
26	MVKPL-2-13	29-April-2014
27	MVKPL-2-14	29-April-2014
28	MVKPL-2-15	29-April-2014
29	MVKPL-2-16	29-April-2014
30	MVKPL-2-17	29-April-2014
31	MVKPL-2-18	29-April-2014
32	MVKPL-2-19	29-April-2014
33	MVKPL-2-20	29-April-2014
34	MVKPL-3-01	29-April-2014
35	MVKPL-3-02	29-April-2014
36	MVKPL-3-03	29-April-2014
37	MVKPL-3-04	29-April-2014
38	MVKPL-3-05	29-April-2014
39	MVKPL-3-06	29-April-2014
40	MVKPL-3-07	29-April-2014
41	MVKPL-3-08	29-April-2014
42	MVKPL-3-09	29-April-2014
43	MVKPL-3-10	29-April-2014
44	MVKPL-3-11	29-April-2014
45	MVKPL-3-12	29-April-2014
46	MVKPL-3-13	29-April-2014
47	MVKPL-3-14	29-April-2014
48	MVKPL-3-15	29-April-2014
49	MVKPL-3-16	29-April-2014
50	MVKPL-3-17	29-April-2014
51	MVKPL-3-18	2-June-2014
52	MVKPL-3-19	29-April-2014
53	MVKPL-4-01	2-June-2014

54	MVKPL-4-02	29-April-2014
55	MVKPL-4-03	29-April-2014
56	MVKPL-4-04	29-April-2014
57	MVKPL-4-05	29-April-2014
58	MVKPL-4-06	02-June-2014
59	MVKPL-4-07	29-April-2014
60	MVKPL-4-08	29-April-2014
61	MVKPL-4-09	2-June-2014
62	MVKPL-4-10	29-April-2014
63	MVKPL-4-11	29-April-2014
64	MVKPL-4-12	29-April-2014
65	MVKPL-4-13	29-April-2014
66	MVKPL-4-14	29-April-2014
67	MVKPL-4-15	29-April-2014
68	MVKPL-4-16	02-June-2014
69	MVKPL-4-17	02-June-2014
70	MVKPL-4-18	29-April-2014
71	MVKPL-4-19	29-April-2014
72	MVKPL-4-20	29-April-2014
73	MVKPL-4-21	29-April-2014
74	MVKPL-5-01	29-April-2014
75	MVKPL-5-02	29-April-2014
76	MVKPL-5-03	29-April-2014
77	MVKPL-5-04	29-April-2014
78	MVKPL-5-05	29-April-2014
79	MVKPL-5-06	29-April-2014
80	MVKPL-5-07	29-April-2014
81	MVKPL-5-08	29-April-2014
82	MVKPL-5-09	29-April-2014
83	MVKPL-5-10	29-April-2014
84	MVKPL-5-11	29-April-2014
85	MVKPL-5-12	29-April-2014
86	MVKPL-5-13	29-April-2014
87	MVKPL-5-14	02-June-2014
88	MVKPL-5-15	02-June-2014
89	MVKPL-5-16	02-June-2014
90	MVKPL-5-17	02-June-2014
91	MVKPL-5-18	02-June-2014
92	MVKPL-6-01	26-July-2014
93	MVKPL-6-02	26-July-2014

94	MVKPL-6-03	26-July-2014
95	MVKPL-6-04	26-July-2014
96	MVKPL-6-05	26-July-2014
97	MVKPL-6-06	26-July-2014
98	MVKPL-6-07	26-July-2014
99	MVKPL-6-08	26-July-2014
100	MVKPL-6-09	26-July-2014
101	MVKPL-6-10	26-July-2014
102	MVKPL-6-11	23-January-2015
103	MVKPL-6-12	26-July-2014
104	MVKPL-6-13	26-July-2014
105	MVKPL-6-14	26-July-2014
106	MVKPL-6-15	26-July-2014
107	MVKPL-6-16	23-January-2015
108	MVKPL-6-17	26-July-2014
109	MVKPL-6-18	26-July-2014
110	MVKPL-6-19	26-July-2014
111	MVKPL-6-20	23-January-2015
112	MVKPL-6-21	23-January-2015

Date of Commissioning at Andhra Pradesh

Burugula @ Andhra Pradesh - 37.40MW (0.85* 44)		
Gamesa Make WTG model G53/850 kW		
S. No.	Machine ID	DOC
1	Location No. 508	21-February-2014
2	Location No. 509	21-February-2014
3	Location No. 510	21-February-2014
4	Location No. 511	21-February-2014
5	Location No. 512	21-February-2014
6	Location No. 513	21-February-2014
7	Location No. 514	21-February-2014
8	Location No. 515	21-February-2014

9	Location No. 516	21-February-2014
10	Location No. 517	21-February-2014
11	Location No. 518	21-February-2014
12	Location No. 519	21-February-2014
13	Location No. 520	21-February-2014
14	Location No. 521	21-February-2014
15	Location No. 522	21-February-2014
16	Location No. 523	21-February-2014
17	Location No. 524	21-February-2014
18	Location No. 525	21-February-2014
19	Location No. 526	21-February-2014
20	Location No. 527	21-February-2014
21	Location No. 528	21-February-2014
22	Location No. 529	21-February-2014
23	Location No. 530	21-February-2014
24	Location No. 531	21-February-2014
25	Location No. 550	21-February-2014
26	Location No. 551	21-February-2014
27	Location No. 532	15-March-2014
28	Location No. 533	15-March-2014
29	Location No. 534	15-March-2014
30	Location No. 535	15-March-2014
31	Location No. 536	15-March-2014
32	Location No. 537	15-March-2014
33	Location No. 538	15-March-2014
34	Location No. 539	15-March-2014
35	Location No. 540	15-March-2014
36	Location No. 541	15-March-2014

37	Location No. 542	15-March-2014
38	Location No. 543	15-March-2014
39	Location No. 544	15-March-2014
40	Location No. 545	15-March-2014
41	Location No. 546	15-March-2014
42	Location No. 547	15-March-2014
43	Location No. 548	15-March-2014
44	Location No. 549	15-March-2014

APPENDIX II: CALIBRATION DETAILS

Vagarai Tamil Nadu state 55.5 MW (37*1.5 MW WTGs)³ 33 KV Substation

S. No.	HTSC No.	Old meter S. No.	Substation	Meter change date	New meter S. No.	Due date of calibration
1.	DRA 002	1209233	33 Kv	25-May-2017	4321945	24-May-2022
2.	DRA 010	1419032	33 Kv	23-May-2017	4322515	22-May-2022
3.	DRA 019	1209145	33 Kv	22-May-2017	4322252	21-May-2022

³ PP is claiming VCS benefits for only 37 WTGs out of 67 WTGs. Rest 30 WTGs are availing Renewable Energy Certificate (REC) benefits. Meter calibration of the 37 WTGs claiming VCS benefits was done at the date of commissioning. Later on these meters were changed in the year 2017 (respective dates are mentioned in the table above). The calibration records of newly installed meters have been submitted to the DOE and the due date of calibration for the respective meters are mentioned in the above table

4.	DRA 037	1209199	33 Kv	20-May-2017	4322069	19-May-2022
5.	DRA 038	1209234	33 Kv	20-May-2017	4321884	19-May-2022
6.	DRA 039	1209226	33 Kv	05-May-2017	4322063	04-May-2022
7.	DRA 042	1209231	33 Kv	20-May-2017	4321949	19-May-2022
8.	DRA 050	1209232	33 Kv	20-May-2017	4322064	19-May-2022
9.	DRA 052	1419033	33 Kv	20-May-2017	4321888	19-May-2022
10.	DRA 055	1419027	33 Kv	22-May-2017	4322067	21-May-2022
11.	DRA 011	1419024	33 Kv	23-May-2017	4322519	22-May-2022
12.	DRA 014	1419029	33 Kv	23-May-2017	4322517	22-May-2022
13.	DRA 016	1419031	33 Kv	23-May-2017	4322521	22-May-2022
14.	DRA 020	1419030	33 Kv	23-May-2017	4322433	22-May-2022
15.	DRA 028	1419033	33 Kv	22-May-2017	4322566	21-May-2022
16.	DRA 029	1419031	33 Kv	22-May-2017	4322574	21-May-2022
17.	DRA 030	1419029	33 Kv	22-May-2017	4322374	21-May-2022
18.	DRA 034	1419033	33 Kv	23-May-2017	4321977	22-May-2022
19.	DRA 035	1419033	33 Kv	22-May-2017	4322581	21-May-2022
20.	DRA 036	1419031	33 Kv	22-May-2017	4322582	21-May-2022
21.	DRA 040	1419029	33 Kv	25-May-2017	4322160	24-May-2022
22.	DRA 041	1419025	33 Kv	25-May-2017	4321952	24-May-2022
23.	DRA 045	1419031	33 Kv	20-May-2017	4321943	19-May-2022
24.	DRA 051	1419032	33 Kv	20-May-2017	4322065	19-May-2022
25.	DRA 053	1419026	33 Kv	20-May-2017	4321944	19-May-2022
26.	DRA 065	1419026	33 Kv	22-May-2017	4322579	21-May-2022
27.	DRA 061	1319704	33 Kv	20-May-2017	4322154	19-May-2022
28.	DRA 056	1419026	33 Kv	25-May-2017	4321973	24-May-2022
29.	DRA 060	1419032	33 Kv	20-May-2017	4321948	19-May-2022
30.	DRA 058	1419027	33 Kv	23-May-2017	4322514	22-May-2022
31.	DRA 057	1419034	33 Kv	23-May-2017	4322513	22-May-2022
32.	DRA 059	1419031	33 Kv	20-May-2017	4322068	19-May-2022
33.	DRA 064	1419027	33 Kv	20-May-2017	4322066	19-May-2022
34.	DRA 067	1419027	33 Kv	22-May-2017	4322573	21-May-2022

Calibration details for Karnataka site WTGs 95.2 MW (112*0.85 MW WTGs) 33 KV Substation

Location	Meter Type	Meter Serial Number	Make	Substation	Accuracy Class	Calibration Date	Due date of Calibration
	Main Meter	13191120	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025

Feeder 1	Check Meter	13191121	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
Feeder 2	Main Meter	13191094	L & T	33Kv	0.2s	20-May-2017	19-May--2022
	Check Meter	13191095	L & T	33Kv	0.2s	20-May-2017	19-May-2022
Feeder 3	Main Meter	13191100	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
	Check Meter	13191104	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
Feeder 4	Main Meter	13191096	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
	Check meter	13191097	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
Feeder 5	Main Meter	13191114	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
	Check Meter	13191122	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
Feeder 6	Main Meter	13191159	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025
	Check Meter	13191380	L & T	33Kv	0.2s	23-Sep-2020	22-Sep-2025

Calibration details for Andhra Pradesh site WTGs 37.4 MW (44*0.85 MW WTGs) 33K Kv wind metering

Meter Type	Meter meter Serial	Calibration Date	Substation	Due Date	New calibration	Due date
Main Meter	APX01701	28-July-2017	33 Kv	27-July-2022	14-Feb-2022	13-Feb-2027
Check Meter	APX01702	28-July-2017	33 Kv	27-July-2022	14-Feb-2022	13-Feb-2027
Standby Meter	APX01703	28-July-2017	33 Kv	27-July-2022	14-Feb-2022	13-Feb-2027
