

ALTO MAYO CONSERVATION INITIATIVE MONITORING & IMPLEMENTATION REPORT N°5 (2018-2020)



Project Title	Alto Mayo Conservation Initiative [Iniciativa de Conservación Alto Mayo]
Project ID	944
Version	1
Report ID	n/a
Date of Issue	01 September 2020
Project Location	Peru, San Martin Department
Project Proponent(s)	Conservation International – Peru Luis Espinel, Country Director Tel: +51 1 610 0300 Email: l.espinel@conservation.org Website: www.conservation.org/sites/peru/
Prepared By	Conservation International-Peru
Validation/Verification Body	AENOR Internacional, S.A.U. Geneva, 6. 28004 Madrid, Spain Telephone: (+34) 915 294 961 e- mail: medioambiente@aenor.com
GHG Accounting/ Crediting Period	15 June 2008 to 14 June 2028 – 20 Years
Monitoring Period of this Report	15 June 2018 to 14 June 2020 – 2 Years
History of CCB Status	CCB Validation and 1st verification on Dec 12, 2012. CCB 2nd verification on June 02, 2015 CCB 3rd verification on September 09, 2016 CCB 4th verification on December 13, 2018
Gold Level Criteria	Exceptional Biodiversity

Table of Contents

1	Summary of Project Benefits	3
1.1	Unique Project Benefits.....	3
1.2	Standardized Benefit Metrics	3
2	General	6
2.1	Project Description	6
2.2	Project Implementation Status	14
2.3	Stakeholder Engagement.....	37
2.4	Management Capacity and Best Practices	42
2.5	Legal Status and Property Rights	46
3	Climate.....	48
3.1	Monitoring GHG Emission Reductions and Removals	48
3.2	Quantification of GHG Emission Reductions and Removals	54
3.3	Optional Criterion: Climate Change Adaptation Benefits	60
4	Community	60
4.1	Net Positive Community Impacts	60
4.2	Offsite Stakeholder Impacts	68
4.3	Community Impact Monitoring	71
4.4	Optional Criterion: Exceptional Community Benefits	72
5	Biodiversity	72
5.1	Net Positive Biodiversity Impacts	72
5.2	Offsite Biodiversity Impacts.....	80
5.3	Biodiversity Impact Monitoring	83
6	Additional Project Implementation Information.....	84
7	Additional Project Impact Information.....	85

1 SUMMARY OF PROJECT BENEFITS

1.1 Unique Project Benefits

Outcome or Impact	Achievements during the Monitoring Period	Section Reference	Achievements during the Project Lifetime
1) Productive surface under some mechanism of international standards certification	2,109 ha under organic certification	4	2,109 ha under organic certification
2) Revenues generated through direct export of certified products.	US\$ 1,664,587.58	4	US\$ 2,971,242.46
3) Improvement in the AMPF governance ¹	6.25% (May 2018 score: 83.33% and June 2020 score: 89.58%)	3 and 5	27.47% (baseline score: 62.11% done in August 2013)

1.2 Standardized Benefit Metrics

Category	Metric	Achievements during Monitoring Period	Section Reference	Achievements during the Project Lifetime
GHG emission reductions & removals	Net estimated emission removals in the project area, measured against the without-project scenario	Not-applicable		
	Net estimated emission reductions in the project area, measured against the without-project scenario	987,901 tCO ₂	3	8,405,814 tCO ₂
Forest ² cover	For REDD ³ projects: Number of hectares of reduced forest loss in the project area measured against the without-project scenario	2,467 ha	3, 5	19,777 ha
	For ARR ⁴ projects: Number of hectares of	Not applicable		

¹ Governance index was measured by using METT Scorecard

² Land with woody vegetation that meets an internationally accepted definition (e.g., UNFCCC, FAO or IPCC) of what constitutes a forest, which includes threshold parameters, such as minimum forest area, tree height and level of crown cover, and may include mature, secondary, degraded and wetland forests (*VCS Program Definitions*)

³ Reduced emissions from deforestation and forest degradation (REDD) - Activities that reduce GHG emissions by slowing or stopping conversion of forests to non-forest land and/or reduce the degradation of forest land where forest biomass is lost (*VCS Program Definitions*)

Category	Metric	Achievements during Monitoring Period	Section Reference	Achievements during the Project Lifetime
	forest cover increased in the project area measured against the without-project scenario			
Improved land management	Number of hectares of existing production forest land in which IFM ⁵ practices have occurred as a result of the project's activities, measured against the without-project scenario	Not-applicable		
	Number of hectares of non-forest land in which improved land management has occurred as a result of the project's activities, measured against the without-project scenario	1,208 ha	4	3,843 ha
Training	Total number of community members who have improved skills and/or knowledge resulting from training provided as part of project activities	2,851	4	6,540
	Number of female community members who have improved skills and/or knowledge resulting from training provided as part of project activities of project activities	674	4	2,345
Employment	Total number of people employed in of project activities, ⁶ expressed as number of full time employees ⁷	90	4	184
	Number of women employed in project activities, expressed as number of full time employees	18	4	54
Livelihoods	Total number of people with improved livelihoods ⁸ or income generated as a result of project activities	905	4	2,897
	Number of women with improved livelihoods or income generated as a result of project activities	405	4	1,302
Health	Total number of people for whom health	134	4	671

⁴ Afforestation, reforestation and revegetation (ARR) - Activities that increase carbon stocks in woody biomass (and in some cases soils) by establishing, increasing and/or restoring vegetative cover through the planting, sowing and/or human-assisted natural regeneration of woody vegetation (*VCS Program Definitions*)

⁵ Improved forest management (IFM) - Activities that change forest management practices and increase carbon stock on forest lands managed for wood products such as saw timber, pulpwood and fuelwood (*VCS Program Definitions*)

⁶ Employed in project activities means people directly working on project activities in return for compensation (financial or otherwise), including employees, contracted workers, sub-contracted workers and community members that are paid to carry out project-related work.

⁷ Full time equivalency is calculated as the total number of hours worked (by full-time, part-time, temporary and/or seasonal staff) divided by the average number of hours worked in full-time jobs within the country, region or economic territory (adapted from UN System of National Accounts (1993) paragraphs 17.14[15.102];[17.28])

⁸ Livelihoods are the capabilities, assets (including material and social resources) and activities required for a means of living (Krantz, Lasse, 2001. *The Sustainable Livelihood Approach to Poverty Reduction*. SIDA). Livelihood benefits may include benefits reported in the Employment metrics of this table.

Category	Metric	Achievements during Monitoring Period	Section Reference	Achievements during the Project Lifetime
	services were improved as a result of project activities, measured against the without-project scenario			
	Number of women for whom health services were improved as a result of project activities, measured against the without-project scenario	27	4	364
Education	Total number of people for whom access to, or quality of, education was improved as a result of project activities, measured against the without-project scenario	188	4	1,031
	Number of women and girls for whom access to, or quality of, education was improved as a result of project activities, measured against the without-project scenario	27	4	203
Water	Total number of people who experienced increased water quality and/or improved access to drinking water as a result of project activities, measured against the without-project scenario	Not applicable		
	Number of women who experienced increased water quality and/or improved access to drinking water as a result of project activities, measured against the without-project scenario	Not applicable		
Well-being	Total number of community members whose well-being ⁹ was improved as a result of project activities	3,126	4	4,331
	Number of women whose well-being was improved as a result of project activities	1,456	4	1,985
Biodiversity conservation	Change in the number of hectares significantly better managed by the project for biodiversity conservation, ¹⁰ measured against the without-project scenario	144,837 ha	5	123,461 ha
	Number of globally Critically Endangered or Endangered species ¹¹ benefiting from reduced threats as a result of project activities, ¹² measured against the without-project scenario	31	5	33

⁹ Well-being is people's experience of the quality of their lives. Well-being benefits may include benefits reported in other metrics of this table (e.g. Training, Employment, Health, Education, Water, etc.), but could also include other benefits such as empowerment of community groups, strengthened legal rights to resources, conservation of access to areas of cultural significance, etc.

¹⁰ Biodiversity conservation in this context means areas where specific management measures are being implemented as a part of project activities with an objective of enhancing biodiversity conservation.

¹¹ Per IUCN's Red List of Threatened Species

¹² In the absence of direct population or occupancy measures, measurement of reduced threats may be used as evidence of benefit

2 GENERAL

2.1 Project Description

2.1.1 Implementation Description

During these last two years, the work in the management of the Alto Mayo Protected Forest has shown significant progress in the conservation of ecosystems and biodiversity, which benefits the families living in this area since they improve their economic and social standards. This work is based on coordinated actions carried out by the members of the project institutions with the local inhabitants.

In this period, the investment of the project was \$ 8,6 million. The CI team could market more than \$6 million carbon credits that were invested in the operation and sustainability of the Natural Protected Area. Therefore, the involvement of financial partners is crucial in order to keep the articulation of the project in the coming years.

The work with local people, many of whom are members of the COOPBAM, has increased. This enable them to sell their coffee at a higher price to the conventional market. Coffees produced by the AMPF inhabitants are exported to special markets in the United States, Europe, Asia and Australia. This represents higher incomes for these families. During this period, the COOPBAM has exported about 500 thousand kilos which has generated an income of about \$ 1.7 million.

In addition, the population participates more in conservation actions. Their commitment, assumed through the conservation agreements with SERNANP, includes good practices in productive activities such as coffee cultivation, and the report on illegal actions that may be occurring in the AMPF.

Also, the project continued to provide technical assistance to improve the quality of crops. It has given benefits packages such as organic fertilizers and pruning tools as well as ongoing training sessions that have strengthened the ability to implement good environmental practices. Benefits packages also include the development of forest-related activities such as the growing of dragon fruit and vanilla, ecotourism, and encouraging the use of vegetable gardens to ensure food security.

Moreover, the AMPF Head Office show an increased leadership in all the processes that have been implemented, and local residents acknowledge SERNANP as the authority within the Protected Area. Therefore, it was important to strengthen the capacities of the technical staff and forest rangers to improve communication with local people. Sixteen training sessions have been delivered in this period. The topics of the sessions dealt with communication for environmental peace, the use of the GIS and the use of drones that have contributed to make surveillance activities more effective. As a result, a new checkpoint and surveillance post has been built in the Flor de Selva sector which is the farthest area from the AMPF.

It is to be noticed that public and private institutions, interested in developing different projects within the AMPF, request the Head Office for compatible technical opinion so as not to put at risk the conservation objects of the Protected Area. A total of 57 applications have been processed, 90% of which received a favorable opinion and their implementation will contribute to the development of communities.

The Management Committee, formed by public and private institutions as well as the organized civil society, has shown a greater interest in the AMPF regarding the governance of the protected area. Currently, this platform is made up of 113 institutions whose participation in the process of updating the Master Plan has been very important.

The Regional Government and the local governments of Alto Mayo are interested in developing mechanisms that contribute to the sustainability of the AMPF. The Regional Government through the Department of Agriculture wants to replicate the success of the project in managing coffee growing in other areas. It has also contributed –through the OPIPS- to approach companies that commercialize biodiversity products such as dragon fruit. Meanwhile, the local Government of Rioja has increased the coordination with the Head Office and implemented actions to carry out sustainable projects such as the ones in the area of tourism. In addition to this, the Alto Mayo association is being boosted, taking the protection of the AMPF as a strategic point.

Therefore, the project strategy is to provide knowledge and strengthen capacities in the Head Office team so that the environmental, productive and social processes have sustainability over the time. The main objective of the annual training plans that are implemented is to have a solid team in the structure of the AMPF Head Office.

All this is complemented with the strategy of supporting projects of the subscribers of conservation agreements. This also includes the work done by the COOPBAM in order to leverage public and private financial resources to consolidate these initiatives.

Finally, the ecosystem functionality of the AMPF, including its high importance as a conservation unit, is guaranteed by the more than 2,271 hectares of forest that were saved from deforestation and generated carbon credits. All these achievements have been possible thanks to the effort of more of 90 professionals based in Rioja, Lima and the United States who firmly believe that the AMPF is a successful model of conservation and development.

2.1.2 Project Category and Activity Type

The Alto Mayo Conservation Initiative (AMCI) promotes activities to reduce emissions from deforestation in the Alto Mayo Protected Forest (AMPF) of the Peruvian Amazon. Therefore, it falls within the *Avoided Unplanned Deforestation and/or Degradation (AUDD)* VCS sectorial scope 14: AFOLU (Agriculture, Forestry and Other Land Uses) category. The AMPF meets the most current definition of frontier configuration, as deforestation occurs in fronts along the routes and rivers in the region that provide access to the forest. The project is not a grouped project

2.1.3 Project Proponent(s)

The project proponent is Conservation International Foundation (CI) through its Peru office (CI-Peru). CI-Peru is responsible for the implementation of the conservation strategies and has overall control and responsibility of the project. As per the Administration Contract, CI-Peru co-manages the AMPF together

with the local Head Office of the National Service of Natural Protected Areas by the State (SERNANP) (Sup.Inf_nprt_02a-e). CI-Peru has the right of use of any greenhouse gas (GHG) emission reductions and/or removals arising during the contract period in connection with its performance of environmental services that generate GHG emission reductions and/or removals in the AMPF. The regulation (RP. 26-2014-SERNANP), provides a specific legal framework to obtain the right from SERNANP to commercialize carbon certificates generated within a natural protected area. Evidences of the procedures followed by CI-Peru to obtain this right in accordance with the resolution enacted by SERNANP were made available to the verifiers (Sup.Inf_MIR_02).

Organization name	Conservation International - Peru
Contact person	Luis Espinel
Title	Vice President, Conservation International – Peru
Address	Av. Antonio Miroquesada 425, Oficina 513-Magdalena del Mar, Lima, Peru
Telephone	+51 (1) 610 0300
Email	lespinel@conservation.org



2.1.4 Other Entities Involved in the Project

The complexity of the project requires a multidisciplinary team, with expertise and skills in AFOLU/REDD project design and implementation; carbon accounting and reporting; spatial analysis and remote sensing; surveillance and monitoring; agroforestry and agronomy; law and public policy; communication; economy; social affairs, conservation, and project management. In order to fulfill these expertise and skills, Conservation International developed partnership with several entities, as listed below:

Servicio Nacional de Áreas Naturales Protegidas por el Estado (SERNANP)

The National Service for Natural Protected Areas Protected by the State (SERNANP) is the government agency responsible for establishing the technical and administrative criteria for the creation and protection of National Protected Areas in Peru. It manages Peru's National System of Natural Protected Areas (SINANPE, or *Sistema Nacional de Áreas Nacionales Protegidas por el Estado*) of which the AMPF is part of. SERNANP has a diverse array of conservation professionals with a wide range of areas of expertise that together make up the basis from which it manages the vast expanse of protected areas at the national level.

SERNANP participates in the project through the AMPF Head Office (*Jefatura*) which is its decentralized branch in charge of managing and protecting the AMPF in the field in accordance with an approved Master Plan. The AMPF Head Office is responsible for signing and monitoring Conservation Agreements with the local population and is the ultimate authority within the AMPF.

SERNANP also supports the AMCI through its Head Office in Lima. For this project, the Head Office has been particularly important for establishing the guidelines and legal framework for implementing Conservation Agreements within a Protected Area. It has also signed an Administration Agreement with CI-Peru which transfers the legal rights to CI to co-manage the area together with the AMPF Head Office

through an Administration Contract. SERNANP is also interested institutionally in the possibility of the AMCI project becoming a model for financing the long-term management of a natural protected area (NPA) through the valuation of its environmental services.

Organization name	Servicio Nacional de Áreas Naturales Protegidas por el Estado (SERNANP)
Role in the project	Protected Area Management
Contact person	Pedro Gamboa
Title	Head of SERNANP
Address	Calle Diecisiete Nro. 355, Urb. El Palomar, San Isidro, Lima
Telephone	+51 1 717 7529
Email	pgamboa@sernanp.gob.pe



Asociación Ecosistemas Andinos (ECOAN)

The Association for Andean Ecosystems (ECOAN) is a Peruvian NGO with more than ten years of experience in implementing conservation projects and conducting research on flora and endangered bird species in Peru. In addition, ECOAN operates ecotourism initiatives and implements community development projects. These projects are located in six regions across Peru, several of which focus on sustainable forestry and forest conservation initiatives. ECOAN manages the Lechucita Bigotona biological station in the buffer zone of the AMPF and has ample experience working with communities living in and around its boundaries. Supported by the AMCI field staff and the AMPF Head Office, it will be responsible for working directly with local settlers to design and implement Conservation Agreements in the field. Since 2016, ECOAN provides support for the implementation of conservation agreements strategies, social management, communications and control and surveillance carried out within the framework of the Administration Contract with between CI Peru and SERNANP.

Organization name	Asociación Ecosistemas Andinos (ECOAN)
Role in the project	Conservation Agreement implementation
Contact person	Constantino Auca Chutas
Title	President
Address	Pasaje Los Pino D-1-B; Urb. La Florida, Wanchaq, Cusco
Telephone	+51 8 422 7988
Email	caucca@ecoanperu.org



Cooperativa Multiservicios Bosques del Alto Mayo Limitada (COOPBAM)

Created in late 2014, the COOPBAM is the AMPF subscriber cooperative. The COOPBAM is the entity responsible of channeling the marketing of coffee produced under conservation agreements. It is

considered a one of a kind cooperative since their partners are in alliance with the SERNANP to which they request the approval of their activities, such as the processes to obtain the organic and fair-trade certifications and the marketing of their products.

Organization name	Cooperativa Multiservicios Bosques del Alto Mayo Limitada (COOPBAM)
Role in the project	Responsible for channeling the marketing of coffee produced and conservation agreement implementation
Contact person	Idelso Fernández Quevedo
Title	General Manager
Address	Jr. Libertad 1196. Rioja. San Martín
Telephone	+51 982 688 360
Email	coopbamaltomayo@gmail.com



Additional stakeholders

The **AMPF management committee** was formally recognized in 2005 through Departmental Resolution N° 007-2005-INRENA-IANP, and since that date some modifications have occurred to guarantee the participation of local stakeholders in the management of the protected area. It currently consists of 113 representatives (54 additional representatives since 2012) from local governments and population centers, regional government, public and private sector institutions, and other organizations with an interest in the management of the Protected Area.

In the last two years the profile of the Management Committee was adapted to better represent the social complexity of the AMPF and to support institutional governance. The new advisors and structure have resulted in a stronger and more active Committee, with better engagement with the national authorities and congressmen. Since July 2019, the presidency of the Management Committee is led by Mrs. María Celmira Bustamante Torres, who in turn belongs to *Asociación de Desarrollo y Turismo Unidos por Palestina* (United for Palestine Development and Tourism Association), a local organization that is a beneficiary of the project. Among others, the major contributions of the new Management Committee to the AMPF management are:

- Establishment of dialogue opportunities with key political leaders in Alto Mayo and local authorities, contributing significantly to the awareness and positioning of the AMPF regarding their rights and obligations.
- Articulation with the legislative power and the Ministry of the Interior to support the prevention of environmental conflicts in the Alto Mayo Protection Forest.
- Leadership on community engagement process, including with key *rondas campesinas* leaders (through individual meetings and participation at their Regional, Provincial and District Assemblies).
- Frequent and active participation in the process of updating the Master Plan that facilitates the identification of strategies to be implemented to further improve the management of the Alto Mayo Protected Forest.

- Active participation in the Monitoring Committee of the Administration Contract, under which the scope of the contract is assessed, and new modalities are proposed to better achieve its objectives and the overall management of the AMPF.

The project recognizes that **individual settlers** that sign Conservation Agreements with the AMPF Head Office also represent key stakeholders in the AMCI initiative. Currently 1,096 Conservation Agreements have been signed with individual settlers.

As described above, the size and complexity of the project requires collaboration among a broad range of partners and local actors with different roles and responsibilities within the project. Figure 1 illustrates the institutional structure of the AMCI REDD project identifying the Project Proponent, its main partners, and the key stakeholders involved. Note that as the ultimate authority responsible for the management of NPAs in Peru, SERNANP and the AMPF Park Service are identified as both a Project Participant and a key Project Stakeholder.

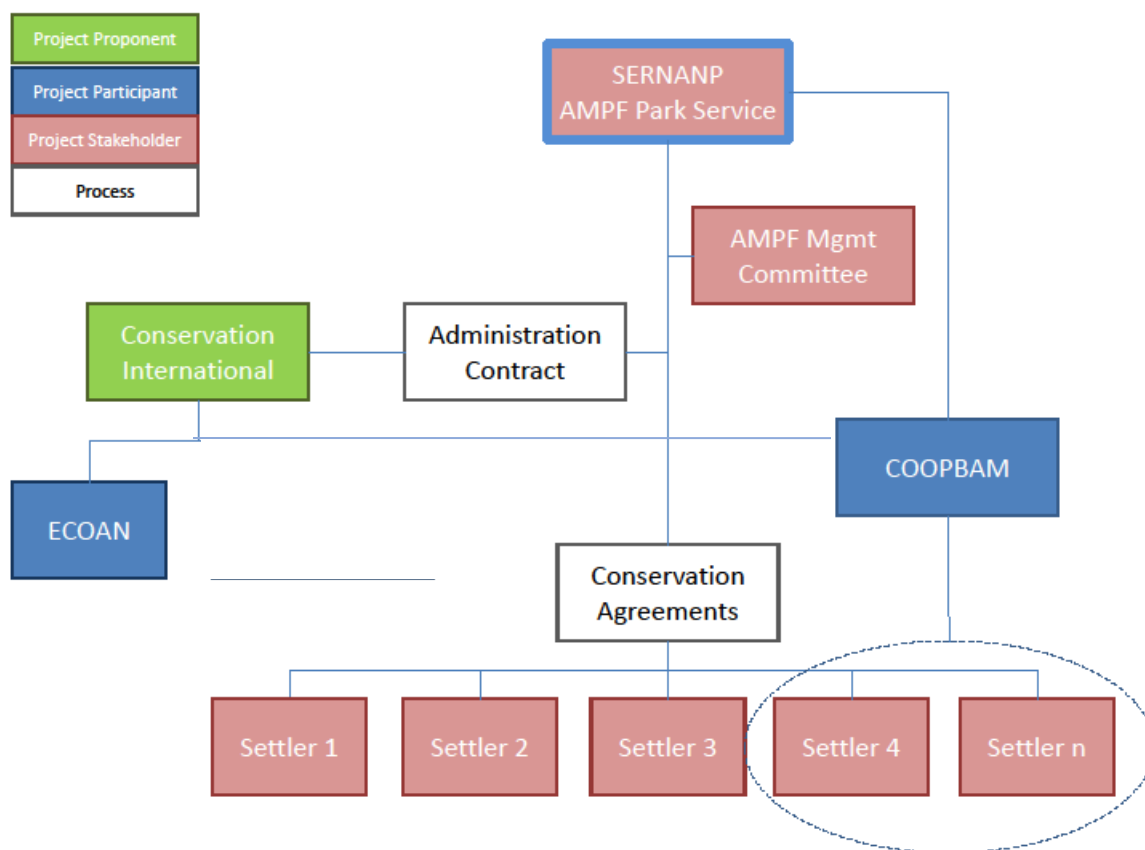


Figure 1 - Institutional Structure of the Alto Mayo project

For a detailed description of the experience of the management team, please refer to the supportive information (Sup.Inf_nprt_01).

2.1.5 Project Start Date (G3.4)

The start date of the project was June 15, 2008. This monitoring period started on June 15, 2018 and ended on June 14, 2020

2.1.6 Project Crediting Period (G3.4)

The start and end date of the project crediting period are, respectively: June 15, 2008 and June 14, 2028, for a total of 20 years. The project crediting is subject to renewals. Project lifetime coincides with the dates of the project crediting period.

2.1.7 Project Location (G3.3)

The project area corresponds to the Alto Mayo Protected Forest (AMPF), an area of 182,000 ha in the northern Peruvian Amazon situated in the department of San Martin, between coordinates 5° 23' 21" S, and 77° 43' 18" W upper left corner and 6° 10' 56" S and 77° 12' 17" W lower right corner. While the AMPF comprises 182,000 ha of land, the VCS defines the project area as the forested area within the AMPF at the project start date, or 153,929 ha of forest.

The leakage belt, as described in detail in Section 2.3 of VCS PD, was estimated as the most probable areas where activities carried out by individuals and communities affected by the project could be displaced to. The leakage belt has a total area of 47,428 ha, and it will be monitored as described in the Section 4 of VCS PD.

The CCBS' project zone includes the communities adjacent to the project that has a direct influence of forest resources of the AMPF and could potentially be affected by the REDD+ project. The project has developed strategies to integrate them into the conservation initiatives, and provide benefits, while minimizing the pressure on the forest, this includes but not limited to establishment of conservation agreements, environmental education and participative management.

Although is not part of the VCS or CCBS project boundaries, it is important to include the AMPF buffer zone, which area is 247,656 ha and its boundaries are delineated according to the master plan, more specifically as: the north and west by the boundaries of the watersheds that originate in the AMPF (Sup.Inf_nprt_12), in the east it is delineated by the Fernando Belaunde Terry highway, the main access road to the Upper Mayo River Basin. Figure 2 illustrates the location of the project area and zone. There are no changes in the project boundaries since validation. GIS files of project boundaries were made available to VV body.

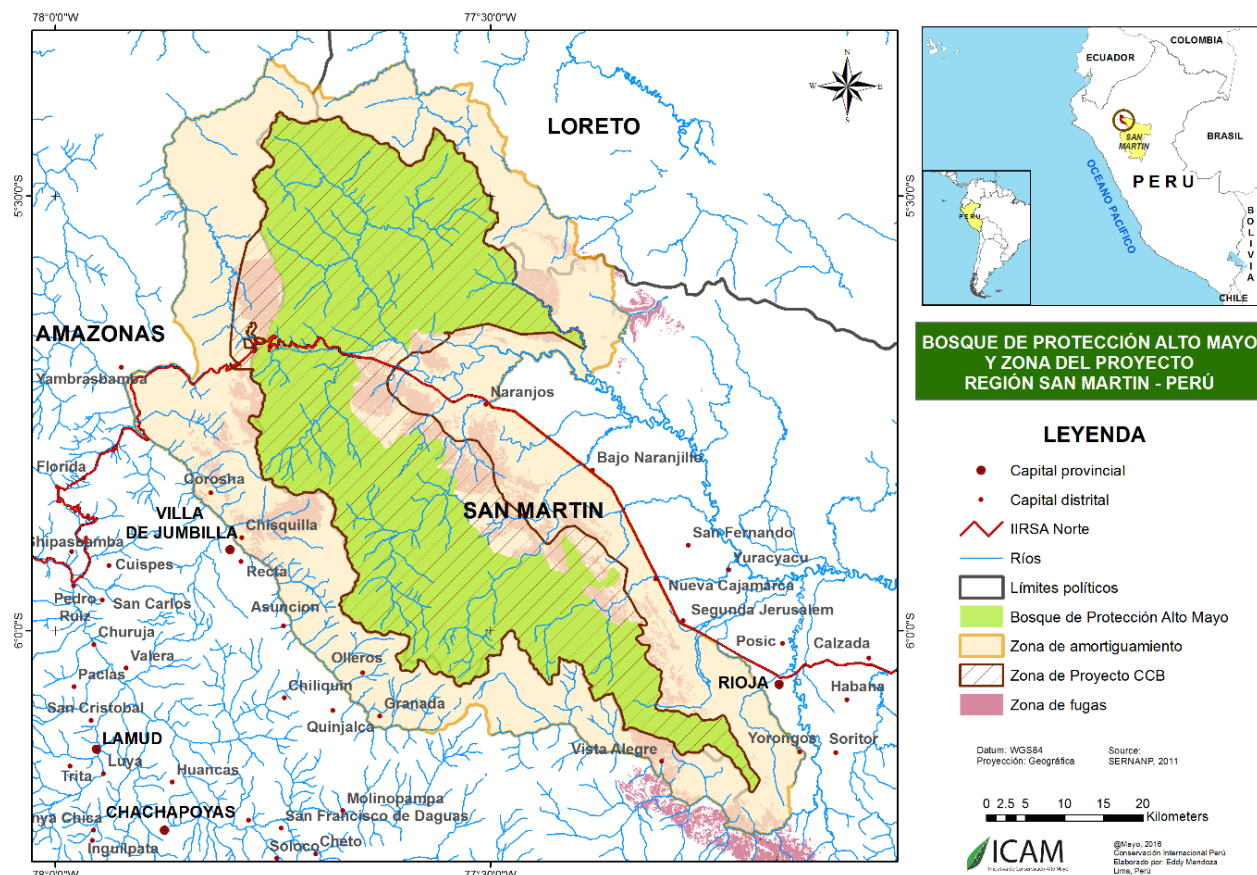


Figure 2- Location of the Alto Mayo Protected Forest and project boundaries

2.1.8 Title and Reference of Methodology

The project applies the “Methodology for Avoided Unplanned Deforestation” (VM0015, Version 1.0) approved by the VCS on July 12, 2011. The project was validated using CCBS second version.

2.1.9 Other Programs (CL1.5)

Peru does not currently have any binding commitments and/or obligations to reduce GHG emissions from the Land Use, Land Use Change and Forestry (LULUCF) sector.

The project has not and does not intend to generate any other form of GHG-related environmental credit for GHG emissions reductions or removals claimed under the VCS Program. The only GHG-related environmental credit generated by the project will be under the VCS. Similarly, the project has not and does not seek to receive project another form of social or environmental credit, including renewable energy certificates, besides CCBS. Farmers that are also subscribers of conservation agreement might aim for organic and, or fair-trade certification, however those certification does not generate credits.

The project has not been registered and is not seeking registration under any other GHG program.

2.1.10 Sustainable Development

Although the project aims to improve the human well-being of local communities and conserve the natural resources of Alto Mayo, and therefore promote a sustainable and harmonized development for the region, the project is not part of any nationally stated sustainable development priority. In addition, the project does not report its impact to any national accounting system on sustainable development. As a co-manager of a protected area, CI-Peru has the commitment to report the achievements according to the technical and financial proposals (Sup.Inf_nprt_02a-e, 04a, 04b) at yearly basis, however the objectives are established between SERNANP and the AMPF based on local circumstances.

2.2 Project Implementation Status

2.2.1 Implementation Schedule (G3.4)

The project was validated and underwent its first verification under the VCS and CCBS standards in 2012. The second, third, and fourth verifications were finalized in 2015, 2016, and 2018 respectively. The project aims to have verifications every two years and will update the baseline after 2020. The rule 3.2.7. of VCS Standards 4.0 requires the reassessment of the baseline every 10 years, however VCS has granted an exemption of this rule (Sup.Inf_MIR_18). The key milestones are organized by project strategies and the implementation schedule is shown in Table 1 (Sup.Inf_MIR_14a+b).

Table 1 - Project implementation schedule 2008-2028

Strategy / Activity	Year																				
	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028
Strategy 1: Improve governance and enforcement capabilities of the AMPF local Head Office																					
Strengthening operational capacity of AMPF local Head Office																					
Control and surveillance	X	X	X	X		X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Hiring additional staff				X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Capacity building		X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Communication			X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Donation of field equipment , computers and vehicle			X	X					X	X	X	X		X			X			X	
Construction of infrastructure			X		X	X	X	X	X	X	X	X									
Strengthening the Management Committee																					
Support to assemblies and meetings		X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Capacity building			X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Strengthening operational management			X	X	X	X	X	X	X	X	X	X	X	X	X						
Administration Contract																					
Preparation of technical proposal					X					X					X					X	
Signature (renewal) of Administration Contract					X					X					X					X	

Strategy / Activity	Year																				
	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028
Implementation of Administration Contract					X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Master Plan																					
General update											X	X	X			X	X				X
Zoning update											X	X	X			X	X				X
Strategy 2 : Promote sustainable use practices aligned with AMPF objectives																					
Conservation Agreements																					
Guideline development			X	X																	
Development, implementation and monitoring	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Renewal					X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Restoration of degraded ecosystems																					
Agroforestry systems				X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
SAF						X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Restoration of grassland with SAF						X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Reforestation of critical areas					X	X	X	X	X	X											
Strategy 3: Establishment of long-term funding mechanism to ensure the sustainability of AMPF management																					
Carbon (REDD)																					
Forest inventories , preparation of PDDs	X	X	X	X	X																
Validation					X																
Registry					X																
Monitoring (VCS & CCBS)					X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Verification					X		X		X		X		X	X			X			X	
Baseline revision														X							X
Other ecosystem services																					
Ecosystem services mapping				X	X																
PSH pilot project Feasibility analysis					X	X	X	X	X												
Implementation of PSH in one sub watershed									X	X											
Strategy 4: Communications and public awareness strategy																					
Communications																					
Institutional positioning AMPF			X	X	X																
Coordination of AMPF with local population		X	X	X	X	X	X		X		X		X		X		X		X		X
Environmental campaigns					X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
School communicators				X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Network of environmental journalists				X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Strategy 5 : Integrate AMPF in regional policies and processes																					
Recognition of AMPF as a model of developing health and sustainable economies																					
Promotion of production models promoted by the project				X	X	X	X	X	X	X	x	X									
Promotion of AMPF as development model in Alto Mayo basin					X	X	X	X	X	X	X	X									
Implement regional policies in favor of AMPF							X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Strategy 6. Implementing AMPF social management strategy																					
Development of conflict						X	X														

Strategy / Activity	Year																											
	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028							
management protocol																												
Development, implementation and monitoring of mgmt. conflict						X	X	X	X	X	X	X	X															
Protocol community engagement						X	X																					
Design, implementation & monitoring of community engagement protocol						X	X	X	X	X	X	X	X															
Advocacy & contribution to implementation of Aguas Verdes functional hub							X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Technical support to the development of stakeholder-based projects							X	X	X	X	X	X	X	X	X	X	X											
Management activities for the development of the BPAM buffer zone							X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X

2.2.2 Methodology Deviations

In accordance with the rule 3.2.7. of VCS Standard 4.0, VM0015 states “...that the baseline projections must be revisited every 10 years and adjusted, as necessary, based on land-use and land-cover changes observed during the past period and changes at the level of agents, driver and underlying causes of deforestation...” The project should reassess and validate the baseline in 2018, however the Government of Peru is developing the rules to nest the projects into the national reference emission level and has granted an extension to Alto Mayo until 2020 (Sup.Inf_MIR_19). Under these circumstances the project requested an exemption of the rule 3.2.7. to Verra which was granted as per Sup.Info_MIR_18.

2.2.3 Minor Changes to Project Description (Rules 3.5.6)

The project uses the adaptive management principles to improve the results and effectiveness of project activities. Although no changes in the project description has occurred in this monitoring period, additional activities and strategies were developed and implemented (e.g. social and communication strategies, or drone images for reforestation mapping)

2.2.4 Project Description Deviations (Rules 3.5.7 – 3.5.10)

Few deviations from the project description (PDD) have occurred in the first monitoring period, which were presented in the previous verification and are repeated below. For this monitoring period, the project has extended the baseline to 2020 using the same process, methods and parameters as described in the PDD, however some VM Tables 9 to 34 have two additional years (2019 and 2020), repeated below for reference. These deviations do not include any change in the project area, project proponent, significant

changes in project activities, or expected impacts of the project. GIS files and spreadsheets were presented to the VVB.

VM Table 9.a. Annual areas of baseline deforestation in the reference region

Project year t	Stratum i in the reference region $ABSLRR_{i,t}$ ha
2009	4,735
2010	4,735
2011	4,735
2012	4,735
2013	4,735
2014	4,735
2015	4,735
2016	4,735
2017	4,735
2018	4,735
2019	4,735
2020	4,735

VM Table 9.b. Annual areas of baseline deforestation in the project area

Project year t	Stratum i of the reference region in the project area $ABSLPA_{i,t}$ ha	Total	
		annual $ABSLPA_t$ ha	cumulative $ABSLPA$ ha
2009	2,478	2,478	2,478
2010	2,368	2,368	4,846
2011	2,220	2,220	7,066
2012	2,155	2,155	9,221
2013	2,149	2,149	11,369
2014	1,966	1,966	13,335
2015	1,903	1,903	15,239
2016	1,917	1,917	17,156
2017	1,884	1,884	19,040
2018	1,802	1,802	20,842
2019	1,640	1,640	22,482

2020	1,673	1,673	24,155
------	-------	-------	--------

VM Table 9.c. Annual areas of baseline deforestation in the project area

Project year t	Stratum i of the reference region in the leakage belt 1 $ABSLK_{i,t}$ ha	Total	
		annual $ABSLK_t$ ha	cumulative $ABSLK$ ha
2009	1,318	1,318	1,318
2010	1,332	1,332	2,650
2011	1,348	1,348	3,997
2012	1,371	1,371	5,368
2013	1,332	1,332	6,700
2014	1,514	1,514	8,214
2015	1,574	1,574	9,788
2016	1,487	1,487	11,275
2017	1,490	1,490	12,765
2018	1,516	1,516	14,280
2019	1,607	1,607	15,887
2020	1,557	1,557	17,444

VM Table 11. Annual areas deforested per forest class icl within the project area in the baseline case (baseline activity data per forest class)

Area deforested per forest class icl within the project area				Total baseline deforestation in the project area	
$IDicl >$ Name >	1 pre-montane forest	2 cloud forest	3 dwarf forest	$ABSLPA_t$ annual	$ABSLPA$ cumulative
Project year t	ha	ha	ha	ha	ha
2009	21	2,456	0	2,478	2,478
2010	9	2,359	0	2,368	4,846
2011	3	2,217	0	2,220	7,066
2012	1	2,154	0	2,155	9,221
2013	2	2,147	0	2,149	11,369
2014	2	1,964	0	1,966	13,335
2015	1	1,902	0	1,903	15,239
2016	1	1,917	0	1,917	17,156
2017	0	1,884	0	1,884	19,040

2018	0	1,801	0	1,802	20,842
2019	-	1,639	2	1,640	22,482
2020	-	1,669	4	1,673	24,155

VM Table 12.a. Annual areas of post-deforestation classes fcl within the reference region in the baseline case

Area established after deforestation per class <i>fcl</i> within the reference region		Total baseline deforestation in the reference region	
Name >	1	ABSLRR _t annual ha	ABSLRR cumulative ha
	non-forest		
Project year <i>t</i>	ha	ha	ha
2009	4,735	4,735	4,735
2010	4,735	4,735	9,470
2011	4,735	4,735	14,205
2012	4,735	4,735	18,940
2013	4,735	4,735	23,675
2014	4,735	4,735	28,410
2015	4,735	4,735	33,145
2016	4,735	4,735	37,880
2017	4,735	4,735	42,615
2018	4,735	4,735	47,350
2019	4,735	4,735	52,085
2020	4,735	4,735	56,820

VM Table 12.b. Annual areas of post-deforestation classes fcl within the project area in the baseline case

Area established after deforestation per class <i>fcl</i> within the project area		Total baseline deforestation in the project area	
Name >	1	ABSLRR _t annual ha	ABSLRR cumulative ha
	non-forest		
Project year <i>t</i>	ha	ha	ha
2009	2,478	2,478	2,478
2010	2,368	2,368	4,846
2011	2,220	2,220	7,066
2012	2,155	2,155	9,221
2013	2,149	2,149	11,369
2014	1,966	1,966	13,335

2015	1,903	1,903	15,239
2016	1,917	1,917	17,156
2017	1,884	1,884	19,040
2018	1,802	1,802	20,842
2019	1,640	1,640	22,482
2020	1,673	1,673	24,155

VM Table 12.c. Annual areas of post-deforestation classes fcl within the leakage belt in the baseline case

Area established after deforestation per class <i>fcl</i> within the leakage belt		Total baseline deforestation in the leakage belt	
Name > <i>ID_{cl}</i>	1	<i>ABSLRR_t</i> annual ha	<i>ABSLRR</i> cumulative ha
	non-forest		
Project year <i>t</i>	ha	ha	ha
2009	1,318	1,318	1,318
2010	1,332	1,332	2,650
2011	1,348	1,348	3,997
2012	1,371	1,371	5,368
2013	1,332	1,332	6,700
2014	1,514	1,514	8,214
2015	1,574	1,574	9,788
2016	1,487	1,487	11,275
2017	1,490	1,490	12,765
2018	1,516	1,516	14,280
2019	1,607	1,607	15,887
2020	1,557	1,557	17,444

VM Table 15.a. Baseline carbon stock change in pre-deforestation (forest) classes

Project year <i>t</i>	Carbon stock changes in initial (pre-deforestation) forest classes in the project area						Total carbon stock change in initial forest classes	
	<i>ID_{cl}</i> = pre- montane	<i>ID_{cl}</i> = cloud	<i>ID_{cl}</i> = dwarf				annual	cumulative
	<i>ABSLPA_{icl,t}</i> ha	<i>Ctot_{icl,t}</i> tCO ₂ -e ha ⁻¹	<i>ABSLPA_{icl,t}</i> ha	<i>Ctot_{icl,t}</i> tCO ₂ -e ha ⁻¹	<i>ABSLPA_{icl,t}</i> ha	<i>Ctot_{icl,t}</i> tCO ₂ -e ha ⁻¹	<i>ΔCBSLPA_{i,t}</i> tCO ₂ -e	<i>ΔCBSLPA_i</i> tCO ₂ -e
2009	21	399	2,456	520	0	88	1,284,780	1,284,780
2010	9	399	2,359	520	0	88	1,229,353	2,514,133

2011	3	399	2,217	520	0	88	1,153,079	3,667,211
2012	1	399	2,154	520	0	88	1,119,680	4,786,892
2013	2	399	2,147	520	0	88	1,116,212	5,903,104
2014	2	399	1,964	520	0	88	1,021,238	6,924,341
2015	1	399	1,902	520	0	88	988,849	7,913,190
2016	1	399	1,917	520	0	88	996,173	8,909,363
2017	0	399	1,884	520	0	88	979,018	9,888,381
2018	0	399	1,801	520	0	88	936,035	10,824,417
2019	0	399	1,639	520	2	88	851,549	11,675,966
2020	0	399	1,669	520	4	88	867,525	12,543,490

Table 15.b. Baseline carbon stock change in pos-deforestation (non-forest) classes

Project year t	Carbon stock changes in final (post-deforestation) non-forest classes in the project area		Total carbon stock change in final non-forest classes	
	$ID_{fd} = 1$		annual	cumulative
	$ABSLPA_{fd,t}$ ha	$C_{tot_{fd,t}}$ tCO ₂ -e ha ⁻¹	$\Delta C_{BSLPA}_{fd,t}$ tCO ₂ -e	ΔC_{BSLPA}_{fd} tCO ₂ -e
2009	2,478	93	231,144	231,144
2010	2,368	93	220,917	452,062
2011	2,220	93	207,105	659,167
2012	2,155	93	201,060	860,227
2013	2,149	93	200,447	1,060,674
2014	1,966	93	183,402	1,244,076
2015	1,903	93	177,575	1,421,651
2016	1,917	93	178,877	1,600,528
2017	1,884	93	175,787	1,776,315
2018	1,802	93	168,104	1,944,419
2019	1,640	93	153,034	2,097,452
2020	1,673	93	156,055	2,253,508

Table 15.c. Total net baseline carbon stock change in the project area

Project year t	Total carbon stock change in initial forest classes		Total carbon stock change in final non-forest classes		Total baseline carbon stock change in the project area	
	annual	cumulative	annual	cumulative	annual	cumulative
	$\Delta C_{BSLPA}_{fi,t}$	ΔC_{BSLPA}_{fi}	$\Delta C_{BSLPA}_{fd,t}$	ΔC_{BSLPA}_{fd}	ΔC_{BSLPA}_t	ΔC_{BSLPA}

	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	1,284,780	1,284,780	231,144	231,144	1,053,635	1,053,635
2010	1,229,353	2,514,133	220,917	452,062	1,008,436	2,062,071
2011	1,153,079	3,667,211	207,105	659,167	945,973	3,008,045
2012	1,119,680	4,786,892	201,060	860,227	918,620	3,926,665
2013	1,116,212	5,903,104	200,447	1,060,674	915,765	4,842,430
2014	1,021,238	6,924,341	183,402	1,244,076	837,835	5,680,265
2015	988,849	7,913,190	177,575	1,421,651	811,273	6,491,539
2016	996,173	8,909,363	178,877	1,600,528	817,296	7,308,835
2017	979,018	9,888,381	175,787	1,776,315	803,232	8,112,067
2018	936,035	10,824,417	168,104	1,944,419	767,931	8,879,998
2019	851,549	11,675,966	153,034	2,097,452	698,516	9,578,513
2020	867,525	12,543,490	156,055	2,253,508	711,469	10,289,982

VM Table 22. Ex ante estimated net carbon stock change in the project area under the project scenario

Project year <i>t</i>	Total carbon stock decrease due to planned activities		Total carbon stock increase due to planned activities		Total carbon stock decrease due to unavoided unplanned deforestation		Total carbon stock change in the project case	
	annual	cumulative	annual	cumulative	annual	cumulative	annual	cumulative
	$\Delta CPAdPA_t$	$\Delta CPAdPA$	$\Delta CPAiPA_t$	$\Delta CPAiPA$	$\Delta CUDdPA_t$	$\Delta CUDdPA$	$\Delta CPSPA_t$	$\Delta CPSPA$
	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	0	0	0	0	526,818	526,818	(526,818)	(526,818)
2010	0	0	0	0	504,218	1,031,036	(504,218)	(1,031,036)
2011	0	0	0	0	472,987	1,504,022	(472,987)	(1,504,022)
2012	0	0	0	0	413,379	1,917,401	(413,379)	(1,917,401)
2013	0	0	0	0	412,094	2,329,496	(412,094)	(2,329,496)
2014	0	0	0	0	335,134	2,664,630	(335,134)	(2,664,630)
2015	0	0	0	0	283,946	2,948,575	(283,946)	(2,948,575)
2016	0	0	0	0	245,189	3,193,764	(245,189)	(3,193,764)
2017	0	0	0	0	160,646	3,354,411	(160,646)	(3,354,411)
2018	0	0	0	0	76,793	3,431,204	(76,793)	(3,431,204)
2019	0	0	0	0	69,852	3,501,055	(69,852)	(3,501,055)
2020	0	0	0	0	71,147	3,572,202	(71,147)	(3,572,202)

VM Table 24. Total ex ante estimated actual net carbon stock changes and emissions of non-CO₂ gasses in the project area

Project year <i>t</i>	Total <i>ex ante</i> carbon stock decrease due to planned activities		Total <i>ex ante</i> carbon stock increase due to planned activities		Total <i>ex ante</i> carbon stock decrease due to unavoided unplanned deforestation		Total <i>ex ante</i> net carbon stock change		Total <i>ex ante</i> estimated actual non-CO ₂ emissions from forest fires in the project area	
	annual	cumulative	annual	cumulative	annual	cumulative	annual	cumulative	annual	cumulative
	ΔCPA_{dPA_t}	ΔCPA_{dPA}	ΔCPA_{iPA_t}	ΔCPA_{iPA}	ΔCUD_{dPA_t}	ΔCUD_{dPA}	ΔCPS_{PA_t}	ΔCPS_{PA}	$EBBPS_{PA_t}$	$EBBPS_{PA}$
	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	0	0	0	0	526,818	526,818	(526,818)	(526,818)	0	0
2010	0	0	0	0	504,218	1,031,036	(504,218)	(1,031,036)	0	0
2011	0	0	0	0	472,987	1,504,022	(472,987)	(1,504,022)	0	0
2012	0	0	0	0	413,379	1,917,401	(413,379)	(1,917,401)	0	0
2013	0	0	0	0	412,094	2,329,496	(412,094)	(2,329,496)	0	0
2014	0	0	0	0	335,134	2,664,630	(335,134)	(2,664,630)	0	0
2015	0	0	0	0	283,946	2,948,575	(283,946)	(2,948,575)	0	0
2016	0	0	0	0	245,189	3,193,764	(245,189)	(3,193,764)	0	0
2017	0	0	0	0	160,646	3,354,411	(160,646)	(3,354,411)	0	0
2018	0	0	0	0	76,793	3,431,204	(76,793)	(3,431,204)	0	0
2019	0	0	0	0	69,852	3,501,055	(69,852)	(3,501,055)	0	0
2020	0	0	0	0	71,147	3,572,202	(71,147)	(3,572,202)	0	0

VM Table 25.c. Ex ante estimated net carbon stock change and non-CO₂ emissions in leakage management areas

Project year <i>t</i>	Total carbon stock change and non-CO ₂ emissions in leakage management areas in the baseline case		Total carbon stock changes and non-CO ₂ emissions in leakage management areas in the project case		Net carbon stock change due to leakage prevention measures	
	annual	cumulative	annual	cumulative	annual	cumulative
	$\Delta CBSLLK_t$	$\Delta CBSLLK$	$\Delta CPSLK_t$	$\Delta CPSLK$	$\Delta CLPMLK_t$	$\Delta CLPMLK$
	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	0	0	0	0	0	0
2010	0	0	0	0	0	0
2011	0	0	0	0	0	0
2012	0	0	0	0	0	0
2013	0	0	0	0	0	0
2014	0	0	0	0	0	0
2015	0	0	0	0	0	0
2016	0	0	0	0	0	0
2017	0	0	0	0	0	0

2018	0	0	0	0	0	0
2019	0	0	0	0	0	0
2020	0	0	0	0	0	0

VM Table 28. Ex ante estimated total emissions above the baseline from leakage prevention activities

Project year t	Carbon stock decrease and non-CO2 emissions due to leakage prevention measures		Total <i>ex ante</i> GHG emissions from increased grazing activities		Total <i>ex ante</i> increase in GHG emissions due to leakage prevention measures	
	annual $\Delta CLPMLK_t$	cumulative $\Delta CLPMLK$	annual $EgLK_t$	cumulative $EgLK_t$	annual $ELPMLK_t$	cumulative $ELPMLK$
	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	0	0	0	0	0	0
2010	0	0	0	0	0	0
2011	0	0	0	0	0	0
2012	0	0	0	0	0	0
2013	0	0	0	0	0	0
2014	0	0	0	0	0	0
2015	0	0	0	0	0	0
2016	0	0	0	0	0	0
2017	0	0	0	0	0	0
2018	0	0	0	0	0	0
2019	0	0	0	0	0	0
2020	0	0	0	0	0	0

Table 29.a. Baseline carbon stock change in initial (pre-deforestation) forest classes in the leakage belt

Project year t	Carbon stock changes in initial (pre-deforestation) forest classes in the leakage belt						Total carbon stock change in initial forest classes	
	pre- montane		ID_{icl} = cloud		ID_{icl} = dwarf		annual	cumulative
	$ABSLK_{icl,t}$	$Ctot_{icl,t}$	$ABSLK_{icl,t}$	$Ctot_{icl,t}$	$ABSLK_{icl,t}$	$Ctot_{icl,t}$	$\Delta CBSLLK_t$	$\Delta CBSLLK_i$
	ha	tCO ₂ -e ha ⁻¹	ha	tCO ₂ -e ha ⁻¹	ha	tCO ₂ -e ha ⁻¹	tCO ₂ -e	tCO ₂ -e
2009	0	399	e	520	-	88	577,395	577,395
2010	0	399	1,088	520	-	88	565,423	1,142,818
2011	0	399	1,082	520	0	88	562,438	1,705,257
2012	0	399	1,203	520	1	88	625,337	2,330,594
2013	0	399	1,290	520	6	88	670,925	3,001,519
2014	0	399	1,281	520	11	88	666,661	3,668,180

2015	0	399	1,491	520	27	88	776,993	4,445,173
2016	0	399	1,596	520	41	88	833,109	5,278,282
2017	0	399	1,715	520	58	88	895,993	6,174,275
2018	0	399	1,700	520	63	88	888,768	7,063,043
2019	0	399	1,517	520	91	88	795,984	7,859,027
2020	0	399	1,459	520	98	88	766,673	8,625,700

Table 29.b. Baseline carbon stock change in final (post-deforestation) non-forest classes in the leakage belt

Project year t	Carbon stock changes in final (post-deforestation) non-forest classes on the leakage belt		Total carbon stock change in final non-forest classes	
	$ID_{fcl} = 1$		annual	cumulative
	$ABSLLK_{fcl,t}$	$Ctot_{fcl,t}$	$\Delta CBSLLK_f$	$\Delta CBSLLK_f$
	ha	tCO ₂ -e ha ⁻¹	tCO ₂ -e	tCO ₂ -e
2009	1,318	93	122,957	122,957
2010	1,332	93	124,241	247,198
2011	1,348	93	125,719	372,917
2012	1,371	93	127,894	500,811
2013	1,332	93	124,241	625,052
2014	1,514	93	141,261	766,313
2015	1,574	93	146,878	913,191
2016	1,487	93	138,708	1,051,900
2017	1,490	93	138,960	1,190,860
2018	1,516	93	141,387	1,332,247
2019	1,607	93	149,922	1,482,169
2020	1,557	93	145,258	1,627,426

Table 29.c. Total net baseline carbon stock change in the leakage belt

Project year t	Total carbon stock change in initial forest classes		Total carbon stock change in final non-forest classes		Total baseline carbon stock change	
	annual	cumulative	annual	cumulative	annual	cumulative
	$DCBSLLK_i$	$DCBSLLK_i$	$DCBSLLK_f$	$DCBSLLK_f$	$DCBSLLK_i$	$DCBSLLK_i$
	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	577,395	577,395	122,957	122,957	454,438	454,438
2010	565,423	1,142,818	124,241	247,198	441,182	895,620
2011	562,438	1,705,257	125,719	372,917	436,719	1,332,340

2012	625,337	2,330,594	127,894	500,811	497,443	1,829,783
2013	670,925	3,001,519	124,241	625,052	546,684	2,376,466
2014	666,661	3,668,180	141,261	766,313	525,400	2,901,866
2015	776,993	4,445,173	146,878	913,191	630,115	3,531,981
2016	833,109	5,278,282	138,708	1,051,900	694,401	4,226,382
2017	895,993	6,174,275	138,960	1,190,860	757,033	4,983,415
2018	888,768	7,063,043	141,387	1,332,247	747,381	5,730,797
2019	795,984	7,859,027	149,922	1,482,169	646,061	6,376,858
2020	766,673	8,625,700	145,258	1,627,426	621,416	6,998,274

VM Table 32. Ex ante estimated leakage due to activity displacement

Project year t	Total <i>ex ante</i> estimated decrease in carbon stocks due to displaced deforestation		Total <i>ex ante</i> estimated increase in GHG emissions due to displaced forest fires	
	annual	cumulative	annual	cumulative
	$\Delta CADLK_t$ tCO ₂ -e	$\Delta CADLK$ tCO ₂ -e	$EADLK_t$ tCO ₂ -e	$EADLK$ tCO ₂ -e
2009	(52,682)	(52,682)	0	0
2010	(50,422)	(103,104)	0	0
2011	(47,299)	(150,402)	0	0
2012	(36,745)	(187,147)	0	0
2013	(36,631)	(223,778)	0	0
2014	(25,135)	(248,913)	0	0
2015	(24,338)	(273,251)	0	0
2016	(16,346)	(289,597)	0	0
2017	(8,032)	(297,629)	0	0
2018	0	(297,629)	0	0
2019	0	(297,629)	0	0
2020	0	(297,629)	0	0

VM Table 33. Ex ante estimated total leakage

Project year t	Total <i>ex ante</i> decrease in carbon stocks due to displaced deforestation		Carbon stock decrease or non-CO ₂ emissions due to leakage prevention measures		Total net carbon stock change due to leakage		Total net increase in emissions due to leakage	
	annual	cumulative	annual	cumulative	annual	cumulative	annual	cumulative
	$\Delta CADLK_t$	$\Delta CADLK$	$\Delta CLPMLK_t$	$\Delta CLPMLK$	ΔCLK_t	ΔCLK	ELK_t	ELK

	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e	tCO ₂ -e
2009	(52,682)	(52,682)	0	0	(52,682)	(52,682)	0	0
2010	(50,422)	(103,104)	0	0	(50,422)	(103,104)	0	0
2011	(47,299)	(150,402)	0	0	(47,299)	(150,402)	0	0
2012	(36,745)	(187,147)	0	0	(36,745)	(187,147)	0	0
2013	(36,631)	(223,778)	0	0	(36,631)	(223,778)	0	0
2014	(25,135)	(248,913)	0	0	(25,135)	(248,913)	0	0
2015	(24,338)	(273,251)	0	0	(24,338)	(273,251)	0	0
2016	(16,346)	(289,597)	0	0	(16,346)	(289,597)	0	0
2017	(8,032)	(297,629)	0	0	(8,032)	(297,629)	0	0
2018	0	(297,629)	0	0	0	(297,629)	0	0
2019	0	(297,629)	0	0	0	(297,629)	0	0
2020	0	(297,629)	0	0	0	(297,629)	0	0

Table 34. Ex ante estimated net anthropogenic GHG emission reductions (DREDDt) and Voluntary Carbon Units (VCUt)*

Project year t	Baseline		Ex ante project		Ex ante leakage		Ex ante net anthropogenic GHG emission reductions		Ex ante VCUs tradable		Ex ante buffer credits	
	carbon stock changes		carbon stock changes		carbon stock changes							
	annual $\Delta CBSLPA_t$ tCO ₂ -e	cumulative $\Delta CBSLPA$ tCO ₂ -e	annual $\Delta CPSPA_t$ tCO ₂ -e	cumulative $\Delta CPSPA$ tCO ₂ -e	annual ΔCLK_t tCO ₂ -e	cumulative ΔCLK tCO ₂ -e	annual $\Delta REDD_t$ tCO ₂ -e	cumulative $\Delta REDD$ tCO ₂ -e	annual VCU_t tCO ₂ -e	cumulative VCU tCO ₂ -e	annual VBC_t tCO ₂ -e	cumulative VBC tCO ₂ -e
2009	1,053,635	1,053,635	(526,818)	(526,818)	(52,682)	(52,682)	474,136	474,136	421,454	421,454	52,682	52,682
2010	1,008,436	2,062,071	(504,218)	(1,031,036)	(50,422)	(103,104)	453,796	927,932	403,374	824,829	50,422	103,104
2011	945,973	3,008,045	(472,987)	(1,504,022)	(47,299)	(150,402)	425,688	1,353,620	378,389	1,203,218	47,299	150,402
2012	918,620	3,926,665	(413,379)	(1,917,401)	(36,745)	(187,147)	468,496	1,822,116	417,972	1,621,190	50,524	200,926
2013	915,765	4,842,430	(412,094)	(2,329,496)	(36,631)	(223,778)	467,040	2,289,157	416,673	2,037,863	50,367	251,293
2014	837,835	5,680,265	(335,134)	(2,664,630)	(25,135)	(248,913)	477,566	2,766,723	427,296	2,465,159	50,270	301,564
2015	811,273	6,491,539	(283,946)	(2,948,575)	(24,338)	(273,251)	502,990	3,269,712	450,257	2,915,416	52,733	354,296
2016	817,296	7,308,835	(245,189)	(3,193,764)	(16,346)	(289,597)	555,762	3,825,474	498,551	3,413,967	57,211	411,507
2017	803,232	8,112,067	(160,646)	(3,354,411)	(8,032)	(297,629)	634,553	4,460,027	570,294	3,984,261	64,259	475,766
2018	767,931	8,879,998	(76,793)	(3,431,204)	0	(297,629)	691,138	5,151,165	622,024	4,606,285	69,114	544,879
2019	698,516	9,578,513	(69,852)	(3,501,055)	0	(297,629)	628,664	5,779,829	565,798	5,172,083	62,866	607,746
2020	711,469	10,289,982	(71,147)	(3,572,202)	0	(297,629)	640,322	6,420,151	576,290	5,748,373	64,032	671,778

Uncertainty discount

Following the requirement of VM0015, an uncertainty discount was applied to the total carbon stock of forest classes, and post-deforestation class. The final carbon stocks, after the discount applied, are smaller and therefore the baseline is more conservative. This discount was not applied in the PDD tables but were fixed in the monitoring reports. The carbon stocks are an input in the VM Table 15a-c, and VM Tables 29a-c. These tables are recalculated at each monitoring period to discount the areas covered by cloud during the reporting period. This correction does not affect the applicability of the methodology, additionality or appropriateness of the baseline.

Minimum Mapping Unit

The historical land cover and land use change analysis (1996-2001), which was used to estimate the forest benchmark, was performed by Conservation International as an effort to map forest loss in the Andean and non-Brazilian Amazonian region. The forest cover and loss were classified using mid-resolution (30 m) Landsat imagery. The final product classification was filtered to a Minimum Mapping Unit (MMU) of 2 hectares, eliminating small patches of forest, and improving the overall classification accuracy. This processing can also be considered more conservative as only patches of forest bigger than 2 hectares was considered in the forest benchmark and therefore as project area.

Version 1.1 of the methodology, approved on December 03, 2012, changed the MMU requirement to a minimum of 1 hectare, irrespective of forest definition. Even though the MMU used by the project does not currently meet the new requirement, it is likely to be more conservative than the 1 ha MMU suggested by the methodology, as changes smaller than 2 ha will not be counted as deforestation in the baseline.

Primate monitoring – Biodiversity Monitoring Protocol

The frequency and abundance of primates (indicator 7a and b of the Biodiversity Protocol) was initially set to be monitored quarterly, considering that a participatory monitoring system would be implemented; however, due to the great need of environmental awareness building, *Proyecto Mono Tocón* is monitoring this indicator biannually. The last monitoring was done in 2017 and the entire protocol was revised based on the lessons learned.

The new protocol (Sup.Inf_MIR_04) is implemented regularly by installing camera traps in different sectors of the AMPF with the participation of the park rangers. The purpose of using camera traps to monitor the area is to know even more about the biodiversity species of the Protected Area which are not currently registered. This will contribute to promote further research.

Likewise, the *Titi Monkey Project* completed the impact measurement study for shade-grown coffee produced under good practices for biodiversity, ecosystem services and livelihoods of coffee producers in the San Martín region, through the use of camera traps.

The study concludes that they have identified 19 species of mammals and 15 species of birds in 17 sectors of the AMPF in 30 days, showing the importance of having coffee crops with Agroforestry Systems. It is to be noted that the study was carried out in partnership with the Arizona State University. At the same time, CI is coordinating the participation of the AMPF Head Office in Wildlife Insights the platform for the identification of species that are registered. (Sup.Inf_MIR_20a+b)).

The expected positive and negative impacts of the project and the indicators are the same as presented in the last monitoring report. However, based on the principle of adaptive management, few new metrics were added to better qualify the indicators, while other metrics will be reported next monitoring period due to the lack of information available for this monitoring period (2016-2018). The metrics measured in this monitoring report are enough to demonstrate the expected impact generated by the project, and therefore

is not affecting the integrity of the monitoring system. Please refer to the Sup.Inf_MIR_01 for a full list of metrics and the results for each of them.

Poverty Index – Socio-Economic Monitoring Protocol

During the first verification, the poverty index was estimated based on the USAID parameter, which establishes a global dollar value earned per household as the threshold of poverty. Since the second verification, the project has been measuring the poverty according to the Progress of Poverty Index (PPI)¹³ that uses the Peruvian definition of poverty and therefore is more accurate. In addition, the Conservation International is applying the PPI in the other livelihood projects and therefore the project can measure the progress against a control sample.

2.2.5 Risks to the Project (G3.5)

Since most of the AMPF biodiversity threat is habitat loss due to change of land use, many of these risks and mitigation activities also apply to benefits generated by the project on biodiversity. The risks are summarized in Table 2, and for more details on the risk assessment, see "Non-Permanence Risk Analysis – Report n6".

Table 2 – Factors analyzed in the Non-Permanence Risk Assessment

Non-Permanence Risks		
Internal	External	Natural
Project Management	Land Tenure	Torrential flows and flood
Financial viability	Community Engagement	Landslides
Opportunity costs	Political support	Geological risks
Project longevity (permanence)		Pest, disease outbreaks
		Forest fires and droughts
		Extreme weather

Additional risks that could prevent the expected benefits regarding Community and Biodiversity aspects were identified. Among them are risks posed by the coffee diseases, such as coffee rust (*Hemileia vastatrix*) or coffee fungus “chicken’s eye” (*Mycena citricolor*); lack of livelihood alternatives, particularly the dependence on coffee as the main source of income; the long-term sustainability of technical assistance, social conflicts, and effects of climate change. For each of these risks we have identified specific actions, described below, that have been implemented in a participatory manner with project beneficiaries to increase their level of resilience to these potential risks.

¹³ <http://www.progressoutofpoverty.org/>

Diseases to coffee, (coffee rust *Hemileia vastatrix* and chicken's eye *Mycena citricolor*)

No significant attacks of coffee rust were recorded during the reporting period. However, there were chicken's eye attacks in some coffee plantations that did not involve losses in production and quality during the period of report. The subscribers who implemented the suggested preventive measures had minimal or no attacks of pests or diseases thus, the efficiency of the technical proposal was validated. These practices include:

- Production and use of organic fertilizers.
- Introduction of rust resistant varieties, such as Castillo and Gran Colombia; incorporation of different varieties of coffee distributed by lots and separated by alleys.
- Preventive and curative control of rust and chicken's eye.
- Introduction of forest species in coffee plantations (shaded agroforestry system), combined with pruning shade, moisture, and aeration control.
- Identification of rust fungus.
- Preparation and use of Bokashi for soil restoration.
- Implementation of regenerative pruning.

Although the varieties of the genetic line of the Catimor (such as Castillo or Gran Colombia) are rust resistant, they need to be fertilized in order to obtain an acceptable produce and quality in cup as well as to resist other pests and diseases. Consequently, the parcels that were correctly fertilized were the ones that produced the best responses to the impacts of the pest.

In addition to the mitigation measures described above, the following practices are being applied and intensified to prevent further loss in the event of future outbreaks:

- Identification of non-sensitive coffee seedlings resistant to coffee rust outbreak; especially varieties of higher quality, such as Nacional Tipica, Caturra, Borbon, Catimor and others. This natural selection of coffee trees helps to obtain genetic material naturally adapted to withstand future outbreaks and ensure good quality coffee.
- Replication of rust resistant coffee varieties to ensure the preservation of coffee production for subscribers, generating income to support their families, even in the event of future rust outbreaks.
- Increased production of Bokashi and incorporation of trees to provide organic matter and a higher percentage of nitrogen to the soil, in order to accelerate the process of soil restoration.
- Maintenance and renovation of rust resistant coffee varieties provided by the project and of the species of coffee trees that survived the plague.
- Gradual renovation of the coffee plants older than six years, which along with other best agriculture practices guarantee high quality coffee.

Lack of alternative livelihoods

In the last two years, the project has prioritized the generation of greater economic income for beneficiary families through:

- **Access to coffee market.** The strengthening and connection to special coffee markets includes the expansion of the commercial coffee portfolio and reduction of intermediaries. This required to build a strong relationship of trust between the COOPBAM and selected specialty coffee importers. Besides setting a premium price, subscribers articulate their coffees directly to the importer, increasing the profit margin by doing without coffee intermediaries; therefore, export costs are covered in a fair manner. Also, since the end of the 2017 campaign, importers of standard coffee qualities, whose production volume can generate higher income for the subscriber, are being searched for.
- **Economic diversification.** In addition to the success indicators obtained through coffee, the project has achieved, on a smaller scale, the positioning of other economic activities that generate economic alternatives for the subscribing families. The pitahaya fruit is being marketed locally, positioning itself as the second income for beneficiary families with conservation agreements. Since February 2020, coordination has begun between the Office for the Promotion of Sustainable Private Investment Projects of the Regional Government of San Martín and the company AGROVAZA in order to commercialize dragon fruit grown in the Alto Mayo Protection Forest. This commercialization is expected to be achieved in the short term. Other activities such as bird and orchid tourism are already seen as successful family entrepreneurship. In addition, some subscribing families have decided to implement coffee shops and/or sell their ground and packaged coffee directly to the local market. A special mention goes to the women's committees' initiatives for the promotion of craft and embroidery techniques. Some of these products have been sold in various environmental events.
- **Food safety.** Through technical assistance from the field team, the project continued to promote the practices of vegetable gardens and small livestock to improve the families' food diet. It has also been working on activities leading to have healthy families through community organization and practices in the correct use of ecological bathrooms and the improved kitchens received as part of the benefits of conservation agreements. These actions are generating a positive impact on the economy of the families, as they do not require greater resources to purchase certain products that they used to find in city markets before.
- **Family financial management.** The subscribing families are being encouraged to understand the high importance of knowing how to spend and invest the economic income they are achieving with so much effort. An empowerment of good practices in financial management has been perceived in these years. Practices that contribute to the improvement of family economy and therefore, generates less dependence on forest resources.

The Long-term Sustainability of Technical Assistance

Although the transfer of knowledge to the technical staff of the Head Office began in 2018, this will not be completed until 2022 due to the diversity of issues that are implemented and the processes that are still underway, such as the good environmental practices in productive activities. For this reason, CI will take a chance on extending the Administration Contract until 2027. This extension of the contract would make a total of 15 years of working together with SERNANP towards an adequate management of the AMPF.

The extension will include the support in the expansion of the Protected Area by almost 32 thousand hectares in the northern zone where the Río Nieva Reserved Zone is currently located.

Additionally, project sustainability processes have been implemented in this reporting period. These actions were addressed towards the AMPF Head Office, the COOPBAM and included a new approach in relation to conservation agreements.

Technical and financial support has been given to the Head Office of the AMPF to update its Master Plan. The update includes workshops with the main actors and local population in the different sectors where SERNANP intervenes. The new Master Plan proposes a new implementation structure with the leadership of the AMPF Head Office and its strategic allies, putting emphasis on the environmental governance approach.

Likewise, the annual training plans were implemented as part of the capacity transfer process for the technical team of the Head Office. The training included topics related to the Geographic Information System, how drones are used, communication for environmental peace and the management of Protected Natural Areas and human rights.

Since the COOPBAM has broadened its scope of intervention to a landscape scale in the Alto Mayo sub-basin, a process of identification and training of tasters is being carried out in order to select talented young people who could later be part of a group of volunteers that provide support in the coffee quality laboratory. Likewise, the project implements actions to improve cultivation, harvest and post-harvest practices in the plots of the COOPBAM partners, and it does so through a cooperation agreement, where the technicians and promoters of the COOPBAM are the ones who provide field assistance.

The Cooperative, having become the main commercial agent of coffee in the AMPF, needs to strengthen its institutional capacities at the managerial and infrastructure level, therefore it relies on the formulation of its Business Plan, and the identification of additional financial sources for the construction of its collection center in the city of Rioja.

Regarding the conservation agreements, a transition process is being carried out, passing from individual to collective agreements where organization is promoted among the subscribing families in each town in order to form a Committee to receive the benefits of the project, and thus facilitate the monitoring of the commitments assumed by the AMPF Head Office and the community.

Having the population organized through Committees will facilitate the search for financial resources through competitive funds in productive issues with good practices, such as bio trade and ecotourism.

Project Baseline Integration with National Forest Reference Emission Level

The project has developed a baseline to estimate the GHG emissions reduction based on the requirements of VM0015. Such baseline has been validated and the actual emissions reduction since 2009 has been verified in multiple verification events. According to the same methodology the project must use national or jurisdictional baselines if available. In case of Peru, the government has developed a Forest Emission Reference Level (FREL) for the amazon region and submitted to the UNFCCC's

secretariat (Sup.Inf_MIR_3). The FREL was defined based on the historical deforestation trend from 2001 to 2014 and projecting to 2020. However, the process and rules to integrate the project-site baselines to FREL or Peruvian's MRV system was not yet defined. As the project has received a letter authorizing the use of current baseline until December 31, 2020 (Sup.Inf_MIR_18), there is a great uncertainty and risk regarding the carbon crediting accounting after 2020. It is dependent to the revision of the current FREL, to extend the GHG emissions past 2021 as well as the definition and nesting rules.

Continuity of the Administration Contract

The Administration Contract was renewed in 2017, which implies that the AMPF co-management will continue at least until November 2022. This will allow consolidating the main technical and social processes promoted by the project, as well as ensuring the transfer of knowledge and strengthening the relationship between the AMPF Head Office, the local population and the various public and private actors that intervene in the management of the NPA (Sup.Inf_nprt_02d+e).

Social conflicts

The AMPF was created in 1987; however, it was not until early 2001 that the State appointed the first Chief of Head Office. Later, around 2005, this Head Office, with the support of donations, obtained the necessary funds for minimum operation within the area. Unfortunately, this state of neglect led to the settlement of people inside the AMPF and the incursion of land and timber dealers that generated a front of opposition to authority and thus, to the preservation of the area.

The attempts to restore the principles of authority and conservation produced, as expected, reactions from the population settled in the AMPF that led to various social conflicts. The conflicts that occurred in Naciente de Río Negro in 2010 and in Aguas Verdes in 2011 were the ones which had the greatest negative impact on management effectiveness. They were both generated by the illegal construction of cart tracks in the AMPF.

Between 2011 to 2016 the implementation of several actions in the AMPF to minimize and avoid social conflicts is producing positive results. Through the joint efforts of the project team and the AMPF Head Office staff, disagreement situations in Aguas Verdes were successfully diffused, and dialogue was established between the *rondas campesinas* and various public institutions, and local, regional, and national political actors. In addition, the project was able to restore the technical committee for conflict resolution of Aguas Verdes. Lastly, the project is working on the implementation of a Government services hub in Aguas Verdes. Protected area legislation restricted the provision of services within the AMPF boundaries; therefore the project began the negotiation with the Government of San Martín and the respective agencies to assure the implementation of a functional hub in the town of Aguas Verdes to meet health and short-term education needs. The town is located in the AMPF buffer zone and should bring a resolution of this social conflict.

Unfortunately, during the second semester of 2016, some colleagues of the project and some leaders of the subscribers were systematic victims of aggressive actions by a group of families settled inside the NPA entirely dedicated to illegal activities. The actions have been classified in the civil-criminal jurisdiction

and follow the respective proceedings. Security measures have been implemented to safeguard the integrity of the project personnel and the allied population; such measures also guarantee compliance with the conservation agreements and the main objectives established for each strategy. The main measures implemented are:

- Transit in areas where civil-criminal proceedings exist should be avoided to nullify the possibility of aggression on the part of opposing families.
- The implementation of field activities planned by conservation agreements and women's committees will be carried out with the support of the COOPBAM. Technical assistance to the subscribers will be provided by the promoters and the delivery of benefits will take place in the town of Aguas Verdes.
- The activities of communication, environmental education and civic actions (including medical campaigns) will be carried out in places where safety could be guaranteed since those involve multisectoral presence and high influx of local population (subscribers and non-subscribers).

The collective institutions led by the Management Committee, the local government of Rioja and the Legislative Power -represented by congressmen from the San Martín region- have involved the Ministry of the Interior in providing the AMPF Head Office and the park rangers team with security during their work, thereby preserving order in the Protected Area. As a result, a new checkpoint and surveillance post has been built in Flor de Selva, the farthest sector of the AMPF, where control and surveillance actions are carried out to mitigate deforestation.

Effects of climate change

During the reporting period, climatic anomalies have been less severe, and no climate events that put risk the productive system and the population in risk were observed. The permanent monitoring performed by the project personnel has contributed to make the plantation more resilient to plagues and diseases, this includes the prioritization of pruning and fertilizing as climate adaptation measures. Further details are provided in the development section of the social management strategy.

2.2.6 Enhancement of High Conservation Values (HCV) (G3.6)

The Alto Mayo Protected Forest, in its entirety, is considered as an HCV, maintaining its ecosystem functionality is fundamental and of high importance for the more than 200 thousand people who live in the provinces of Rioja and Moyobamba. In that sense, all the activities carried out during the reporting period have helped to face the great management challenges of such an important NPA turning them into opportunities to obtain historical results, not only for the AMPF, but also for the national system of NPAs.

The actions of the management of the AMPF are aimed at seeking the welfare of the local population through the conservation and sustainable use of natural resources and ecosystem services of the NPA. A tangible example of this is the more than 5,500 hectares of degraded forest that are being restored with coffee under the agroforestry systems. More than 2000 hectares out of those provide coffee of excellent

quality to the special markets of Canada, USA, New Zealand, and Germany being sold directly at preferential prices through the COOPBAM.

Additionally, tourism initiatives, at family and community levels, are increasing. This is mainly because local population has realized that the management of natural capital is an opportunity to generate economic income. That is why family initiatives on birds and orchid tourism are being complemented with communal initiatives such as Urkuchaqui waterfalls (Nueva Zelandia), butterfly farms (Palestina) and the Onercocha lagoon (El Paraiso).

Proposals for competitive funds to leverage complementary funds that consolidate activities are being designed as actions for the sustainability of tourism ventures. In the Arena Blanca reserve, *Turismo Emprende*, a program of the Ministry of Tourism, granted funds for the installation of cabins for tourists to spend the night.

Finally, the conservation of the AMPF has a direct effect on the development of the region. It has an impact on the private sector that buys the carbon credits, on the importers and consumers of the coffee produced in the NPA and on the various specialized tourists who visit the bird tourism pilots. Conserving such an important protected natural area is the result of the joint work of more than 90 professionals based in Rioja, Lima and the United States who are constantly disseminating the concept that preserving areas such as the AMPF means to preserve lives.

2.2.7 Benefit Permanence (G3.7)

The sustainability of the benefits generated by the project in terms of climate, community and biodiversity lies mainly in the consolidation of the integral governance of the Alto Mayo Protected Forest. This governance implies that:

- i) the State leads all the processes within the NPA and its buffer zone, making public investment visible when improving access to and quality of basic services, supporting and guaranteeing the conditions for the articulation of private investment.
- ii) the local population, in its various levels (family and community), must be empowered in the implementation of family and healthy community concepts which are the premises for the design of the various benefits delivered within the framework of the strategies of conservation agreements and social management.
- iii) the COOPBAM must achieve financial autonomy and optimum technical managerial levels to self-manage and maintain the growth projections that greatly benefit the population allied to the management of the NPA.
- iv) the Management Committee should be consolidated as the main platform to bring together public and private institutions, social groups, educational entities and other actors whose roles contribute to the management of the NPA, both at the regional and national levels.

Everything described above must have a positive impact on the development of the local population settled in the project area and the one living in the provinces of Rioja and Moyobamba and at the same time, it has to achieve the conservation, the use of natural resources and the maintenance of the ecosystem functionality of the AMPF. In order to accomplish this vision, the project has been conducting:

- i) The transfer of leadership of all the management processes to the staff of the AMPF Head Office, which implies a permanent training of capacities and the building of a community-institutional relationship.
- ii) The gradual implementation of healthy families and communities as fundamental concepts. This is being done through social management strategies, conservation agreements, communication and environmental education. These fundamental concepts are seen in the various benefits that increase living conditions, as well as in the various multisectoral actions for community benefits such as medical campaigns and civic actions. The evolution of conservation agreements from family to community level is a crucial issue in this process. Their approval and implementation by the competent authority will start a new stage of benefits to the community that should be complemented with public investment for access to and improvement of basic services.
- iii) In relation to public investment, and as part of the sustainability of our interventions, the project has supported the preparation of project profiles to benefit tourism ventures in Aguas Verdes and the Nueva Zelandia community. Through Turismo Emprende, a program of the Ministry of Foreign Trade and Tourism, financing was obtained for building infrastructure in the Arena Blanca reserve for \$60 thousand dollars for lodging service. Also, the project proposal to improve the trails to the Urkuchaqui waterfall in the Nueva Zelandia community is under evaluation.
- iv) The strengthening and permanent support to the Management Committee is a vital part in the management of the NPA. Coordination with the main national authorities such as the Regional Congressmen, Ministers and the Prime Minister has been achieved through this platform. This includes, for example the execution of the Project SNIP 10477 by PEAM (PEAM, which is the executing agency of the Regional Government) that built the field school in the town of Sol de Oro which was later given in a session of use to the Head Office of the AMPF to use it as part of its activities in control and surveillance, in addition to serving as a space for meetings and workshops with the population in order to raise awareness in the conservation of the Alto Mayo Protected Forest.
- v) The COOPBAM has been financially growing according to plan. Since the first sale in 2015, more than \$2.9 million have been exported. In 2019, the COOPBAM got the highest export volume, reaching 13 containers, and it is projected that by 2020 they will have reached 20 containers, four of them would be micro-lots, called high-quality coffees scoring more than 84 points in the cup. These results have strengthened the members who have been dealing with financial institutions to obtain loans that allow them to face the coffee harvesting campaigns.

2.3 Stakeholder Engagement

2.3.1 Community Consultation (G3.8)

The team maintain an active communication with the stakeholders throughout the project period, and has performed an intensive consultation process before start the activities. In addition, the conservation agreement – the main mechanism to promote conservation – is designed with the stakeholder participation. The conservation agreements are reviewed and renewed annually giving the opportunity to adjust and improve the consultation process. In addition, the implementation of specific activities such as the promotion and creation of a Conservation Agreement Subscriber Committees allowed the implementation of communal agreements, the development of the Life Plan and the design of the tourism project in New Zealand. Those are few examples of processes that have been developed jointly with the local population and subject to consultation and voluntary approval.

In addition, throughout the reporting period the project has engaged with the different stakeholder using different communication strategies as described below.

Rondas Campesinas

Most of the population living in the AMPF is organized in *rondas campesinas*, a type of social organization protected by Law No. 27908 and its regulations. None of these patrol groups settled in the AMPF is officially registered with the *Superintendencia Nacional de Registros Públicos* (national entity that holds public records in Peru) - SUNARP (from its acronym in Spanish). All *rondas campesinas* groups should be registered with SUNARP to be in compliance with the law. However, in practice, these *rondas* omit this essential step and district, provincial, regional and national patrols acknowledge and support the *rondas campesinas* settled in the AMPF even without formally complying with the law.

As reported during the previous verification period, the AMPF Head Office signed, during 2013, two agreements with *rondas campesinas* from El Triunfo and Aguas Verdes, which represent 19 of the 26 existing towns. The implementation of both agreements transcends until the present reporting period and can be seen in the activities of conservation agreements, social management, tourism promotion, articulation to public investment, support in the coordination with other public bodies, commercial articulation through the cooperative, among others.

Coordination meetings have been held with leaders of the Peasant Rounds of different villages that are located within the Protected Area in order to have their participation in the process of updating the Master Plan. There was a high turnout of participants in the workshops; even rounds from the Candamo sector, who oppose conservation actions, were present. Although the latter have tried to boycott the events of the Master Plan, without success, since there has always been a larger number of participants from allied entities.

Since November 2018, the AMPF Head Office was taken over by Eng. Ivonne Paico, who has maintained the dialogue with various social groups, including the opposing Peasant Rounds. The *Frente de Defensa de los Intereses de Moyobamba* (FEDEIMAN), whose president is a former leader of the Peasant Rounds has acted as a mediator in the dialogue. However, further dialogues are still required for a complete alignment with the guidelines of AMPF.

Technical Advisory Group (Mesa Técnica)

Due to the construction of an illegal trail that runs from the town of Aguas Verdes (buffer zone) to El Triunfo (within the AMPF), the population organized and created the *Frente de Defensa de los Intereses de los Poblados de Aguas Verdes* (Front for the Defense of the Interests of the Villages of Aguas Verdes) which, as in the case of the *rondas campesinas*, has not been registered with SUNARP either. However, the AMPF Head Office has been coordinating with this front for more than two years in search of solutions to their proposals, which are contrary to the regulations of NPAs and the wholesomeness of AMPF.

The Technical Advisory Group for the resolution of this conflict was created as a result of the dialogue with the Front for the Defense and with the *rondas campesinas* settled in the AMPF. The Technical

Advisory Group is a body that brings together not only these actors and the AMPF Head Office, but also representatives of the Regional Government of San Martín, the local governments of Miguel Pardo Naranjos, Rioja and Moyobamba, the Ombudsman Office, Conservation International and others.

The Advisory Group is the highest instance for dialogue between local people and the State. All the complaints from the local population are brought there, but also their aspirations for development, generating proposals that meet these aspirations without reducing the AMPF.

Additionally, this platform was designated by the Presidency of the Council of Ministers as the primary instance for the solution of socio-environmental conflicts that occurred within the NPA, such as those that occurred since the second semester of 2016 and described in the preliminary sections. The support of the project to this platform is permanent and carried out through the NPA Headquarters and the Management Committee which are the optimal entities and with the right attributions to represent the position and alternative solutions proposed by the AMPF management team.

Since January 2019 there has been a new management in the local governments and in the Regional Government of San Martín which, in order to obtain votes during their political campaigns, made some offerings in the surrounding areas of the Protection Forest. Therefore, they refused to activate this technical advisory group. Likewise, coordination has been maintained with the Office for the Promotion of Sustainable Private Investment and the Management of the Regional Authority in order to reactivate the investment plan in the Nucleo Funcional de Aguas Verdes, but this was stopped by the high management of the Regional Government of San Martín.

Subscribers and promoters

This group of stakeholders is the main actors from the local communities with whom we work as a project and as a comprehensive management for the AMPF.

Since its inception, technical staff is constantly maintained in different sectors where these agreements are implemented. This facilitates the flow of communication between the population and the technicians who serve as spokesmen for the concerns, disagreements, and suggestions of the subscribers. Any complaints are answered immediately, and are assumed by the head responsible of the implementation in the field in support of a specialist from the AMPF Head Office. In specific situations, meetings between subscribers, the AMPF Chief of Head Office and the Manager of the Administration Contract are encouraged in order to promote transparency and to solve the most critical complaints from the subscribers.

It is noteworthy that the team formed by the person responsible for the implementation of Conservation Agreements and the specialist from the AMPF Head Office promote and participate in meetings with the subscribers in each of the sectors. They are constantly providing feedback to the management team on the advances made under the strategy and any issues or problems arising from the subscribers.

The promoters of Conservation Agreements have made great contributions. Even though their primary role is purely technical, they function as conciliators and communicators of the AMPF management. They retransmit any question that local people may have (be they subscribers or not) to the technician or to any

personnel from the management team. This relationship was strengthened with the creation of the COOPBAM.

The COOPBAM deserves a special recognition as the main actor in the NPA management. The contribution of the cooperative goes beyond providing various commercial and welfare benefits to the subscribing population that has voluntarily decided to become a member of the COOPBAM. The cooperative is also one of the main speakers of the NPA management. The testimonies given by all its members reflect the great effort and benefit that the partnership with the State implies.

The conflict resolution department of the CI Head Office gave support to consolidate the good relationship between the park rangers staff, the field technicians and the subscribers so as to strengthen the effective communication capacities in favor of environmental peace. The techniques and tools are implemented entirely in the field so the interaction between the management team and the beneficiaries has evidently improved.

Local people

The direct meetings with local people were identified as the best mechanism for the collection of complaints regarding the activities of the project and the management in general. The grievance resolution mechanism proposed during the validation is still maintained, however barely used. Most of the local population avoids making complaints in writing. This does not mean they are fearful about the mechanism, it is not common practice of the population to make written complaints. In order to adapt to this cultural nuance, it was decided to promote meetings with people settled in the AMPF.

The AMPF management team has been holding regular field meetings with the local population. This was achieved thanks to its various strategies: communications, Conservation Agreements, community engagement, monitoring and surveillance, and institutional impact.

The project has been explained in all the villages during the initial meetings. Additionally, all sort of institutional individualization of the management of the AMPF is avoided. Therefore, the presentation of professionals always claims to be part of the management team of the area.

No complaints about the intervention of the project have been received from local residents during this reporting period. On the contrary, the people who had never worked under the AMPF management got closer. One of the reasons for this approach is the achievements that these people have witnessed in relatives and neighbors who are part of the project and who have been requesting to join in order to receive benefits to help them improve their living conditions. In the last two years, 95 heads of household have joined the project.

Additionally, the growth of the COOPBAM is the most visible achievement in the local population, obtaining better prices in the sale of coffee, which is supported by exporting companies that seek, not only a quality coffee, but also successful family stories that relate to productive activity, forest conservation and biodiversity.

This year, the COOPBAM has received loans from Conservation International Ventures to deal with the harvest of coffee and is about to obtain loans from Nest and Root Capital, finance companies that are interested in strengthening the managerial capacities of the cooperative team and its financial management.

Awajún Indigenous Communities

It has been confirmed that the project does not generate any negative impact on Awajún indigenous communities since they do not maintain traditional use of resources or territory within the AMPF.

It is noteworthy that CI-Peru ongoing projects with some Awajún indigenous communities are considered a plus in the intervention strategy. The periodicity in the implementation of these projects helps to socialize the intervention in the AMPF and to be aware of any comments that may arise on the part of the indigenous communities about any concern or benefit attributable to the project. To date, the technical staff of the project in Awajún communities have not received or heard of any adverse comment about the AMPF management.

The success of the COOPBAM has led coffee producers in indigenous territories whose activities are monitored by the CI's projects to request to be part of the members of the cooperative to benefit from the commercial articulation in special markets, generating as well, good environmental practices in the productive systems and a good relationship with the members of the indigenous communities in Alto Mayo and Shampuyacu.

2.3.2 Public Comment Period Publicity (G3.9)

This report was uploaded into the Climate, Community and Biodiversity Alliance's website for public comments. The public comment period will be at least 30 days. The project informed the stakeholders with internet access of the website and the opportunity to comment of the document. For people living in the project zone without internet access, information regarding the content of the document was communicated through the Management Committee, park rangers, and conservation agreement technicians with information on how to submit their comments. Hard copies of the document were available for public viewing and comment during the public comment period at the AMPF Head Office as well as at Conservation International's offices in Rioja, allowing local, regional and national stakeholders to provide feedback on the document.

2.3.3 Distribution of Project Information (G3.9)

In addition to the measures described in the section 2.3.2 Public Comment Period Publicity, key information about the project and the main results of the monitoring report was translated into Spanish and organized in a poster to facilitate the comprehension of local population. The poster was displayed in various parts of the AMPF and major towns in the project zone.

2.3.4 Conflicts and Grievances (G3.10)

Any complaint or grievance received by the project during this monitoring period was addressed following the requirements from the CCBS. The project has developed and implemented a conflict resolution mechanism that is described in detail in the section G3.10 of the CCBS PD. The mechanism has not changed during this monitoring period and has the following steps: 1) reception of complaints/grievances by the AMPF Head Office; 2) Identification of stakeholders and interested parts in the conflict; 3) Discussion and agreement; 4) Monitoring of resolution; 5) Documentation and archiving. The grievance process has been publicized to communities and stakeholders, and project responses have been given within 30 days. The process is supported by *Defensoria de Pueblo*, a third-party organization.

As part of the national process of designing the national REDD+ program, the Peruvian government has assumed the commitment of developing a complaint mechanism for its donors. CI Peru has been identifying ways in which the complaint mechanism of the AMCI project can contribute to the mechanism to be established at national level so that queries, requests or complaints that may occur within the framework of the AMCI project can also be recorded in the future safeguards information system that Peru designs.

2.4 Management Capacity and Best Practices

2.4.1 Required Technical Skills and Expertise (G4.2)

The size and complexity of the project requires collaboration among a broad range of partners and local actors with different roles and responsibilities within the project. For details on the expertise of each of the partners with regards to REDD, please see sections 2.1.3 and 2.1.4). The Management team includes individuals with significant (i.e. at least 5 years) experience in all skills necessary to successfully undertake all project activities. For a detailed description of the experience of each of the members of the project management team, see Sup.Inf_nprt_01.

The work team consisted of 90 professionals, mainly members from four institutions: Conservation International, *Asociación Ecosistemas Andinos* (ECOAN), The National Service of Natural Protected Areas (SERNANP) and *Cooperativa de Servicios Múltiples Bosques del Alto Mayo* (COOPBAM).

The diversity of professionals involved in the management of the AMPF facilitates understanding the dynamics of working in the field with the population and state institutions. Professionals from the sciences, biology, forestry and environment, as well as technicians in agriculture, lawyer and others contribute to the daily work. Some of these professionals develop training in Protected Areas.

2.4.2 Worker Training (G4.3)

The team has developed annual Capacitation Plans (Sup.Inf_MIR_13a+b) which were designed for the AMPF management personnel. The plan prioritized issues related to the actions developed by the

REDD+ project such as; geographic information systems, drone system Management, communication techniques and skills for environmental peace, management of NPA, human rights, first aid entrepreneurship, the strengthening of productive activities in coffee (including 16 training on organic certification training), meliponiculture, vanilla, food security (bio-gardens and raising of small animals), ecotourism, community life plans and relations, conservation agreements, among others. In total over 77 trainings were provided during this monitoring period. More information regarding worker training is detailed in section 4.1.1 (Impact 3).

Conservation Agreements Technical Team

In the last year, a group of field promoters -through the COOPBAM- joined the technical team of conservation agreements managed by ECOAN, to further strengthen the activities of good productive practices especially in the production of coffee. This strategy of articulation with the COOPBAM has been aimed at pointing out the work done by the members of the Cooperative and the subscribers of conservation agreements to improve product quality and meet the objectives required by the organic certification processes.

The technical coordination of Conservation International held meetings with the coordinators of both organizations and the technical team, ECOAN and COOPBAM, to analyze the implementation of the field work and the fulfillment of the commitments assumed by SERNANP and the local population. This also helped to provide feedback on the implementation actions under the principle of lessons learned, while each entity holds weekly meetings with its team to evaluate and reflect on the various circumstances that occur.

On the other hand, constant visits have been made, at random, to the towns where conservation agreements are in place. This has permitted to verify in situ the veracity of the information reported by the field technicians. The information has been collected through group workshops in each of the places visited. This was a good opportunity to present and refresh the objectives of the conservation agreements that families had signed with SERNANP. In total, 95 new agreements were implemented during this training period.

Monitoring and Surveillance Technical Team

One of the important processes that has been addressed in the project's technical monitoring and surveillance team is how to tackle the illicit activities identified in the population so as to prevent them from happening again. One way to deal with this problem is to offer the offender the possibility to work in coordination with SERNANP. For this reason, between 2018 and 2019 the training sessions on conflict resolution using techniques and instruments for the construction of Environmental Peace were prioritized. In addition to this, actions were carried out in the field to gather information that may help to build the life plans and the development of the communities prioritized in the project. The message that is being conveyed is to make use of natural resources in accordance with the conservation guidelines of the Protected Area.

Undoubtedly, a priority action is to strengthen the capacities of the AMPF Head Office team, specialists, and park rangers on the use of the GIS and drones which help to identify and prove illegal actions made in the field.

About the Surveillance and Control System in the NPA, the specialist of the AMPF participated in a short duration course that contributed to strengthen his capacities. The course was given through the virtual platform of the University for International Cooperation of Costa Rica.

The AMPF Head Office

The dynamics of the management of the area led to an increase in the size of the staff team, including park rangers and technical team. They are paid for by the project, but many of them report directly to the AMPF Head Office and also access the training from SERNANP.

Between 2018 and 2020, 16 training sessions were held for the AMPF management personnel. The session that stood out most was the one on communication techniques for environmental peace which had been requested by the Head Office as a way to continue with the training on socio-environmental conflict management. The sessions had the active participation of the current Head of the AMPF.

Another important issue that CI has been supporting the AMPF Head Office with is the strengthening of the technical team for the updating of the Master Plan. This involved workshops and work meetings with specialists from the Directorates of Environmental Management and Strategic Development of SERNANP in Lima. In addition, the Head Office is implementing a new strategy; requested technical opinions on projects in the AMPF should no longer be given exclusively by only one specialist. Therefore, the whole technical team is being trained in order to be able to carry out these procedures. CI team provides continuous technical advice to the AMPF Head Office and the Management Committee to make their participation effective in the different public/private spaces around the NPA.

2.4.3 Community Employment Opportunities (G4.4)

The hiring of new staff for the AMPF Head AMPF Head Office and for the various partners of the Administration Contract, as well as for CI-Peru followed the guidelines established and described in the CCBS PD. Therefore, employment opportunities have been generated considering only the capabilities of the candidates for the required skills and knowledge to perform the job without any exclusion or discrimination.

Of the total number of personnel hired during the evaluation period for the REDD project, 73% (78 out of 106 professionals) come from San Martín and from adjoining regions such as Amazonas and Loreto. This percentage has not changed in the last years taking into account that the purpose of the project is to forge local capacities in order to empower the conservation of ecosystems and forests of the AMPF. It should be noted the high level of knowledge about the local environmental context that professionals from the region have which, coupled with the capacity to arrange and engage with the local population around the project, helps to shorten times in different processes.

2.4.4 Relevant Laws and Regulations Related to Worker's Rights (G4.5)

A comprehensive list of laws and regulations covering worker's rights in Peru is described in the section G4.5 of CCB PD. In addition, CI has specific policies that go beyond the formal regulations to ensure a safe, comfortable, enriching work environment. These policies include, for example, Anti-Discrimination and Equal Opportunity Employment Policy, Harassment Policy, Professional Development Policy, and Workplace Conduct Policy. CI follows all the labor laws and regulation, and its internal policies and ensure that employees are aware of them.

Induction Protocol

All new staff of the AMPF, regardless of the organization that hires them, receives an induction orientation from their supervisor. This orientation aims to contextualize the new employee on the AMPF management, the current context, and the expected contribution from the professional as well as their rights and obligations. Where necessary, and depending on the degree of responsibility of the position, the AMPF Chief of Head Office or Administration Contract Manager (or both) will conduct further dialogue with the new staff in order to reinforce the high importance of their responsibilities within the management area (Sup.Inf_MIR_06).

Since the Project is developed in the AMPF where SERNANP is the main authority, the induction protocol for the new worker is carried out following the guidelines designed by the State which has the purpose of empowering the functioning of the System of Natural Protected Areas and the self-conservation of Protected Natural Areas. Then, and according to the institution hiring the staff, the new personnel are made aware of the internal policies of work development.

2.4.5 Occupational Safety Assessment (G4.6)

To date, the risks in the development of the work of the management team have been minimized thanks to the implementation of the security protocol. The major risks still remain the same: risks of natural disasters, of accident and illness, and from violent situations (see Section G4.6 of the CCBS PD for further details). The action to maximize worker's safety includes: at least two rangers in each patrol, avoiding verbal or physical confrontation, avoiding trekking at night, carrying survival kits and antivenom in the first aid kits, defensive driving, and following evacuation and emergencies protocols.

The security protocol has remained unchanged from the previous monitoring period and its implementation remains as planned (Sup.Inf_MIR_07). During this monitoring period, a series of training was provided to refresh these protocols.

2.4.6 Financial Health of Implementing Organization(s) (G4.7)

The financial viability was evaluated as part of the Non-Permanence Risk assessment (see AM Non-Permanence Risk Report n6) and the evidences demonstrate an adequate financial health to continue to implement the project (Sup.Inf_nppt_06, 07a, 07b, and 08)

2.5 Legal Status and Property Rights

2.5.1 National and Local Laws (G5.1)

An extensive analysis of laws, statutes and regulations that are applicable to the project, including worker's rights, was done and is described in detail in the Section 1.11 of the VCS PD and Sections G4.5 and G5.1-2 of the CCBS PD. Since the last monitoring period, there were no changes in the laws and statues listed in the PDs.

2.5.2 Free, Prior and Informed Consent (G5.3)

The Alto Mayo Protected Forest is a natural area protected by the Peruvian State registered in *Partida Registral* N° 04015312 of the *Sección Especial de Predios Rurales de la Zona Registral* N° 3 (Special Section of Rural Plots of the Registration Zone No. 3) - Moyobamba – SUNARP (National Superintendence of Public Registries) on March 28, 2000. According to the Legal Report made in 2011 by the Peruvian Society of Environmental Law, the rural plot of the AMPF does not overlap with any pre-existing property of third parties. Furthermore, the main actions of the project are primarily implemented within the rural property of the AMPF and in the plots of farmers who voluntarily subscribe to the conservation agreements.

Under these premises, it can be concluded that there is no third-party property within the NPA AMPF. Therefore, private property rights are not violated. However, the activities promoted by the AMPF management are coordinated and consulted with the local population. The most visible example of this is the signing of conservation agreements, documents signed to the whole of their will by the parties. Likewise, we proceeded with the signing of the agreements between the AMPF Head Office and the *rondas campesinas* during 2013.

So far, no claim on usurpation of private property has been sent to the NPA Headquarters nor to Conservation International or any of its partners, so, it is presumed that the local population that interacts with the project, be subscriber or non-subscriber, allied or contrary to the management of the NPA, has stated its position on possible violations of the right of private property by the project.

2.5.3 Property Rights Protection (G5.4)

The legal and related contexts explained in the previous verification are kept up to date. The project area remains the same as when it was validated. Also there is no variation in the Peruvian or international legislation which requires a re-evaluation of this issue, including the encroachment of private, community, or governmental properties (see section G5.3 of CCBS PDD for further details). In addition, in late 2015

SERNANP started an in-situ assessment of the AMPF limits, in order to analyze any potential conflict with adjacent properties and identify areas that require a physical demarcation. Only 20% of the AMPF perimeter is naturally delineated by natural features (e.g. topography) and does not required any field demarcation. If any inconsistency or potential overlap with other land or use rights holders is identified in the final report, then a conflict resolution mechanism will be set to reconciled and find a commonly agreed solution. This conflict resolution process will be framed in the corresponding Peruvian normative.

The project does not intend to involuntarily reallocate people or the activities important for the livelihoods and culture of the communities. The basic needs and the development infrastructure for the local population living in the AMPF are not possible to implement within this NPA because they are illegal by the State. However, the project is aware that the natural evolution of the management of the AMPF involves creating opportunities for these populations. As explained in Section 2.3, the project supports the technical advisory groups as a platform for dialogue and to solve the socio-environmental conflicts, which ultimately is facilitating access to basic services such as health, education to the local communities, by bringing such services to the buffer zone.

At the same time, the management of the AMPF, with the support of the project, is implementing social benefits aimed at improving the living conditions of the people who have voluntarily committed to become allies of the AMPF management. As a result of the various inter-agency coordination, the AMPF Head Office, the Management Committee and CI Peru have made agreements with several institutions; for instance: The Local Education Management (environmental education in the formal curricula), Regional Government of San Martin (implementation of Aguas Verdes Functional Hub), Provincial Municipality of Rioja (evaluation of public investment in tourism) and the Ministry of Energy (implementation of the National Program for Rural Electrification). The objective of these pilots is to generate family management models compatible with their environment ensuring improvements in living conditions, as well as test the implementation of the multisectoral actions (like health campaign and civic activities).

2.5.4 Identification of Illegal Activity (G5.5)

No project benefits are derived from any illegal activity. The project has been working closely with the AMPF Head Office to control and halt any illegal action might that occur in the project area. The most common illegal activities inside the AMPF are the deforestation due to coffee plantation, poaching, butterfly and orchids extraction and land trafficking. These illegal activities have a direct influence on the project's climate, community, and biodiversity impact. Deforestation not only leads to GHG emissions but also causes forest fragmentation, species habitat isolation, and depletion of environmental services important for the surrounded communities. Fauna and flora extraction, including poaching, affects the quality of the habitat, can reduce the quantity of pollinate and seed dispersers vectors.

Between July 2018 and April 2020, more than 793 ranger patrols have been implemented to prevent and mitigate illegal activities (mainly deforestation and fauna and flora extraction); this is a significant increase compared with the last verification period and reflects the adaptive management processes set in place. It should be noted that the patrols in the northern area of the BPAM are carried out between park rangers and members of the Peruvian National Police, a collaboration that has been taking place since September 2018, which contributes greatly to the reduction of environmental illicit .

In addition, all the AMPF strategies supported by the project contribute to reduce these activities and provide livelihood alternatives to the settlers. The Conservation Agreements, for instance, provide tangible benefits while explicitly mention that no illegal activities are accepted. Further details of each project strategy and results are described in section 2.1.1.

3 CLIMATE

3.1 Monitoring GHG Emission Reductions and Removals

3.1.1 Data and Parameters Available at Validation

No changes were made to the data and parameters presented to the validators during the validation process. Please refer to the VCS PD Section 4.1 for the list of data and parameters, also publicly available at the VCS website.

3.1.2 Data and Parameters Monitored

Data / Parameter	Forest Cover and Change Map (2018-2020)
Data unit	Map
Description	Digital map of forest cover in 2020 and change 2018-2020 in the project area and leakage belt (Figure 3 and Figure 4)
Source of data	Sentinel-2 (MR Table 01.a.)
Description of measurement methods and procedures to be applied	Satellite imagery-based forest cover change classification using decision tree and Random Forest methods.
Frequency of monitoring/recording	At every verification period
Value monitored	0.5 ha of forest patch as minimum threshold
Monitoring equipment	QGIS 2.18 and R statistical program 3.14.1
QA/QC procedures to be applied	Quality Control and Assurance procedures are detailed in the Methodological Annex. The overall map accuracy is above the 90% required by the VM0015
Purpose of the data	Calculation of project emissions and leakage.
Calculation method	n/a
Comments	Raster format – 30m resolution – projection system UTM zone 18S – datum WGS84. GIS files provided to the verifier.

Data / Parameter	ABSLPAi,t
Data unit	ha yr ⁻¹
Description	Annual area of observed deforestation in the project area for the period 2018-2020
Source of data	GIS processing

Description of measurement methods and procedures to be applied	Results of overlaying the forest cover map with the project area boundaries
Frequency of monitoring/recording	At every verification period
Value monitored	GIS files of the project boundary
Monitoring equipment	Computer and QGIS 2.18 and ArcGIS 10.5 software
QA/QC procedures to be applied	Projection system and datum was kept consistent. Clear and detailed documentation and independent desk review to assure consistency and accuracy of the GIS procedures
Purpose of the data	Calculation of project emissions
Calculation method	Spatial Analysis tool (tabulate area in zonal statistics toolbox)
Comments	n/a

Data / Parameter	ABSLLKi,t
Data unit	ha yr ⁻¹
Description	Annual area of observed deforestation in the leakage belt for the period 2018-2020
Source of data	GIS processing
Description of measurement methods and procedures to be applied	Results of overlaying the forest cover map with the leakage belt boundaries
Frequency of monitoring/recording	At every verification period
Value monitored	GIS file of the leakage belt
Monitoring equipment	Computer and QGIS 2.18 and ArcGIS 10.5 software
QA/QC procedures to be applied	Projection system and datum was kept consistent. Clear and detailed documentation and independent desk review to assure consistency and accuracy of the GIS procedures
Purpose of the data	Calculation leakage.
Calculation method	Spatial Analysis tool (tabulate area in zonal statistics toolbox)
Comments	n/a

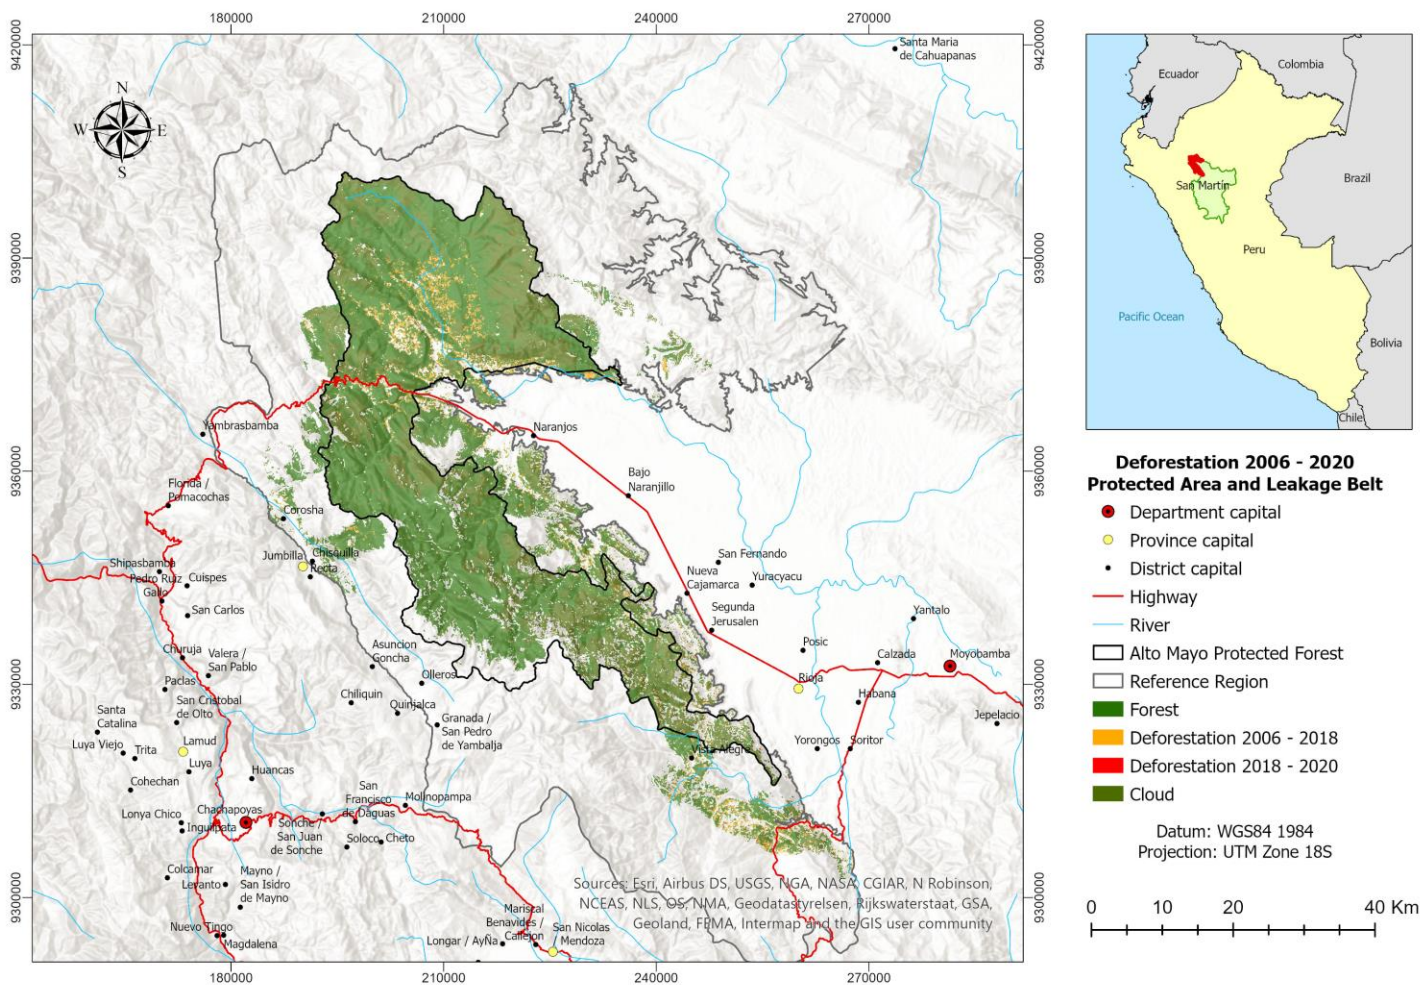


Figure 3 -Deforestation map 2006-2020. It shows the observed changes between forest and non-forest classes within the project area and leakage belt

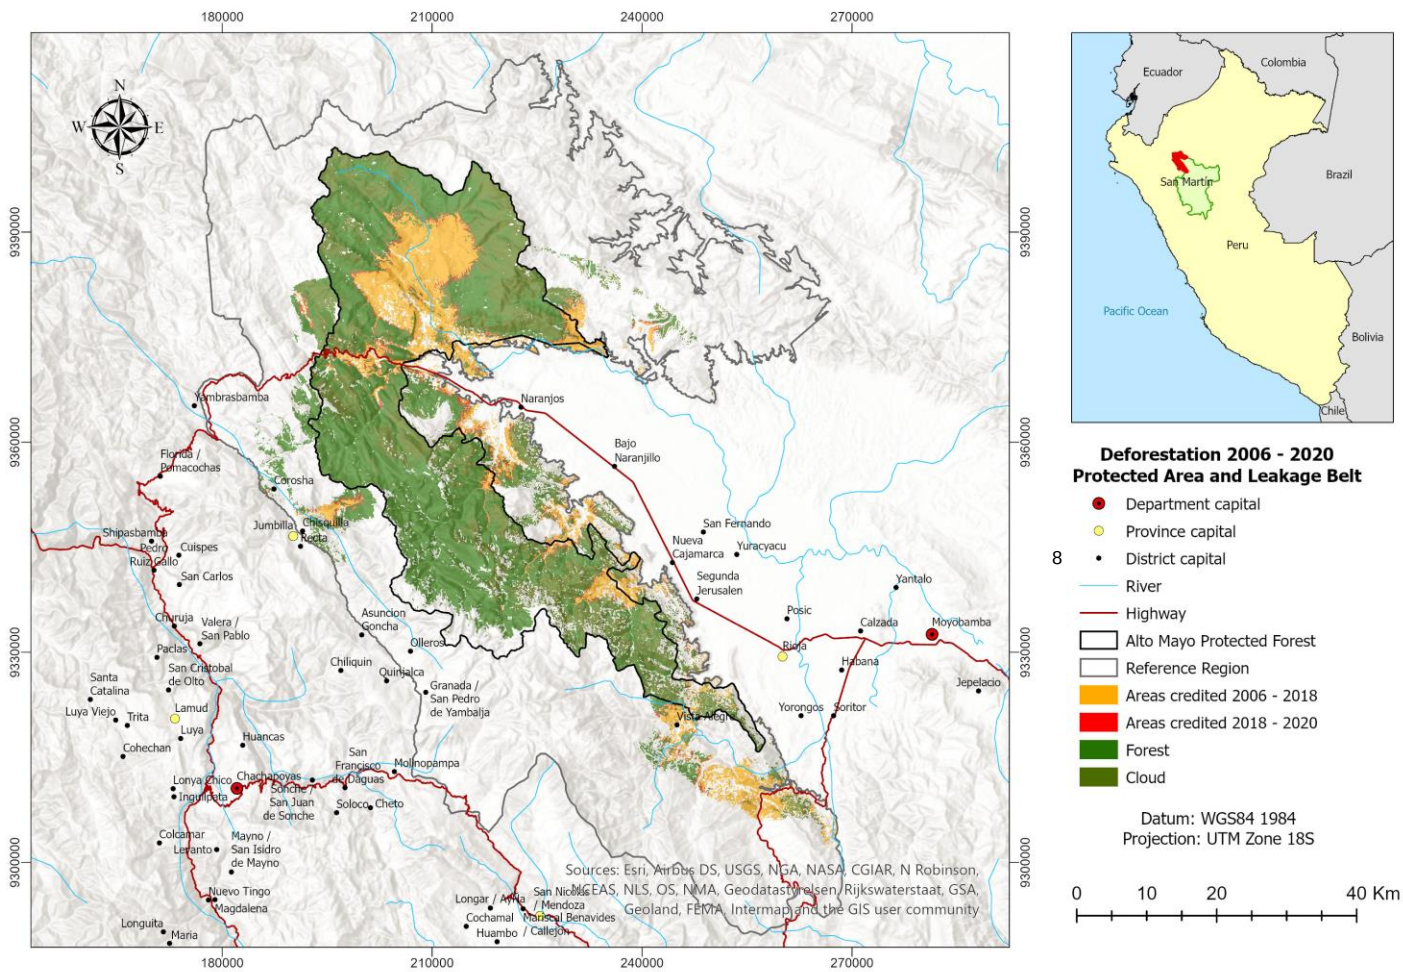


Figure 4 - Map of cumulative areas credited for the 2018-2020 monitoring period

3.1.3 Monitoring Plan

The project followed all the process and schedule described in the monitoring plan. There was no deviation or changes of the methodology or monitoring plan – excepted the ones described in Section 2.2.4. A full description of the data management plan of AMCI's monitoring plan is provided in the Section 4.3 of CVS PDD, and the technical description of the monitoring process is detailed in the VCS PDD's Methodological Annex (part 3). These two documents describe:

- The organizational structure, responsibilities and competencies of the personnel that carried out the monitoring activities.
- The methods used for generating/measuring, recording, storing, aggregating, collating and reporting the data on monitored parameters.
- The procedures used for handling any internal auditing performed and any non-conformities identified.
- The implementation of sampling approaches, including target precision levels, sample sizes, sample site locations, stratification, frequency of measurement and QA/QC procedures.

Below we summarize the main technical steps of the land cover and change monitoring procedures. In order to assure consistence and high quality analysis the monitoring plan closely followed the methods, rules, and procedures used in the last monitoring period and specified in Conservation International's standard change detection methodology (Sup.Inf_MIR_08a+b).

1. The land cover and change maps were produced following the technical steps described below and detailed in Sup.Inf_MIR_08, including quality assurance procedures. Accuracy assessment as described in Steps 2.4 and 2.5 of Part 2 of the AMCI Methodological Annex was performed, and the results are detailed in the Sup.Inf_MIR_09. Sentinel2 images of 2 dates in 2020 were acquired from the Copernicus Space Component Data Access Portal of the European Spatial Agency, and merged to ensure minimal cloud cover. Multiple images were used in the verification to fill areas obscured by clouds, as listed in MR Table 1.a:

MR Table 1.a. Data used for monitoring LU/LC change analysis

Vector (Satellite or airplane)	Sensor	Resolution		Coverage (km ²)	Acquisition date (DD/MM/YY)	Scene or point identifier	
		Spatial	Spectral			Path / Latitude	Row / Longitude
Sentinel-2	MSI	10m	0.4 – 2.5 µm	100 x 100 km	7-Jun-20	T18MTU	T18MTU
Sentinel-2	MSI	10m	0.4 – 2.5 µm	100 x 100 km	7-Jun-20	T17MTU	T17MTU
Sentinel-2	MSI	10m	0.4 – 2.5 µm	100 x 100 km	28-May-20	T18MTU	T18MTU
Sentinel-2	MSI	10m	0.4 – 2.5 µm	100 x 100 km	28-May-20	T17MTU	T17MTU
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	12-Jul-20	151117	1004
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	12-Jul-20	151116	1004
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	12-Jul-20	151115	1004
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	12-Jul-20	151005	1013
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	12-Jul-20	151003	1013
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	25-Mar-20	145916	0e0f
Planet	PlanetScope	3m	0.45 – 0.86 µm	8 x 25 km	25-Mar-20	145917	0e0f

2. All of the images used in the analysis were cloud masked and orthorectified.
3. The images were classified in two-date image stacks (2018/2020) using decision tree analysis (RandomForest), using the following sub-steps;
 - a. Map classes include: 1=forest, 2=non-forest, 4=water, and 5=cloud.
 - b. Training sites were selected to represent both change and non-change areas.
 - c. Training sites included numerous sub-classes for each land-cover and change class, to incorporate the full range of spectral variability within the image.
4. The final classification was filtered in QGIS using a neighborhood majority filter 3x3. Then the map product was processed to eliminated patches less than 0.5-hectare in size.
5. Areas of change from forest to non-forest were extracted from the final 2018-2020 land-cover change map and overlaid on the forested area from the original 2018 classification to create the updated 2020 land-cover map. Thereby minimizing the amount of erroneous transitions and reducing the map agreement error.
6. Areas of cloud in the 2018 land cover map were updating using a two-date images stack form 2006-2020, and then updated following the same methods described in steps 3-5. Areas that were obscured by clouds in 2020 were excluded and will be updated in future monitoring periods.

The project used high resolution images (3 m) circa 2020 and park ranger patrols to validate the final land cover change. This process was used to measure the omissions from the final forest cover/change map. In order to assess the commissions or false alarms (i.e. areas deforested in the classification, but not in the field), 200 points were distributed over the observed 2018-2020 deforestation, however, some points fell out the image range and 171 points checked on the high-resolution images. These points were allocated randomly using a GIS tool. The GIS Specialist did a visual interpretation of the classes (forest and non-forest) observed in the high-resolution images for each of the pointed and recorded in a excel spreadsheet (Sup.Inf_MIR_09). The result of the error matrix (or confusion matrix) was above the required 80% accuracy from the VM0015 methodology. The estimated overall accuracy of the final 2018-2020 classification was 89.5%. See Table 3 for the confusion matrix. In addition, the accuracy of commission (or false alarms) was 84.7% (72 out of 85 points) and omission accuracy (or misses) was 93.5% (72 out of 77).

Table 3 - Overall accuracy of land change (2018-2020) matrix (confusion matrix).

LC Classes - Map	LC Classes - Ground		LC Classes - Total	User's Accuracy
	Forest	Non-Forest		
Forest	81	5	86	94.19%
Non-Forest	13	72	85	84.71%
LC Classes - Map total	94	77	171	
Producer's accuracy	86.17%	93.51%	Overall Accuracy of Land Change Map (153/171) = 89.5%	

3.1.4 Dissemination of Monitoring Plan and Results (CL3.2)

The results of the monitoring period were widely publicized in the local language to the communities and other stakeholders, and comments received were incorporated in the report. In addition, the Project Implementation Report was submitted to CCBA for a 30-day public comment period, and any relevant observation will be addressed.

3.2 Quantification of GHG Emission Reductions and Removals

3.2.1 Baseline Emissions

The baseline carbon stock changes in the initial (pre-deforestation) forest classes in the project area during the monitoring period are shown in MR Table 02.a. The baseline carbon stock changes in the single final (post-deforestation) non-forest class considered by the project during the monitoring period are shown in MR Table 02.b. The total baseline carbon stock changes in the project area during the monitoring period are shown in MR Table 02.c. Note that, areas covered by clouds in the 2020 land cover map have been temporarily excluded from this monitoring report and therefore the numbers in the MR Tables 02.a, b and c differ slightly from those shown in VM Tables 15.a, b, and c, respectively.

MR Table 02.a. Baseline carbon stock changes in pre-deforestation (forest) classes in the project area during the monitoring period (2020 cloud free)

Project year t	Carbon stock changes in initial (pre-deforestation) forest classes in the project area						Total carbon stock changes in initial forest classes	
	ID_{icl}	pre-montane	ID_{icl}	cloud	ID_{icl}	dwarf	annual	cumulative
	$ABSLPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$ABSLPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$ABSLPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$\Delta CBSLPA_i$ tCO ₂ -e	$\Delta CBSLPA_i$ tCO ₂ -e
2019	0	399	1,319	520	2	88	685,383	685,383
2020	0	399	1,339	520	3	88	695,814	1,381,198

MR Table 02.b. Baseline carbon stock changes in post-deforestation (non-forest) classes in the project area during the monitoring period (2020 cloud free)

Project year t	Carbon stock changes in final (post-deforestation) non-forest classes in the project area		Total carbon stock changes in final non-forest classes	
	ID_{fcl}	= non-forest	annual	cumulative
	$ABSLPA_{fcl,t}$ ha	$Ctot_{fcl,t}$ tCO ₂ -e ha ⁻¹	$\Delta CBSLPA_f$ tCO ₂ -e	$\Delta CBSLPA_f$ tCO ₂ -e
2019	1,320	93	123,192	123,192
2020	1,342	93	125,190	248,382

MR Table 02.c. Total baseline carbon stock changes in the project area during the monitoring period (2020 cloud free)

Project year	Total carbon stock changes in	Total carbon stock changes in	Total baseline carbon stock
--------------	-------------------------------	-------------------------------	-----------------------------

<i>t</i>	initial forest classes		final non-forest classes		changes in the project area	
	annual $\Delta CBSLPA_i$ tCO ₂ -e	cumulative $\Delta CBSLPA_i$ tCO ₂ -e	annual $\Delta CBSLPA_f$ tCO ₂ -e	cumulative $\Delta CBSLPA_f$ tCO ₂ -e	annual $\Delta CBSLPA_t$ tCO ₂ -e	cumulative $\Delta CBSLPA$ tCO ₂ -e
2019	685,383	685,383	123,192	123,192	562,192	562,192
2020	695,814	1,381,198	125,190	248,382	570,624	1,132,816

3.2.2 Project Emissions

The ex-post actual carbon stock changes in the initial (pre-deforestation) forest classes in the project area during the monitoring period are shown in MR Table 03.a. The ex-post actual carbon stock changes in the single final (post-deforestation) non-forest class considered by the project during the monitoring period are shown in MR Table 03.b. The total ex-post actual carbon stock changes in the project area during the monitoring period are shown in MR Table 03.c. In addition, areas that were temporarily excluded from the previous monitoring period (2006-2012, 2012-2014, 2014-2016, or 2016-2018) but observed in 2020 were included in this report, and any deforestation observed was attributed to this monitoring period. The observed deforestation for the monitoring period was assumed to be equally distributed per year.

MR Table 03.a. Ex-post actual carbon stock changes in pre-deforestation (forest) classes in the project area during the monitoring period (2020 cloud free)

Project year <i>t</i>	Carbon stock changes in initial (pre-deforestation) forest classes in the project area						Total carbon stock changes in initial forest classes	
	<i>ID_{icl}</i>	pre-montane	<i>ID_{icl}</i>	cloud	<i>ID_{icl}</i>	dwarf	annual	cumulative
	$APSPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$APSPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$APSPA_{icl,t}$ ha	$Ctot_{icl,t}$ tCO ₂ -e ha ⁻¹	$\Delta CPSPA_i$ tCO ₂ -e	$\Delta CPSPA_i$ tCO ₂ -e
2019	1	399	170	520	25	88	90,694	90,694
2020	1	399	170	520	25	88	90,694	181,389

MR Table 03.b. Ex-post carbon stock change in post-deforestation (non-forest) classes in the project area during the monitoring period (2020 cloud free)

Project year <i>t</i>	Carbon stock changes in final (post-deforestation) non-forest classes in the project area		Total carbon stock changes in final non-forest classes	
	<i>ID_{fcl}</i>	= non-forest	annual	cumulative
	$APSPA_{fcl,t}$ ha	$Ctot_{fcl,t}$ tCO ₂ -e ha ⁻¹	$\Delta CPSPA_f$ tCO ₂ -e	$\Delta CPSPA_f$ tCO ₂ -e
2019	195	93	18,237	18,237
2020	195	93	18,237	36,474

MR Table 03.c. Total ex-post carbon stock change in the project area during the monitoring period (2020 cloud free)

Project year t	Total carbon stock changes in initial forest classes		Total carbon stock changes in final non-forest classes		Total ex-post carbon stock changes in the project area	
	annual $\Delta CPSPA_{i,t}$ tCO ₂ -e	cumulative $\Delta CPSPA_i$ tCO ₂ -e	annual $\Delta CPSPA_{f,t}$ tCO ₂ -e	cumulative $\Delta CPSPA_f$ tCO ₂ -e	annual $\Delta CPSPA_t$ tCO ₂ -e	cumulative $\Delta CPSPA$ tCO ₂ -e
2019	90,694	90,694	18,237	18,237	72,457	72,457
2020	90,694	181,389	18,237	36,474	72,457	144,915

3.2.3 Leakage

The total baseline carbon stock changes in the leakage belt during the monitoring period (2020 cloud free) are shown in MR Tables 04.a, b, and c. In addition, areas that were temporarily excluded from the previous monitoring period (2006-2012, 2012-2014, 2014-2016 or 2016-2018) but observed in 2020 were included in this report, and any deforestation observed was attributed to this monitoring period. The observed deforestation for the monitoring period was assumed to be equally distributed per year.

MR Table 04.a. Baseline carbon stock changes in initial (pre-deforestation) forest classes in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Baseline carbon stock changes in initial (pre-deforestation) forest classes in the leakage belt						Total carbon stock change in initial forest classes	
	ID_{icl} pre-mont		ID_{icl} cloud		ID_{icl} dwarf		annual	cumulative
	$ABSLLK_{icl,t}$	$Ctot_{icl,t}$	$ABSLLK_{icl,t}$	$Ctot_{icl,t}$	$ABSLLK_{icl,t}$	$Ctot_{icl,t}$	$\Delta CBSLLK_i$	$\Delta CBSLLK_i$
	ha	tCO ₂ -e ha ⁻¹	ha	tCO ₂ -e ha ⁻¹	ha	tCO ₂ -e ha ⁻¹	tCO ₂ -e	tCO ₂ -e
2019	0	399	1,183	520	90	88	622,331	622,331
2020	0	399	1,139	520	95	88	600,127	1,222,458

MR Table 04.b. Baseline carbon stock changes in final (post-deforestation) non-forest classes in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Baseline carbon stock changes in final (post-deforestation) non-forest classes		Total carbon stock change in final non-forest classes	
	$ID_{fcl} = 1$		annual	cumulative
	$ABSLLK_{fcl,t}$ ha	$Ctot_{fcl,t}$ tCO ₂ -e ha ⁻¹	$\Delta CBSLLK_{f,t}$ tCO ₂ -e	$\Delta CBSLLK_f$ tCO ₂ -e
2019	1,272	93	118,683	118,683
2020	1,234	93	115,114	233,797

MR Table 04.c. Total net baseline carbon stock change in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Total carbon stock change in initial forest classes		Total carbon stock change in final non-forest classes		Total net baseline carbon stock change in the leakage belt	
	annual $\Delta CBSLLK_i$ tCO ₂ -e	cumulative $\Delta CBSLLK_i$ tCO ₂ -e	annual $\Delta CBSLLK_f$ tCO ₂ -e	cumulative $\Delta CBSLLK_f$ tCO ₂ -e	annual $\Delta CBSLLK_t$ tCO ₂ -e	cumulative $\Delta CBSLLK_t$ tCO ₂ -e
2019	622,331	622,331	118,683	118,683	503,648	503,648
2020	600,127	1,222,458	115,114	233,797	485,012	988,661

The total ex-post actual carbon stock changes in the leakage belt during the monitoring period (2020 cloud free) are shown in MR Tables 05.a, b, and c.

MR Table 05.a. Ex-post carbon stock changes in initial (pre-deforestation) forest classes in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Ex-post actual carbon stock changes in initial (pre-deforestation) forest classes in the leakage belt						Total ex-post carbon stock changes in initial forest classes	
	ID_{icl} $APSLK_{icl,t}$ ha	pre-mont $C_{tot_{icl,t}}$ tCO ₂ -e ha ⁻¹	ID_{icl} $APSLK_{icl,t}$ ha	= cloud $C_{tot_{icl,t}}$ tCO ₂ -e ha ⁻¹	ID_{icl} $APSLK_{icl,t}$ ha	= dwarf $C_{tot_{icl,t}}$ tCO ₂ -e ha ⁻¹	annual $\Delta CPSLK_i$ tCO ₂ -e	cumulative $\Delta CPSLK_i$ tCO ₂ -e
2019	0	399	63	520	1	88	33,056	33,056
2020	0	399	63	520	1	88	33,056	66,112

MR Table 05.b. Ex-post actual carbon stock changes in final (post-deforestation) non-forest classes in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Ex-post actual carbon stock changes in final (post-deforestation) non-forest classes in the leakage belt		Total ex-post carbon stock changes in final non-forest classes	
	ID_{icl} $APSLK_{icl,t}$ ha	= non-forest $C_{tot_{icl,t}}$ tCO ₂ -e ha ⁻¹	annual $\Delta CPSLK_f$ tCO ₂ -e	cumulative $\Delta CPSLK_f$ tCO ₂ -e
2019	64	93	6,012	6,012
2020	64	93	6,012	12,024

MR Table 05.c. Total ex-post actual carbon stock changes in the leakage belt during the monitoring period (2020 cloud free)

Project year t	Total ex-post carbon stock changes in initial forest classes		Total ex-post carbon stock changes in final non-forest classes		Total ex-post carbon stock changes in the leakage belt	
	annual $\Delta CPSLK_i$ tCO ₂ -e	cumulative $\Delta CPSLK_i$ tCO ₂ -e	annual $\Delta CPSLK_f$ tCO ₂ -e	cumulative $\Delta CPSLK_f$ tCO ₂ -e	annual $\Delta CPSLK_t$ tCO ₂ -e	cumulative $\Delta CPSLK_t$ tCO ₂ -e
2019	33,056	33,056	6,012	6,012	27,044	27,044
2020	33,056	66,112	6,012	12,024	27,044	54,088

The total ex-post actual net carbon stock changes in (i.e. above the baseline) in the leakage belt during the monitoring period are shown in MR Table 06. According to the methodology, if the cumulative sum of ΔCLK_t within a fixed baseline period is > 0 , ΔCLK_t shall be set to zero. Therefore, no credits were discounted due to leakage during this monitoring period.

MR Table 06. Total net carbon stock changes in the leakage belt in the project scenario above the baseline during the monitoring period (2020 cloud free)

Project year t	Total baseline carbon stock changes in the leakage belt		Total ex-post actual carbon stock changes in the leakage belt		Total ex-post actual net carbon stock changes in the leakage belt*	
	annual $\Delta CBSLLK_t$ tCO ₂ -e	cumulative $\Delta CBSLLK$ tCO ₂ -e	annual $\Delta CPSLK_t$ tCO ₂ -e	cumulative $\Delta CPSLK$ tCO ₂ -e	annual ΔCLK_t tCO ₂ -e	cumulative ΔCLK tCO ₂ -e
2019	503,648	503,648	27,044	27,044	476,604	476,604
2020	485,012	988,661	27,044	54,088	457,968	934,573

3.2.4 Net GHG Emission Reductions and Removals

The ex-post estimated net anthropogenic GHG emission reductions were estimated similarly to the ex-ante calculation using the equation below (adapted from Equation 23 of the VM0015 methodology)

$$\Delta REDD_t = (\Delta CBSLPA_t) - (\Delta CPSPA_t) - (\Delta CLK_t + ELK_t) \quad \text{Eq (23). Where:}$$

$\Delta REDD_t$	Ex-post estimated net anthropogenic GHG emission reduction attributable to the project activity at year t ; tCO ₂ e
$\Delta CBSLPA_t$	Sum of baseline carbon stock changes in the project area at year t ; tCO ₂ e
$\Delta CPSPA_t$	Sum of ex post estimated actual carbon stock changes in the project area at year t ; tCO ₂ e
ΔCLK_t	Sum of ex post estimated leakage net carbon stock changes at year t ; tCO ₂ e
ELK_t	Sum of ex post estimated leakage emissions at year t ; tCO ₂ e
T	1, 2, 3 ... T , a year of the proposed crediting period; dimensionless

The ex-post estimation of total net GHG emissions reductions generated by the project and the calculation of ex-post Verified Carbon Units (VCUs) generated in the monitoring period of 2018-2020 are summarized in MR Table 07a. All emission reductions from this reporting period will be issued with the vintage dates of 15 June 2018 – 14 June 2020 (MR Table 07b).

MR Table 07a. Annual ex post estimated net anthropogenic GHG emission reductions ($\Delta REDD_t$) and Voluntary Carbon Units (VCU_t)

Project year t	Baseline carbon stock changes		Ex post project carbon stock changes		Ex post net carbon stock changes		Ex post leakage carbon stock changes		Ex post net anthropogenic GHG emission reductions		Ex post buffer credits*		Ex post VCUs tradable	
	annual $\Delta CBSLPA_t$ tCO ₂ -e	cumulative $\Delta CBSLPA$ tCO ₂ -e	annual $\Delta CPSPA_t$ tCO ₂ -e	cumulative $\Delta CPSPA$ tCO ₂ -e	annual $\Delta CPSPA_t$ tCO ₂ -e	cumulative $\Delta CPSPA$ tCO ₂ -e	annual ΔCLK_t tCO ₂ -e	cumulative ΔCLK tCO ₂ -e	annual $\Delta REDD_t$ tCO ₂ -e	cumulative $\Delta REDD$ tCO ₂ -e	annual VBC_t tCO ₂ -e	cumulative VBC tCO ₂ -e	annual VCU_t tCO ₂ -e	cumulative VCU tCO ₂ -e
2019	562,192	562,192	72,457	72,457	489,734	489,734	0	0	489,734	489,734	48,974	48,974	440,760	440,760
2020	570,624	1,132,816	72,457	144,915	498,167	987,901	0	0	498,167	987,901	49,817	98,791	448,350	889,110

Ex-post buffer credits are calculated based on a 10% Risk Factor (RF) attributed to the project based on the VCS non-permanence risk tool

MR Table 07b. Ex post estimated net anthropogenic GHG emission reductions ($\Delta REDD_t$) and Voluntary Carbon Units (VCU_t) for the reporting period

Project year t	Baseline carbon stock changes total $\Delta CBSLPA$ tCO ₂ -e	Ex post project carbon stock changes total $\Delta CPSPA$ tCO ₂ -e	Ex post leakage carbon stock changes total ΔCLK tCO ₂	Ex post net anthropogenic GHG emission reductions total $\Delta REDD$ tCO ₂ -e	Ex post buffer credits* total VBC tCO ₂ -e	Ex post VCUs tradable total VCU tCO ₂ -e
2018-2020	1,132,816	144,915	0	987,901	98,791	889,110

3.3 Optional Criterion: Climate Change Adaptation Benefits

Not applicable. The project did not include the optional climate change adaptation benefits criterion in the project description.

4 COMMUNITY

4.1 Net Positive Community Impacts

The methodological framework used to estimate the net positive impact of the project on communities is detailed in the *Protocolo de Monitoreo Socioeconomico* and are based on the results chain analysis of the project strategies. The indicators were designed to measure the positive and negative impact inside and outside the project zone. The Table 4 summarizes the expected impacts on the communities.

Table 4 - List of impact on communities inside and outside the project

	Expected Socioeconomics Impacts	
	Positives	Negatives
Inside Project Zone	1. Governance of the AMPF is strengthened. 2. Production systems of the local population are improved and coffee associations in connection to special markets are promoted. 3. Capacity building and knowledge is generated among local people for sustainable management of their production systems. 4. Living conditions of the local population in harmony with the objectives of the AMPF are improved. 5. Economic alternatives for the population are generated through conservation actions aligned with AMPF management. 6. Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of population in the project zone. 7. Natural resources within the BPAM are sustainably managed by the local population. 8. The partnership between the local population and the AMPF Head Office are empowered for conservation.	9. Decrease economic opportunities from illegal activities 10. Decrease provision of basic services within the AMPF 11. Improved control over the expansion of the agricultural frontier 12. Less support from land holders to their families in the area of origin
Outside Project	13. Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of the population outside the project zone. 14. Technology is transferred to improve coffee production systems outside project zone. 15. New projects for sustainable development of the Alto Mayo watershed are leverage.	16. Demand for conventional coffee practices are displaced to native communities increasing unsustainable land use in areas rented by them. 17. Customary uses of the native communities are affected by increased surveillance and control program of the NPA.

Note that, in order to comply with the new VCS-CCBS reporting template, the impacts were numbered in

a sequential order in Table 4, however might not be listed in a logical sequence in the sub-sections. The Table 4 follows the assumptions and design developed in the monitoring plan.

4.1.1 Community Impacts (CM1.1)

Impact 1: Governance of the AMPF is strengthened

The strengthening of governance within the framework of the project is mainly focused on supporting the effectiveness of the AMPF Head Office and consolidating the institutionality of the Management Committee. In this sense, SERNANP has continued to be supported by financial resources through a donation agreement of 3.3 million soles which are used for equipment, food and logistic expenses in patrol activities, conditioning of checkpoints, payment of park guards, technical and administrative personnel, and for office expenses. These resources, in addition to the resources directly allocated by SERNANP, contribute to an effective work for the sustainability of the AMPF (Sup.Inf_MIR_01).

The Management Committee continued to receive financial support to carry out its executive meetings and assemblies, which deal with important issues for the AMPF and which purpose is to provide support for the correct decision making of the AMPF Head Office. During this period, 4 assemblies and 8 executive committee meetings were held.

In this last period, support has been given to the AMPF Head Office and the Management Committee to specify the agreements and commitments with public institutions at the regional level. The Presidency of the Council of Ministers, as well as the Ministries of the Interior and the Environment, in order to strengthen the presence of the State in the NPA, support the surveillance and control joint actions of the park rangers team and the members of the National Police. It is worth mentioning that, the CI team provides continuous technical advice to the AMPF Head Office and the Management Committee to make their participation effective in the different public/private spaces around the NPA.

The agreement between SERNANP and the Municipality of Rioja to explore public investment projects in the AMPF and its buffer zone stands out. The project has generated rapprochement with the Regional Government of San Martín through the Office for the Promotion of Public and Private Investment for the commercial articulation of dragon fruit with private companies, and that would benefit the subscribers of conservation agreements.

The reactivation of the commonwealth of the Alto Mayo valley is being supported. This involves an articulation by the Local Government of Rioja that will favor the design of larger projects that include the ecosystem services of the AMPF that will later be implemented with public funds. This articulation also includes other municipalities in the sub basin of Mayo.

CI has promoted agreements with the Research Institute of the Peruvian Amazon (IIAP) and the University of Applied Sciences to tackle cooperation actions around the research priorities in the AMPF.

Technical documents for the management of the NPA have been designed last monitoring period were approved by the Head Office in this period. The implementation of these are consolidating the social processes in the AMPF. Some of the most important documents are: the Research Strategy

(Sup.Inf_MIR_10), the Plan for the Management of Renewable Resources (Sup.Inf_MIR_11), the Community Development Plan (Sup.Inf_nprt_17), and the Plan for Touristic and Recreational Use (Sup.Inf_MIR_12), the Life Plan for the Community of Nueva Zelandia (Sup.Inf_MIR_23) was also designed in this period. The design of projects that will benefit the Cooperative and the tourism ventures in Urcuchaqui are in progress. Public funding through state programs is expected.

It should be mentioned that coordination is carried out with the Regional Environmental Authority of the Regional Government of San Martín for the setup of orchid nurseries, which were arranged as a result of a rescue strategy in old coffee plantations.

Impact 2: Production systems of the local population are improved and coffee associations in connection to special markets are promoted.

The COOPBAM was created at the end of 2014. It is the first producer cooperative within a NPA in Peru to subscribe conservation agreements. This demonstrates that the cooperative is compatible with the creation objectives of the AMPF.

The COOPBAM, with the support of an allied cooperative, exported its first production to Denmark in 2015. Around 14 thousand kilos of coffee generated an income close to \$58 thousand. However, when exported through another cooperative, the net profits of the COOPBAM were minimal. This made the partners react and decide to obtain organic and fair-trade certifications as well as direct export rights. Therefore, during the 2016 campaign, the COOPBAM directly exported around 45 thousand kg of coffee of high quality achieving an income superior to \$ 185 thousand. This meant breaking down the barriers that kept the cooperative from growing. The biggest commercial milestone of 2016 was the articulation of a coffee container acquired by OPTCOP, importer of Joffrey's Coffee and Tea Company, the exclusive coffee supplier of the Disney theme parks, where the COOPBAM coffee is sold.

The 2017 campaign capitalized on all the lessons learned during the first years of the COOPBAM. More than 250% was exported in quantity (113 thousand kilos) and 266% of income (\$ 492 thousand) was obtained. However, the most outstanding aspect of that campaign was the commercial articulation to markets of greater quality demand such as Red Fox and the consolidation of a strong commercial relationship with HACOFCO, a German importer that bought a container in 2016, three in 2017 and has already bought four containers during 2018 with an intention of additional purchase depending on the production capacity. In conclusion, 2017 has been the year for the business growth of the COOPBAM.

Nine containers of coffee (over 173 tons) were exported in 2018 and 13 in 2019 which made a total of 248 tons of green coffee. It should be noted that the English company FALCON COFFEES has been participating since 2018. This company bought 80% of the coffee production produced by the subscribers of conservation agreements during 2019. Also, in this period, 44,781 kilograms of high-quality coffee (2.36 containers) was exported by RED FOX. This amount represents the highest volume exported to date.

Also, the COOPBAM membership has increased. During the last verification period (2016-2018), only 280 subscribers were part of the cooperative. In 2020, the membership reached 463 subscribers. In all these

years, the organic certification has been renewed, maintaining an average of more than 800 hectares where coffee is produced under high socio-environmental standards.

In addition to the amount of coffee exported (more than 421 tons) and the revenues generated (more than \$ 1.6 million), the COOPBAM's main contribution to the management of the NPA is to share their experience with the local population and the public and private institutions and to demonstrate that the model proposed by the project, that is, to increase the welfare of families by conserving the AMPF, is possible and generates significant benefits and contributions to the development of this part of the region.

As previously mentioned, the project has been supporting the consolidation and sustainability of the COOPBAM, whose actions have focused on the identification of competitive funds to invest in infrastructure, and on the design of their management instruments. All this combined will strengthen the operational and commercial management activities.

Impact 3: Capacity building and knowledge is generated among local people for sustainable management of their production systems.

A great effort and budget of the project is devoted to the capacity building on sustainable practices, as these are considered a core strategy to change behavior and mitigate the deforestation. During 2018-2020 period there have been 53 training practices on the sustainable improvement of coffee health families, meliponiculture and pitahaya cultivation with 1,800 attendees and over 4,300 hours of technical assistance in the same period.

As result, 93 of subscribers mention that they practiced at least 2 organic management techniques in their farms (e.g. organic fertilization, organic control of pests and diseases, pruning and post-harvesting management), and 98 of subscribers mentioned they learned this sustainable practice from the conservation agreements. The subscribers are also reinvesting their revenues in organic production – the proportion of subscribers has increased from 19% in 2014 to 42.5% in 2020. The average amount invested by each subscriber was S/.826 .

Moreover the project continues to observe an increase in adopting best practices compared with the previous monitoring period in several metrics, including: use of solar tents for drying their coffee, production and selling of organic coffee, implementation of agroforestry systems, decrease or termination in the use of chemicals (Sup.Inf_MIR_01).

In terms of sales, coffee with organic and fair-trade certification, exported directly through the COOPBAM, was sold at a price between US \$ 190.00 and US \$ 250, per quintal in this period. In general, the average price has remained the same in comparison to previous years. The most important thing to notice is the increase in quality coffee production that is produced by farmers and that helps to improve the family economy.

The sales volume reached in 2018 was 4,210 QQ, in 2019, 5,395 QQ were sold 28% more than in the previous year, and in 2020, 5,175 QQ have been stockpiled so far.

Impact 4: Living conditions of the local population in harmony with the objectives of the AMPF are improved.

Since the first monitoring period, the project shown a positive impact improving the living conditions of people living in the AMPF. Also, all economic activities promoted by the project to improve living conditions of local population are aligned with the AMPF conservation objectives.

Since the reporting period 2014-2016, the project started using the Progress out Poverty Index (PPI)¹⁴ to quantify the improvement of living conditions of the AMPF settlers. In the previous monitoring period 2016-2018 the index showed that 46.7% of the AMPF beneficiaries is living below the poverty line.

This period PPI showed that 41% of the AMPF beneficiaries is living below the poverty line. According to the answers gave by the project beneficiaries, 46% of them perceive that their economic well-being improved and 75% of them associate this to the signing of conservation agreements. Also, 88% of beneficiaries have access to primary schools and 53% have access to secondary schools. Additionally, 81 % have access to a dispensary, health center or medical post. Access to drinking water is still a challenge, because only 8% of subscribers have access. Nevertheless, 21% of subscribers mention this service improved with the project intervention

Impact 5: Economic alternatives for the population are generated through conservation actions aligned with AMPF management.

During this monitoring period, the impact generated by economic alternatives and conservation actions wages continues. Through the promotion of economic alternatives on conservation actions 309 wages were generated and S/. 43,000 (soles) were paid to 135 people, including subscribers and their families. Is important to mention that these numbers include conservation activities such as reforestation, nursery activities and patrolling and are additional incomes to the ones generated through the increase of crop productivity due to the implementation of best practices from the conservation agreements.

Impact 8: The partnership between the local population and the AMPF Head Office are empowered for conservation

The environmental education and awareness actions for the beneficiaries of the project were led by the AMPF Head Office which, with the support of a group of volunteers called *Hinchas de la Conservación* (Conservation Fans), held workshops, talks and fairs in schools and public spaces. This helped to promote the wealth of natural resources that the Protected Area has.

An interaction with more than 3,000 people was achieved thanks to these actions. It was mostly child population who received the knowledge through dynamics and interactive games with materials developed by a specialist in environmental education: puzzles and *Faunibpam* (a notebook to color that highlights the species and wildlife that represents the AMPF).

¹⁴ Further information about the Progress out of Poverty Index is available at <http://www.progressoutofpoverty.org/>

Strategic actions are implemented taking the Environmental Education Plan into account which establishes prior coordination with the Units of Local Educational Management, with whom SERNANP has also signed letters of intent to strengthen inter-institutional cooperation in the Protected Forest. The purpose is to insert environmental topics throughout the year in the school curricula established by the Ministry of Education. There is also an environmental project focused on the production of vegetable gardens. The schools that were benefited during this period were those located in the towns of Juan Velasco, Alto Valle and Santa Rosa del Mirador, where more than 1,300 students participated.

The environmental education and awareness talks are also given to the adult population, who wants to continue strengthening the change in attitude and the good environmental practices. The members of the National Police of Peru have also been trained as they are who provide support to SERNANP during patrols.

4.1.2 Net Positive Community Well-Being Impacts (CM1.1)

Overall, the net socioeconomic impacts in the project area are quite positive. The successful implementation of conservation agreements in the area has enabled a transition to more sustainable practices and livelihoods, thus reducing the potential negative impacts associated the elimination of illicit activities – namely, a decrease in overall economic activity in the area in the form of both wages and services, in this case,

Impact 9: Economic opportunities arising from illegal activities are decreased

By 2020, subscribers and non-subscribers continue reducing their illegal economic activities in the AMPF such as hunting, wood loading and chainsaw operating. The field survey revealed that of the total number of subscribers who quit doing some type of activity in the AMPF, 38% quit doing illegal activities. The same trend occurs with non-subscribers.

It is important to mention that 85% of the income generated by subscriber's wages comes from legal and conservation activities.

Impact 10: Provision of basic services within the AMPF is decreased

Contrary of what was supposed to happen because of the enforcement of current legislation and regulations regarding natural protected areas, access to basic services such as education and health increased. To ensure compliance of legislation without decreasing basic services provision to the AMPF population, Conservation International and the AMPF Head Office develop a strategy to provide basic services in areas designated by law and complementary activities and alliances that allow improving access to these services specially in sectors where conservation agreements are being implemented and the population have a commitment to preserve the AMPF.

In 2019, the San Martín Regional Government, through the Alto Mayo Special Project (PEAM), completed the building of the Field School in the town of Sol de Oro, whose facilities are used to promote environmental education and good productive practices in the local population. The PEAM has handed over the school to SERNANP so that park rangers can use it, improving their accommodation and staying conditions in this sector for patrolling and social outreach work.

It should be noted that CI and the Head Office have maintained coordination with the Regional Government to evaluate the investment package in the Nucleo Funcional de Aguas Verdes, where families located within the AMPF are provided with basic services such as education and health in accordance with the territorial planning policy.

According to the field survey 99% of subscribers have access to primary schools and 66% have access to secondary schools. 81% have access to a dispensary, health center or medical post. Compared to information gathered on the previous period, the percentage of people that could access to these services increased considerably.

The Head Office has given a favorable technical opinion to 13 projects on water and sanitation and three on education services in the Buffer Zone of the AMPF. This undoubtedly contributes to the development of the well-being of the families that live in the Protected Area.

Is important to mention that one third of the subscribers mention access to basic services maintain the same or improved because of project implementation.

Access to drinking water is still an important challenge to be addressed. Only 8% of subscribers have access to drinking water.

Impact 11: Control over the expansion of the agricultural frontier is improved

The obligation generated by the signing of conservation agreements involves the commitment of not increasing the area for agricultural production, which is why the conservation agreement becomes the main tool to control this impact. Coffee technicians in the field are the ones who assist with enforcement of this commitment and therefore along with the park rangers are in the front line to halt the expansion of deforestation.

Since last monitoring period the number of conservation agreements with settlers has increased by 9%, meaning not only an increase of control for the expansion of the agricultural frontier but also an increase of the number of conservation allies in the forest to prevent new entrances to the area that could potentially install new agricultural plots.

Patrolling, performed by AMPF park rangers, is another way to monitor deforestation. During this period 793 patrolling entries 79 special patrolling and 714 routine patrolling were developed. The process of using unmanned aerial vehicles (drones) is being used to monitor Conservation Agreements areas. Almost 50% of the area have been overflight to create the base line that will allow the project to implement the monitoring of the forest cover in this area and the land use map.

These actions are complemented with a change in the agreements, going from family to community conservation agreements. This allows to monitor collective agreements and commitments related to the control of deforestation and bad management practices in crops such as coffee. SERNANP continues to coordinate with the community surveillance committees established in four towns in the buffer zone, which represents a strength to carry out joint patrol work within the AMPF area.

Impact 12: Families located in their area of origin receive less support from AMPF settlers

The project assumed that due to the project implementation and control of illicit activities the AMPF settlers would have less incomes and consequently less chances to send remittances to their families in their area of origin. However, with the increase of conservation agreements and the alignment with the AMPF objectives, illegal activities were reduced, but the settlers' incomes maintained or even increased. As observed in the field survey, over 31% of settlers perceived an improvement in their income coming from legal activities and 54% maintain their incomes. This evidences the development opportunities that families have in accordance with the conservation guidelines of the Protected Area.

4.1.3 Protection of High Conservation Values (CM1.2)

In general, all the population groups in the Alto Mayo basin (settlers, native communities, and peasant communities) make small scale use of different areas of the AMPF to meet some of their basic needs, characterizing HCVs. The areas within the AMPF, where resources such as firewood and construction materials are used and the collecting of different forest products is made, are concentrated in areas near the population centers of the main sub-basins where population is settled.

No negative impacts on the areas of community-related HCVs were observed. On the contrary, the strategies of project have been designed and implemented to ensure the achievement of the conservation objectives of the AMPF while delivering benefits to the communities. The strategies and activities implemented to mitigate the potential negative impact are described in detail in section 2.2.

Impact 6: Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of population in the project zone.

According to the 2018-2020 socio-economic survey, settlers have pointed out that water, fresh air, firewood, medicinal plants, and bush meat are the 5 most valued ecosystem services provided by the AMPF. The order of ecosystem services importance is the same as the previous reporting period. It is important to mention that all surveyed (100%) between subscribers and non-subscribers consider that the forests of AMPF are very important for their livelihoods and development.

Impact 7: Natural resources within the BPAM are sustainably managed by the local population.

The population settled in the AMPF still depends on natural resources to meet their housing and cooking needs. Firewood that is collected for cooking comes mainly from fallen trees, remnants of coffee plantations that are being restored or have been abandoned due to rust, or from remnants from agroforestry systems pruning. To further reduce the consumption of firewood the project has implemented a total of 293 improved cooking stoves since 2009, these stoves reduce firewood use by up to 52%. The technical team monitors the use of improved stoves to check the actual use they are given, and thereby measure the level of dependence on the increased use of forest resources. The results indicate that everyone makes correct use of the improved stoves. As a result, families breath less smoke and therefore, their health has improved.

Renewable resources with market potential have also been identified which are considered as opportunities in the livelihoods of families since they contribute to reducing dependence on commercial trees. During this period, vanilla (*Vanilla pompon*) has been identified as a resource of high value in the market. Currently, there are 6 subscribers managing demonstration plots, who also participated in an internship to learn cultivation techniques.

Dragon fruit growing, meliponiculture and ecotourism are other productive activities being promoted in the communities; activities that are being consolidated as alternatives to the use of forest resources.

4.2 Offsite Stakeholder Impacts

4.2.1 Mitigation of Negative Impacts on Other Stakeholders (CM2.2)

The specific indicators selected to monitor the impact on offsite community demonstrated that minimal if any negative impacted was observed. Overall, there is a positive impact mostly supported by the implementation of sustainable practices in the buffer area carried out by CI Peru.

Impact 16: Demand for conventional coffee practices are displaced to native communities increasing unsustainable land use in areas rented by them.

It is not possible to establish a consistent method to quantify this impact. During this reporting period partnership with the Shampuyacu and the Alto Mayo Native Communities continue, and Conservation Agreements have been signed with both communities to conserve their forest as well as shift from conventional coffee management to sustainable practices, involving not only community members but also land tenants.

In 2019, CI started a new project in Alto Mayo that specified actions in six native communities more, which added to the other two that had already been intervened making up a total of eight communities. The objective is to work on issues of governance and to strengthen the FERIAAM, as well as to improve their production systems from conventional coffee to specialty coffees, where good practices are developed without the use of agrochemicals. For this reason, the COOPBAM has initiated articulation with producers in the communities to evaluate and identify the quality of coffee to offer it to their customers.

Eleven producers were considered for the 2020 coffee campaign during the VI Organic Certification of the COOPBAM. This represents a total of 52 hectares in which good environmental and sustainable practices are implemented, a number that is expected to be increased in the future under the technical assistance provided by the field team.

Impact 17: Customary uses of the native communities are affected by increased surveillance and control program of the NPA

There are no actions concerning this indicator. Generally, the Native Communities are performing their usual activities in their territory and there is no evidence that they are affecting the AMPF. During this monitoring period, there have been no recorded conflicts between settlers of Native Communities and staff of the AMPF due to customary practices within the protected area.

CI Peru has been implementing since 2014 to date the project "Strengthening Governance and Capacities of Awajún Indigenous Communities to Develop Partnerships for Sustainable Product Sourcing in the Alto Mayo Basin" in the Awajún community located in the buffer zone in Alto Mayo. The project's main objective is to achieve a suitable level of indigenous governance in this community to contribute to the conservation of remnant plant cover and the implementation of sustainable practices that improve production in deforested areas. This is done through the conservation agreements model that capitalizes the great experience gained within the NPA and the projects that CI Peru implements in the community of Awajún Shampuyacu.

The primary actions of this project are based on strengthening the relationship between the AMPF Head Office and the indigenous community, where community surveillance actions, implementation of good agricultural practices and restoration of degraded ecosystems are being implemented.

There is a good relationship between SERNANP and the Native Community of Alto Mayo where a checkpoint and surveillance post has been established in the Huasta annex. This facilitates park ranger personnel to perform patrols in the surrounding area of the AMPF. No difficulties have been reported as to prevent these actions from being performed during this period.

4.2.2 Net Impacts on Other Stakeholders (CM2.3)

This region overall is rich with natural and cultural resources, and current and expected future net impacts on other stakeholders are positive. Overall, benefits have related specifically to the provision of ecosystem services in the form of clean water, the development of PES compensation mechanisms, technology transfer to beyond the direct project participants, and an increase in investment in the area.

Impact 13: Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of the population outside the project zone.

AMPF basins provide important ecosystem services to local communities, including water and genetic resources; and to the global population through climate stabilization. Run-off from the Alto Mayo forests provides clean and plentiful water for local communities and the development of the various economic activities in the watershed of the Mayo River. The project was able to avoid 2,271 ha of forest loss in 2018-2020 and over 19,581ha since the project start date in 2008, which corresponds to 8.4 M tCO₂ secured in the forests of AMPF.

The compensation mechanism for water service in three watersheds located in the buffer zone is being implemented as a result of the increased proactivity and restructuring of the Management Committee, and the work done together by CI Peru, SUNASS -the National Superintendence of Sanitation Services-, the Provincial Municipality of Rioja and SEDAPAR S.R.L -the Municipal Water Company- in Rioja. This initiative had initial financial support from the project and ensure the conservation of forest cover where the three watersheds that supply water to the main settlements of Rioja are born. This complements the conservation efforts and the provision of this ecosystem service of the AMPF.

Impact 14: Technology is transferred to improve coffee production systems outside project zone.

After over ten years of continuous work with subscribers of conservation agreements, more than 90% of active subscribers are replicating, in and outside the project area, the good farming practices learned without the technical or economic support given for the implementation of demonstration plots. Also, they transfer their knowledge to other coffee growers in the area, not only at the level of management of coffee plantations, but also for the production and spreading of native forest species that will help, in some way, to recover the Alto Mayo Valley forest cover.

During this monitoring period, the range of populations where technology is being directly transferred has expanded significantly. The interventions that are supported by the project include demonstration activities with key stakeholder groups in the Alto Mayo basin in order to contribute to building a sustainable landscape.

The techniques that are implemented consist of the elaboration of Bokashi using organic remains and beneficial microorganisms that after a degradation process are used for fertilizing the plants, pruning practices, and post-harvest handling which involves adequate drying and storage so that the product preserves the quality of the grains. In addition, coffee is sown in association with forest species (SAF) that are produced in 6 nurseries that were established within the scope of the project, and that each producer receives upon request.

These actions have aroused the interest of the public investment projects promoted by the Regional Government. Coordination has been established with the Regional Directorate of Agriculture through the Technical Table in order to strengthen the capacities of field technicians in relation to the good practices that are implemented in these cultivation systems.

The growth and positioning of the COOPBAM helps expand good farming practices. Its promoters provide technical assistance to the Native Communities of Shampuyacu and Alto Mayo¹⁵, and the districts of Jepelacio, Calzada and Habana that belong to the province of Moyobamba where about 650 producers are benefited, who in turn, guarantee a product of quality to offer to the special markets.

Also noteworthy is the participation of the COOPBAM as a member of the Board of Directors of the Coffee Technical Table, a platform where the private sector, the state and the organized civil society participate, and which has been helping to disseminate the results that have been achieved with the project. Its message is the replica of the work model used with the producers in terms of the area of intervention of other institutions.

Impact 15: New projects for sustainable development of the Alto Mayo watershed are leverage

During the reporting period, CI project's portfolio for the Alto Mayo watershed includes more than 10 projects with a budget superior to \$17 million; during 2018 to 2020, CI Peru invested more than \$ 6 million outside the AMPF. Work has been prioritized in the Awajun indigenous towns, located in both the buffer zone of the AMPF and the upper area of the Mayo River basin, because most of the landscape scale deforestation is concentrated in these communities. The forests of these communities are being leased to migrant population to establish temporary crops, mainly rice and coffee, as well as tabasco red pepper, pineapple, banana and cacao. The technical unsustainability in the production of these crops will produce heavily degraded soils in these communities in the future. This will imply a greater deforestation of the indigenous forests and a greater demand of land by the migrant population, which can potentially put pressure on the forests or areas restored within the AMPF.

The design of these projects is aligned with the REDD objectives and complement the actions taken to effectively reduce the drivers of deforestation. They provide a sustainable path for the development of the region increasing human welfare, strengthening land management and the development of a mini conservation corridor in the Alto Mayo basin. A brief description of these projects is summarized in the Community Engagement section of the Non-Permanence Risk Report n6.

4.3 Community Impact Monitoring

4.3.1 Community Monitoring Plan Development (CM3.3)

Not applicable. The monitoring plan was developed and within one year from the validation and its implementation was verified in the second, third and fourth verification events, respectively 2015, 2016 and 2018.

4.3.2 Community Monitoring Plan Results (CM3.1, CM3.2, GL2.5)

¹⁵ Local people that have learned farming techniques who are now part of the field technical team of the COOPBAM.

During the monitoring period of this report 2018-2020, there was no deviation in the data analysis from the methods and procedures described in the *Protocolo de Monitoreo Socioeconomico*. Community variables were included in the validated project description, and all communities (including community groups, other stakeholders, and HCVs related to well-being) were identified in the monitoring plan. The community impact monitoring plan also outlines the dates, frequency, and other details for the sampling methods and monitoring process, along with evaluation of the monitoring.

Most of the information was collected in the field through patrolling and survey, complemented by GIS and remote sensing analysis. The technician of the AMPF Head Office collects and systematizes the data gathered by the park rangers during the monthly patrolling. The socio-economic survey is applied at every verification event and the data is organized and analyzed by CI's socio-economic coordinator.

Data of over 100 metrics was analyzed and aggregated in several indicators. See Sup.Inf_MIR_01 for a complete list of indicators and data collected. It is important to mention that one indicator might contribute to one or more biodiversity and community impact, as all the activities and strategies are integrated.

4.3.3 Dissemination of Monitoring Plan and Results (CM3.3)

The results of the monitoring period were widely publicized in the local language to the communities and other stakeholders, and comments received were incorporated in the report. In addition, the Project Implementation Report was submitted to CCBA for a 30-day public comment period, and any relevant observation will be addressed. A poster was created with key information about the project and the main results of the monitoring report to facilitate the comprehension of local population. The poster was displayed in various parts of the AMPF and major towns in the project zone and made available to the VV body

4.4 Optional Criterion: Exceptional Community Benefits

Not applicable. The project did not include the optional climate change adaptation benefits criterion in the project description.

5 BIODIVERSITY

5.1 Net Positive Biodiversity Impacts

The methodological framework used to estimate the net positive impact of the project on biodiversity is detailed in the *Protocolo de Monitoreo de la Biodiversidad*. The indicators were designed to measure the positive and negative impact inside and outside the project zone. The Table 5 summarizes the expected impacts on the biodiversity.

Table 5 - List of impact on biodiversity inside and outside the project

Expected Impacts on Biodiversity		
	Positives	Negatives
Inside Project Zone	18. The habitat of high importance species for the biodiversity of the AMPF is conserved. 19. Habitat fragmentation of high importance species for the biodiversity of the AMPF is avoided. 20. High Conservation Value Areas of the AMPF is maintained and/or enhanced. 21. Populations of endemic and threatened species above its critical level are maintained and / or recovered. 22. Pressure reduced to ecosystems of the AMPF through the promotion of sustainable use practices by local people. 23. Operational capacity of the AMPF Head Office is strengthened and the response to the pressures on the area is improved. 24. Degraded ecosystems of the AMPF are restored through the implementation of reforestation and agroforestry systems. 25. Biodiversity and ecosystem services of the AMPF are recognized and valued by locals, who become allies in the conservation. 26. Illegal extraction of wildlife in the AMPF is reduced.	N/A
Outside Project Zone	27. Connectivity of the Conservation Corridor Abiseo-Cóndor-Kutukú – CCACK is maintained. 28. Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of population outside project zone. 29. Biodiversity and ecosystem services by AMPF natural resources stocks outside project zone are recognized and valued. 30. Technology is transferred to improve coffee production systems outside project zone. 31. New projects for the conservation of biodiversity in the Alto Mayo are leveraged.	32. Deforestation of the habitat of the species of high importance for biodiversity is displaced to in the leakage belt. 33. Illegal extraction of flora and fauna is displaced to out of the project area creating additional pressure on forests in the buffer zone.

Note that, in order to comply with the new VCS-CCBS reporting template, the impacts were numbered in a sequential order in Table 5, however might not be listed in a logical sequence in the sub-sections. The Table 5 follows the assumptions and design developed in the monitoring plan.

5.1.1 Biodiversity Changes (B1.1)

Impact 18: The habitat of high importance species for the biodiversity of the AMPF is conserved.

The ultimate goal of the project is to reduce the deforestation, while providing tangible benefits to local populations and improving the biodiversity. During the last monitoring period, the project was able to reduce substantially the deforestation inside the AMPF when compared with the baseline. Some impact is

also observed comparing the actual (project scenario) deforestation rates. The observed deforestation decreased 42% from 339 ha/y in the first monitoring period (2008-2012) to 195 ha/y in 2018-2020 (Figure 5), demonstrating the effectiveness of the project's strategies. In 2020, 144,837 ha of forest were successfully protected in the AMPF and over 2,271 ha of forest loss was avoided.

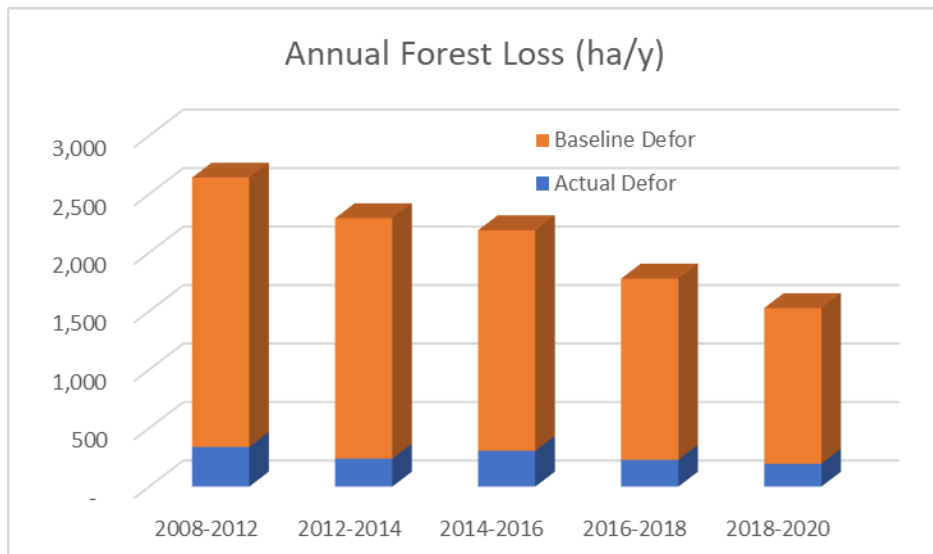


Figure 5 - Annual actual and projected deforestation per monitoring period

Impact 19: Habitat fragmentation of high importance species for the biodiversity of the AMPF is avoided.

Unlike conservation indicators of forest cover, we found none or a slight improvement in the case of forest fragmentation between the baseline scenario and the present (with project). This is because the AMPF still acts as a large block of forest where, despite a high rate of deforestation, it is adjacent to its edges and consequently there is a low rate of fragmentation inside. However, we have seen that with the project the edge effect increases slightly (25% of the forest habitat of the AMPF is found within 100 m of a non-habitat edge in the project scenario while without the project this holds at 23%). This is due to the difference between the distributions of deforestation in the spatial projection model vs current deforestation. While the spatial model has a low stochasticity and therefore most of the deforestation "expands" from non-forest areas with high probability of deforestation, current deforestation (observed) is more sporadically distributed within these areas, occurring in isolated patches within areas of high probability of deforestation and thus generating a greater edge effect compared to the scenario without the project.

In the without project scenario, the proportion of forest habitat in the AMPF found in patches of less than 100 km², or in forest fragments which are too small to support suitable habitat for biodiversity, is same proportion (3%) compared to the current project scenario (3%). Although fragmentation in the AMPF is not a current threat to the habitat of important species for the conservation of biodiversity, we will continue to monitor these indicators of forest fragmentation due to the importance of maintaining continuous areas of forest for endemic and endangered species such as the yellow-tailed woolly monkey.

Impact 21: Populations of endemic and threatened species above its critical level are maintained and / or recovered

The monitoring of primates ended in June 2017 with the presentation of the book “AMPF Experiences” by the Titi Monkey Project (Sup.Inf_MIR_05). The book includes a summary of the primate evaluation carried out in 7 micro-watersheds (Naranjos, Naranjillo, Aguas Verdes, Yuracyacu, Serranoyacu, Huasta and Rio Negro). A primate baseline was set in all these micro-watersheds which included an evaluation of the social perception of primates, highlighting the recognized species and their main threats. The reduction of space due to agricultural and livestock activities is considered the main threat to the primate populations of the AMPF.

The monitoring of primates was carried out in 6 micro-watersheds. It covered 33 transects measuring more than 1 km each. These transects were paths used by local people. Opening new trails that could be used in such a way was avoided since they can cause a negative impact on the ecosystem in the future (i.e. selective logging and hunting).

The probability of primate sighting is linked to phenological changes, abundance of fruits and, at the same time, to the impact generated by the inhabitants settled in the area.

The Huasta sub-basin provided habitat for a greater number of primate species (*L. flavicauda*, *A. miconax*, *S. macrocephalus* and *C. yuracus*), but their monitoring could not be carried out due to conflicts with some inhabitants. In general, when monitored, the number of recorded species was equal or higher than the baseline.

The most commonly found species in all the sub-basins assessed was the Peruvian yellow-tailed woolly monkey (*Lagothrix flavicauda*), followed by the Andean white-fronted capuchin monkey (*Cebus yuracus*) and the Andean night monkey (*Aotus miconax*), unlike the large-headed capuchin monkey (*Sapajus macrocephalus*) that was only found in the Huasta sub-basin.

In 2018, the assessment of alternatives for the development of a participatory biodiversity monitoring was also proposed. In this sense, CI's experience in the development of the Tropical Ecology, Assessment and Monitoring (TEAM) Initiative was taken in advantage. This initiative has been widely used in the preparation of baselines and biological monitoring in protected natural areas worldwide (Sup.Inf_MIR_04). The new monitoring protocol will be implemented in the AMPF in 2018, with the group of terrestrial vertebrates mainly. This will allow evaluating the stability of trophic networks, identifying key species, and assessing the large variety of species within the protected natural area.

The monitoring is primarily focused on evaluating significant differences in terrestrial vertebrate species in forest areas, degraded areas and agricultural land areas with good and bad practices that surround plots of subscribers of conservation agreements in the AMPF.

During this reporting period the project has implemented a research in AMPF in partnership with Arizona State University (AZU) called “Café & Fauna” which shows mammal fauna captured by trap cameras in agroforestry crops of conservation agreements subscribers (Sup.Inf_MIR_20+b), and was permanently recording fauna and flora observations in park ranger patrols.

Impact 22: Pressure reduced to ecosystems of the AMPF through the promotion of sustainable use practices by local people.

As reported in the community section on positive impacts in the project area, the adoption of sustainable practices, and the awareness of the importance of the forest continues to increase. As result, a reduction in the pressure by the local population to convert land to coffee plantations was observed. In addition, the implementation of agroforestry system is having a positive effect, as native species are being planted and the habitat is being restored. 300 hectares of pilot plots under agroforestry systems were installed and 2,109 hectares are under organic certification.

Impact 23: Operational capacity of the AMPF Head Office is strengthened and the response to the pressures on the area is improved.

As reported in the community section on positive impacts in the project area, the strengthening of the operational capacity of the AMPF is one of the key priorities for the project and a great positive impact is observed in this monitoring period. The numerous trainings – over 16 events – improved the quality and effectiveness of the AMPF management. The project has implemented the AMPF Management Information System Data Platform (SID AMPF) where allied institutions that implement activities in the field can upload information in order to facilitate access for those who require it. The project Continues working on the consolidation on the financial sustainability and supports the AMPF Head Office in order to have a new Master Plan according to the real needs of the protected area. The plan will also be useful to request the SERNANP to be included in the Heritage Initiative of Peru which receives financial support from the Peruvian state resources to overcome the gaps identified which prevent the efficient management of the AMPF.

During these two years, the project has generated three management documents that are being implemented with different groups of beneficiaries in the AMPF. Their impacts will benefit the AMPF Head Office since the allied population will be trained and strengthened in the following subjects; i) Technical managerial capacities plan for the COOPBAM (Sup.Info_MIR_21), ii) Organizational capacity building plan for women's committees (Sup.Info_MIR_22) and iii) Life Plan for the community of Nueva Zelandia (Sup.Info_MIR_23), along with the existing, though valid, management documents were approved by the AMPF Headquarters: i) the Research Strategy (Sup.Inf_MIR_10), ii) Plan for the Management of Renewable Natural Resources (Sup.Inf_MIR_11), iii) the Tourism Plan (Sup.Inf_MIR_12), iii) the Community Development Plan, iv) the Management Plan for the Sustainable Use of Natural Resources, and iv) the Communication Plan, which have been implemented and have contributed to the fulfilment of the NPA goals (Sup.Inf_nprt_15a+b), and v) Stakeholder Engagement Plan (Sup.Inf_nprt_16).

During this period, CI Peru -in coordination with their Headquarters in Washington- has been able to raise about \$ 6.1 million from the sale of carbon credits, with the approval of SERNANP. This has served to continue implementing the conservation strategies of the forests and ecosystems of the AMPF.

Impact 24: Degraded ecosystems of the AMPF are restored through the implementation of reforestation and agroforestry systems.

The results show that significant progress has been made in the recovery of degraded areas and in mitigating the impact of firewood collection on these forests. For areas in the process of being restored, almost 21,500 seedlings of native tree species have been produced and over 10,300 have been taken to the field and this has contributed to the restoration of more than 15 ha of forest, 1208 ha under conservation agreements. Additionally, COOPBAM pursued the organic certification of 2,109 ha at annual basis where 622 ha of the total farm area are devoted to coffee crops. The implementation of these plantations is aimed at meeting the demands of the agroforestry system (protection and land recovery, provision of shade).

It is also aimed at meeting the needs of the population (firewood, timber for construction) and thus to ensure the future contribution of these areas to the recovery and connectivity of local biodiversity and their care by local populations. An increase in the use of improved cooking stoves has also been observed. The project has promoted the use of up to 293 new improved cooking stoves in the area since project inception, which consume an average of 52% less firewood than regular cooking stoves. The use of improved cooking stoves helps reduce pressure on forest fragments and remaining primary forests in areas close to the population.

Impact 25: Biodiversity and ecosystem services of the AMPF are recognized and valued by locals, who become allies in the conservation.

In order to achieve this goal, communication and environmental education strategies addressed to the population within the forest were combined. The guiding objective was to incorporate the concept of conservation into the vision of local development.

The Environmental Education Plan that is designed every year aims to sensitize the local population and members of the key actors with whom the project interacts. This means, more than 3,000 people trained in this period, including local governments and executive units at the regional level. This is important since it is essential to incorporate the concept of sustainable development in the different programs that are promoted in various institutions.

During the process of updating the Master Plan, the empowerment of the members of the Management Committee on the representative species of the AMPF was perceived. They have requested that the strategies and actions that are being implemented continue during the next 5 years, time in which research with specialized institutions and the academy should be promoted.

On the other hand, the subscribers of conservation agreements increasingly value biodiversity species, mainly avifauna, stating that they generate the interest of tourists who come to their sectors to watch them. Undoubtedly, the COOPBAM partners also show awareness of biodiversity and ecosystem services, such as taking care of water sources, which impact is reflected in the organic certification process. As a result of these communication campaigns, the vast majority of the population within the AMPF (99%) recognized the importance of the ecosystem services in their well-being and are willing to develop conservation actions

Impact 26: Illegal extraction of wildlife in the AMPF is reduced

The results on environmental illicit activities reported by the surveillance and control area of the AMPF management office indicated that 16 interventions were made on wood trafficking. There were 31 findings of logging and/or deforestation, 14 in primary forests and 17 in secondary forests, however 80% were occurred in the buffer zone. On the contrary, no wildlife traffic has been reported. In the last few years, the rangers have been collaborating with the National Policy on the control and surveillance tasks. These results, compared with the ones obtained in previous years, show a reduction of environmental illicit acts. This is due to a greater dissemination of the importance of conserving the forests of the AMPF, where park rangers have joined to carry out awareness actions for the local population and with whom they interact. In addition to this, they have the opportunity to work within the framework of conservation agreements, which provides economic development while keeping with the conservation of the NPA.

5.1.2 High Conservation Value Protection (B1.2)

Impact 20: High Conservation Value Areas of the AMPF is maintained and/or enhanced.

The effectiveness of the project strategies to maintain or improve these High Conservation Values is evaluated by monitoring deforestation in the Strict Protection Area within the AMPF – which includes areas with species or ecosystems that are unique, rare or fragile, and require a high level of protection and isolation to stay pristine – and within the habitats for species of greatest importance for the conservation of biodiversity in the AMPF, such as the yellow-tailed woolly monkey, the night monkey endemic to San Martin, the titi monkey, and the spectacled bear.

Table 6 summarizes the results on the habitat of species of high biodiversity significance and show that the projection activities to mitigate deforestation have managed to retain high value forests for biodiversity conservation. The results were obtained by superimposing the important areas of habitat for these species according to Rondinini et al. (2011) and the NatureServe maps on changes in forest cover. The subset of priority species has been selected based on the category of threat, endemism and its importance to the conservation targets of the AMPF.

In addition, no negative impacts on the areas of biodiversity-related HCVs were observed. On the contrary, the strategies of project have been designed and implemented to ensure the achievement of the conservation objectives of the AMPF, as observed in the indicators above.

Table 6 - Deforestation of habitat of high importance species for biodiversity avoided

Scientific Name / Common Name	Deforested hectares (ha) in areas of high importance for biodiversity in the scenario with the project	Deforested hectares (ha) in areas of high biodiversity importance in the scenario without the project	Avoided deforestation hectares (ha) in areas of high importance for biodiversity
<i>Aotus miconax</i> (night	381	3,924	3,543

monkey / mono nocturno) *			
<i>Flavicauda Lagothrix</i> (yellow-tailed woolly monkey / mono choro cola amarilla) **	329	2,333	2,004
<i>Callicebus oenanthe</i> (titi monkey / titi monkey)**	0	32	32
<i>Tremarctos ornatus</i> (spectacled bear / oso andino)*	235	2,364	2,129

*Source: Rondinini et al. (2011);

**Source: NatureServe

5.1.3 Invasive Species (B1.3)

Only native species have been used in the restoration areas, and is limited to: *Alnus sp* (Aliso), *Guadua sp* (Bambú), *Guazuma crinita* (Bolina), *Pouteria sp* (Caimito), *Swietenia macrophylla* (Caoba), *Calycophyllum spruceanum* (Capirona), *Micandra sp* (Caraña), *Cedrela odorata* (Cedro), *Guarea sp* (Cedron), *Gustavia sp* (Chope), *Pouteria sp* (Fruto Del Paraíso), *Inga sp* (Guaba), *Ficus spp* (Higuerón), *Minuartia guianensis* (Huacapu), *Euterpe precatoria* (Huasai), *Tabebuia chrysantha* (Huayacan Amarillo), *Tabebuia sp* (Huayacan Rojo), *Jenipa sp* (Jagua), *Calophyllum brasiliense* (Lagartocaspi O Alfaro), *Eugenia sp* (Lanchillo), *Guarea sp* (Latapi), *Cordia alliodora* (Laurel), *Leucaena leucocephala* (Leucaena), *Clarisia rasemosa* (Mashona), *Caryodendron orinocense* (Metohuayo), *Miconia sp* (Miconias), *Nectandra sp* (Moena), *Inga brachyptera* (Pacae), *Erythrina poepigiana* (Pajurillo), *Erithrina edulis* (Pajuro), *Vitex sp* (Paliperro), *Inga sp* (Palta Paca), *Artocarpus altilis* (Pan De Arbol), *Schizolobium amazonicum* (Pino Chunchu), *Ireartea deltoidea* (Pona), *Manilkara sp* (Quinilla Amarilla), *Guarea trichilioides* (Requia), *Pouteria sp* (Sacha Caimito), *Colubrina glandulosa* (Shaina), *Inga sp* (Shimbillo), *Cedrelinga catenaeformis* (Tornillo), *Styrax sp* (Tumbe), *Pourouma cecropiaefolia* (Uvilla), *Terminalia oblonga* (Yacushapana), *Cybistax antisiphilitica* (Yangua o Llangua), *Matisia cordata* (Zapote).

In addition, the project has used non-native species in the agroforestry system, however those species were already introduced to the AMPF previously to the project and has not resulted to be invasive (see Table 7).

5.1.4 Impacts of Non-native Species (B1.4)

Table 7 - Impacts of Non-native Species

Species	<i>Coffea arabica</i> var catimor (castillo and gran colombia coffee variety), <i>Persea americana</i> (Palta), <i>Lycopersicum esculentum</i> (Tomate), <i>Brassica oleracea</i> (Repollo), <i>Lactuca sativa</i> (Lechuga), <i>Raphanus sativus</i> (Rabanito), <i>Allium fistulosum</i> (Cebolla china), <i>Beta vulgaris</i> (Acelga), <i>Coriandrum sativum</i> (Culantro), <i>Cucumis sativus</i> (pepinillo), <i>Capsicum anuum</i> (ají pápikra), <i>Brassica rapa</i> (nabo), <i>Daucus carota</i> (zanahoria).
Justification of Use	Agroforestry system for food security
Adverse Effect	No adverse effect was observed or previously documented

5.1.5 GMO Exclusion (B1.5)

No genetically modified organisms (GMO) have been used.

5.2 Offsite Biodiversity Impacts

5.2.1 Negative Offsite Biodiversity Impact Mitigation (B2.2)

As the principle of governance is restored in the project area, project strategies will pressure illegal environmental actors who, in case they do not respect the current legislation, could conduct their illicit activities beyond the project area, causing negative impacts in areas where we have no interference. The following impact analysis was made based on this premise by determining the progress in the threats and analyzing the mitigation measures that should be implemented if these indicators were registered. The strategies and activities implemented to mitigate the potential negative impact are described in detail in section 2.2. Overall, no negative offsite biodiversity impact was observed at this monitoring period confirming that the measures taken to mitigate the threats were efficient.

Impact 32: Deforestation of the habitat of the species of high importance for biodiversity is displaced to in the leakage belt.

The indicators about the state of biodiversity, using spatial analysis with satellite images, show that the project has reduced deforestation in the area without significant negative impacts on the leakage belt. The implications for the conservation of biodiversity in the AMPF are several, including the maintenance of forest areas in the buffer zone to ensure the connectivity of the different populations of species as well as the maintenance of forests that provide refuge outside the project area when threats arise within the project area. Additionally, maintaining the habitat outside the project area creates conditions for the existence of flora and fauna to thrive, which may imply that the pressures on these species are kept outside the project area.

Similarly, deforestation in the habitat of species of high importance for biodiversity caused by the project in the leakage belt can also be considered zero, because it is lower than in the baseline. The maintenance of habitat for species of high importance for biodiversity in leakage areas ensures connectivity between populations of species within and outside the project area as well as the existence of habitat shelters outside the project area.

Impact 33: Illegal extraction of flora and fauna is displaced to out of the project area creating additional pressure on forests in the buffer zone.

In the project design the assumption that increasing the control and surveillance inside the AMPF would displace the illegal activities to outside the AMPF was considered. However, the integrated approach used by the project, increased the awareness of the importance of the ecosystem services provide by the forest and its biodiversity, and provided alternative livelihoods to the settlers. As shown in the Sup.Inf_MIR_01 the local communities not only decrease the extraction of flora and fauna inside, but also

became conservationists, through the signage of conservation agreements. Consequently, the project has a minimal (if any) negative impact on the flora and fauna outside the project area.

However, in order to monitor and ensure the change, a park ranger shelter has been set up in the Huasta annex of the Alto Mayo Native Community. This limits with the AMPF, so that patrolling and forests and biodiversity conservation monitoring tasks are carried out. The presence of park rangers in this place has strengthened the relationship with the communities and settlers who settled down to work in the cultivation of coffee, also achieving awareness of the importance of the AMPF.

Another action that CI has implemented through the project in the Native Community of Shampuyacu, is the formation of community police, which members were also trained in installing camera traps to identify biodiversity species, and also to observe who was committing environmental crimes. Offenders got in camera were later summoned by the local authority to implement corrective actions which later contributed to reducing poaching.

5.2.2 Net Offsite Biodiversity Benefits (B2.3)

Impact 27: Connectivity of the Conservation Corridor Abiseo-Cóndor-Kutukú – CCACK is maintained.

The Conservation Corridor Abiseo-Condor-Kutukú (CCACK) is one of the most diverse regions of the world, not only for its abundance of species, but also for its high degree of endemism. The project area is located in the center of the CCACK. In 2020, 144,837 ha in the AMPF remain under intact forest cover in the project scenario, contributing to the connectivity and conservation of High Conservation Values in the CCACK.

Impact 28: Ecosystem services of the AMPF (water and soil) are maintained and improved for the benefit of population outside project zone.

Maintaining the vegetation cover of the AMPF continues to generate direct benefits to the population settled in the middle and lower areas of the Alto Mayo basin. The allocation of water resources for human, agricultural and industrial consumption of cities, villages and settlements located from the edge of the AMPF to the Mayo River is guaranteed by the level of conservation of the AMPF.

It is important to mention that the 9 districts of the province of Rioja have their catchment of water for human consumption in the buffer zone of the AMPF. In this context, the AMPF management has been involved, through the Management Committee, in the Compensation Mechanism for Ecosystem Services to comply with the strategies that are being implemented, and that will allow the Water Service Provider Company of Rioja to leverage financial resources to implement conservation projects in the micro-basin of the Negro river, whose waters originate in the AMPF, and which benefit more than 30,000 inhabitants.

On the other hand, the conservation areas of the AMPF provide refuge to the flora and fauna of the basin. They allow the development of touristic potentials in the buffer zone, such as the one in the Arena Blanca Reserve in the Aguas Verdes buffer zone (avitoirism pilot project within the framework of conservation agreements and articulated to the international market), or the one in the settlement of Palestina in the

buffer zone, where the associated population is implementing a butterflies breeding center for tourism, in which the germplasm is collected within the protected area.

Additionally, the Head office has received a request for technical opinion from 67 projects in the AMPF and its buffer zone; 36 of them are compatible with the NPA and are being developed in accordance with the conservation guidelines favoring the local population.

Impact 29: Biodiversity and ecosystem services provided by AMPF natural resources stocks outside project zone are recognized and valued.

The Communications team of the AMPF Management focused its efforts on the production of audiovisual information material that was later disseminated on the radio and television to sensitize the population of Alto Mayo about the importance of conserving the Protected Area. In addition, advocacy was made with the local and national press to disseminate the achievements of the project, including reports on the state channel through TV Peru channel 7, and the newspapers *el Comercio* and *la República*.

Also, the news has been monitored in the local media where 118 pieces of news about the AMPF were reported. The topics were related to sustainable coffee, environmental education, capacity building, sustainable productive activities and institutional positioning. The leadership in control and surveillance actions as well as the updating of the Master Plan are highlighted in the news.

Another means for the dissemination of the achievements of the AMPF management is Facebook. This platform allows the interaction with a large number of users. The number of followers up to date is 19 thousand. This platform has been used to promote live presentations of the actions that are developed as a project, which are carried out by members of the technical team of the participating institutions (CI, ECOAN and SERNANP).

As mentioned before, the implementation of the Environmental Education Plan made it possible to sensitize more than 3,000 residents through different activities such as fairs, talks and workshops, which contributes to the positioning of the AMPF as an ecosystem of high importance for the well-being of the population.

Impact 30: Technology is transferred to improve coffee production systems outside project zone.

Since the last monitoring period the project has been training the best conservation agreement subscribers as promoters of the coffee production systems. They have played an important role not only in disseminating the techniques for best practices but also working (at their own initiative) as conciliators, communicators, and environmental educators. Their work is now being transferred to the COOPBAM that will be responsible to the long-term technical capacitation for coffee producers inside and outside the protected area.

In addition, CI, through the sustainable landscape approach implemented in the Alto Mayo watershed, has been using similar technology applied in the conservation agreements, to coffee producers in the Alto Mayo watershed (outside the protected area). Since 2014, over 600 coffee producers have received

training on the management of coffee plantations, and production of native forest species that will help, to some extent, restore forest cover in the Alto Mayo Valley.

The impact generated by the technological transfer of the coffee production system outside the scope of the project has aroused the interest in coffee as a PIP. This is led by the Regional Directorate of Agriculture, to articulate good practices with farmers who currently perform conventional actions, but not discarding replicas in the models of conservation agreements.

Impact 31: New projects for the conservation of biodiversity in the Alto Mayo are leveraged.

In addition to the investment made within the AMPF, CI Peru invests in strategic areas at the scale of the Alto Mayo landscape to ensure the maintenance of biodiversity connectivity through a mini conservation corridor that unites the AMPF and the awajunes communities of Alto Mayo and Shampuyacu. The processes carried out in this mini corridor include the process of river restoration and reduction of chemical use through agroforestry systems, protection and maintenance of primary forests (including patches of flooded forests) (Sup.Inf_MIR_15a-d).

The use of camera trap to record wildlife at strategic points in both communities as well as the monitoring of plant cover (primary forests and restored areas) through the use of drones, have registered important findings about large mammals and felines. They have also registered a decrease in the rate of deforestation in the Awajún community of Alto Mayo and an increase in the forest area in the agroforestry systems of both communities (Sup.Inf_MIR_16a+b).

5.3 Biodiversity Impact Monitoring

5.3.1 Biodiversity Monitoring Plan Development (B3.3)

Not applicable. The monitoring plan was developed and within one year from the validation and its implementation was verified in the second, third and fourth verification events, respectively 2015, 2016 and 2018.

5.3.2 Biodiversity Monitoring Results (B3.1, B3.2)

During the monitoring period of this report 2018-2020, there was no deviation in the data analysis from the methods and procedures described in the *Protocolo de Monitoreo de la Biodiversidad*. The protocol along with the monitoring reports describes the dates, frequency, location and sampling methods. Most of the information was collected in the field through patrolling and biodiversity transects, complemented by GIS and remote sensing analysis. The technician of the AMPF Head Office collects and systematizes the data gathered by the park rangers during the monthly patrolling.

Data of over 100 metrics was analyzed and aggregated in several indicators (see Sup.Inf_MIR_01 for a complete list of indicators and results). The indicators were chosen based to demonstrate the impact of

the strategies implemented by the project in conserving the biodiversity of AMPF, including the HCVs. It is important to mention that one indicator might contribute to one or more biodiversity and community impact, as all the activities and strategies are integrated. Similarly, more than one indicator is needed to demonstrate the impact and effectiveness of the strategies. In the sections above we highlight the aggregated result and evaluation of monitoring to each of the expected (positive or negative) impact that the project will have.

5.3.3 Monitoring Plan and Results Dissemination (B3.3)

The results of the monitoring period were widely publicized in the local language to the communities and other stakeholders, and comments received were incorporated in the report. In addition, the Project Implementation Report was submitted to CCBA for a 30-day public comment period, and any relevant observation will be addressed. A poster was created with key information about the project and the main results of the monitoring report to facilitate the comprehension of local population. The poster was displayed in various parts of the AMPF and major towns in the project zone and made available to the VV body

6 ADDITIONAL PROJECT IMPLEMENTATION INFORMATION

The following paragraphs document the additional information that clarify and explain how the project has been implemented in accordance with the validated CCB and/or VCS project description.

The land cover and change analysis for this monitoring period was done based on the 2012 forest benchmark map. It was assumed that the rate of forest change was evenly distributed between the 2018-2020 period.

Areas identified as cloud in the 2020 land cover map were temporarily excluded from this monitoring period from both scenarios – baseline and project - and will be included in subsequent monitoring periods based on the availability of cloud-free images. Therefore, the total baseline carbon stock changes in the project area during this monitoring period reported in MR Tables 02.a-c differ from the total baseline carbon stock changes in the project area reported on VM Tables 15.a-c of the AMCI Methodological Annex, respectively. Similarly, the total baseline carbon stock changes in the leakage belt during the monitoring period reported in MR Tables 04.a-c differ from the total baseline carbon stock change in the leakage belt reported in VM Tables 29.a-c of the AMCI Methodological Annex, respectively.

Areas obscured by clouds in 2012, 2014, 2016 and/or 2018 but revealed in 2020 as non-forest were accounted as deforestation in this monitoring period. Although some landslides were observed in the forest change analysis, the forest loss due to this event was minimal and was not accounted as deforestation when compared with the baseline. During this monitoring period, no other natural disturbances or catastrophic events occurred in the project area and leakage belt.

The 90% Confidence Interval value of the carbon stock was applied to the average carbon stock of pre-montane forest, dwarf forest and post-deforestation land use, as the uncertainty of the carbon estimate was above 10%.

Non-CO₂ emissions from forest fires and animal grazing were not monitored as they were not included in the baseline.

Since the date of validation and verification, no regional, national, or jurisdictional monitoring system of land-use and land-cover change was in place. In the UNFCCC Conference of Parties in Paris, the government of Peru has presented the forest reference emission level (FREL) for the amazon region, with subsequent submission to the secretariat for assessment. The FREL was defined based on the historical deforestation trend from 2001 to 2014 and currently does not provide information of the spatial distribution of future deforestation, nor define the rules for grandfathering projects (see Sup.Inf_MIR_3a and Sup.Inf_MIR_3b). As consequence the project was not subject of nesting during this monitoring period.

7 ADDITIONAL PROJECT IMPACT INFORMATION

7.1 Exceptional Biodiversity Benefits (GL3)

The CCBS PD includes the list of species found in the AMPF categorized by the International Union for Conservation of Nature (IUCN) as Critically Endangered (CR) and Endangered (EN), according to the requirements of the GL3.1.1 indicator. Table 8 shows the updated list of these species, as part of the criterion for the Gold Level on Biodiversity.

Table 8 - Species of fauna y flora Critically Endangered (CR) and Endangered (EN) in the project area

Scientific name	Common name	Threat Status (2010 IUCN)	Threat Status (2013 IUCN)	Threat status (2017 IUCN)	Threat status (2019 IUCN)
<i>Atelopus seminiferus</i>	Upper Amazon stub foot toad	CR	CR	CR	EN
<i>Oreonax flavicauda</i>	Yellow-tailed woolly monkey	CR	CR	CR	CR
<i>Callicebus oenanthe</i>	Andean Titi monkey	CR	CR	CR	CR
<i>Zamia disodon</i>	Palm tree	CR	CR	CR	CR
<i>Zamia hymenophyllidia</i>		CR	CR	CR	CR
<i>Zamia macrochiera</i>		CR	CR	CR	CR
<i>Zamia urep</i>		CR	CR	CR	CR
<i>Herpsilochmus parkeri</i>	Ash-throated Antwren	EN	EN	EN	EN
<i>Heliangelus regalis</i>	Royal sunangel	EN	EN	EN	EN
<i>Loddigesia mirabilis</i>	Marvelous spatuletail	EN	EN	EN	EN
<i>Xenoglaux loweryi</i>	Long-whiskered owlet	EN	EN	EN	EN
<i>Grallaricula ochraceifrons</i>	Ochre-fronted antpitta	EN	EN	EN	EN
<i>Picumnus steindachneri</i>	Speckle-chested piculet	VU	EN	EN	EN
<i>Poecilatriccus luluae</i>	Lulu's Tody- Flycather	VU	EN	EN	EN
<i>Ateles belzebuth</i>	White-bellied spider monkey	EN	EN	EN	EN
<i>Pteronura brasiliensis</i>	Giant otter	EN	EN	EN	EN
<i>Virola surinamensis</i>	Baboonwood	EN	EN	EN	EN

<i>Aotus miconax</i>	Andean Night Monkey	VU	VU	VU	EN
----------------------	---------------------	----	----	----	----

The CCBS Project Document (PD) includes the list of species found in the AMPF categorized by the IUCN as Vulnerable (VU), according to the requirements of the GL3.1.2 indicator. Table 9 shows the updated list of these species

Table 9 - Vulnerable species (VU) in the project area

Scientific Name	Common Name	Threat Status (2010 IUCN)	Threat Status (2013 IUCN)	Threat status (2017 IUCN)	Threat status (2019 IUCN)
<i>Podocnemis unifilis</i>	Yellow-spotted River Turtle	VU	VU	VU	VU
<i>Ara militaris</i>	Military Macaw	VU	VU	VU	VU
<i>Touit stictopterus</i>	Spot-winged Parrotlet	VU	VU	VU	VU
<i>Leptosittaca branickii</i>	Golden-plumed Parakeet	VU	VU	VU	VU
<i>Patagioenas oenops</i>	Peruvian Pigeon	VU	VU	VU	VU
<i>Thripophaga berlepschi</i>	Russet-mantled Softtail	VU	VU	VU	VU
<i>Cacajao calvus ssp</i>	Bald-headed uacari	VU	VU	VU	VU
<i>Priodontes maximus</i>	Giant armadillo	VU	VU	VU	VU
<i>Tapirus terrestris</i>	Lowland Tapir	VU	VU	VU	VU
<i>Tremarctos ornatus</i>	Spectacled Bear	VU	VU	VU	VU
<i>Telmatobius truebae</i>		EN	EN	VU	VU
<i>Myrmecophaga tridactyla</i>	Giant Anteater	VU	VU	VU	VU
<i>Atelopus pulcher</i>	Harlequin frog	CR	CR	CR	VU

In the CCBS PD 15 bird species of restricted distribution were identified, according to the requirements of the GL3.2.1 indicator. Table 10 shows the updated list of these species.

Table 10 - Restricted-range bird species in the AMPF

Scientific Name	Common Name
<i>Xenoglaux loweryi</i>	Long-whiskered owlet
<i>Grallaricula ochraceifrons</i>	Ochre-fronted antpitta
<i>Heliangelus regalis</i>	Royal sunangel
<i>Picumnus steindachneri</i>	Speckle-chested piculet
<i>Grallaria blakei</i>	Chestnut antpitta
<i>Grallaria przewalskii</i>	Rusty-tinged antpitta
<i>Hemitriccus cinnamomeipectus</i>	Cinnamon-breasted tody-tyrant
<i>Henicorhina leucoptera</i>	Bar-winged wood-wren
<i>Phylloscartes gualaquiza</i>	Ecuadorian tyrannulet

Source: ICAM 2012, Birdlife International 2020

Four species (*Thripophaga berlepschi*, *Campylopterus villaviscensio*, *Phlogophilus hemileucurus* and *Xenerpestes singularis*) were removed from the list and six species were added (*Herpsilochmus parkeri*, *Leptopogon taczanowskii*, *Zimmerius viridiflavus*, *Myiophobus cryptoxanthus*, *Ramphocelus*

melanogaster and *Tangara argyrofenges*), since the updated information from Birdlife International indicates a distribution range higher than 50,000 km².¹⁶

¹⁶ BirdLife International (2020) Important Bird Areas factsheet: Abra Patricia - Alto Mayo. Downloaded from <http://datazone.birdlife.org/site/factsheet/abra-patricia--alto-mayo-iba-peru/details> on 30/07/2020.
